

CHICAGO SUMMIT 2008

ORD Airfield Equipment Status

Ellen Kijowski, Engineering Services

September 17-18, 2008



Federal Aviation
Administration



Runway 10/28 (future 10L/28R)

- **Commissioning**
 - Extension to be charted on 9/25/08
- **Flight Checks – Completed**
- **Estimated Completion of Burn-In* (CAT II/III)**
 - 10L LOC: 11/18/08
 - 10L GS: 3/10/09
 - 28R LOC: 12/14/08
 - 28R GS: N/A (In Service)

*Estimates change daily based on airport configuration



10L LOC (New 20 element, Old 14 element)



Runway 9L/27R

- **Commissioning CAT I**
 - Scheduled for 11/20/08
- **Flight Checks – Completed**
- **Estimated Completion of Burn-In (CAT II/III)**
 - 9L LOC & GS: 2/10/09
 - 27R LOC & GS: 11/24/08



27R ALSF and 9L LOC

27R Approach




North ATCT (NATCT)

- **Occupancy Permit Date - 9/15/08**
- **Final Punch List Items in Progress**
- **Controller Training Started on 9/15/08**
- **TechOps Familiarization to be Completed on 11/03/08**
- **Commissioning Scheduled for 11/20/08**



NATCT

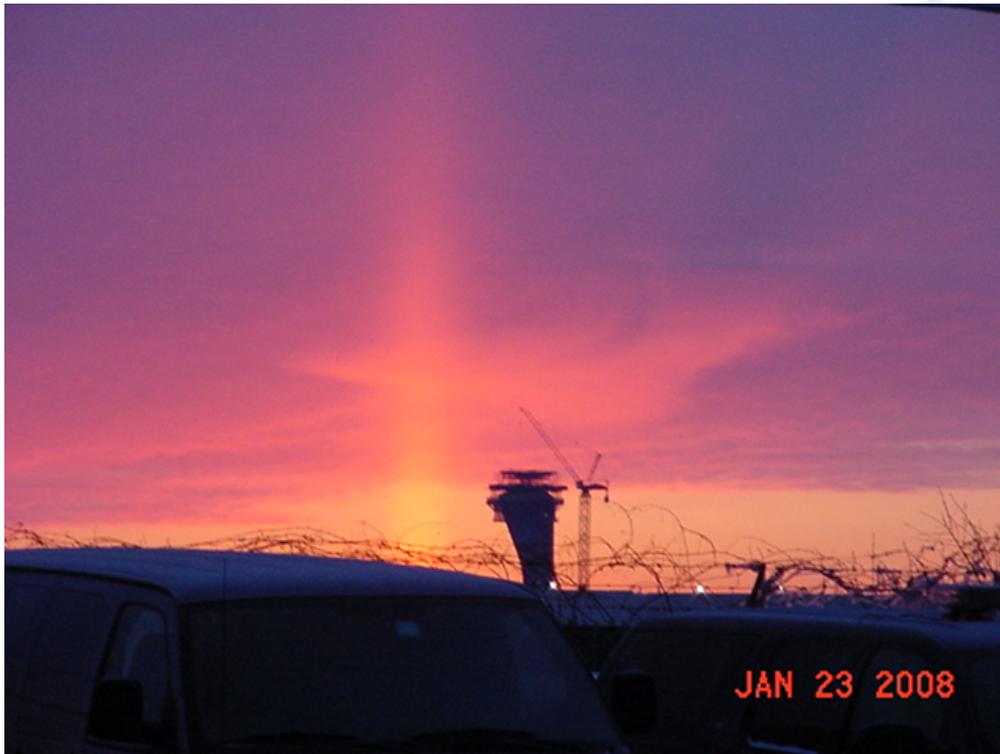

Other Support Facilities

- **ASDE-X**
 - Structural issues with cab roof installation
 - North airfield coverage will come from standalone facility
 - Interim procedures established
- **Airport Surveillance Radars (ASR-9)**
 - North Airfield ASR commissioning scheduled for February, 2009
 - Warrenville ASR to accommodate runway 10C/28C
 - Scheduled for 2012



North ASR-9
