



		2018						2019						2020						2021					
	Project	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN
A	Terminal B																								
B	TWYs M & Z																								
C	Terminals C & D																								

	Project	Description of Work	Estimated Dates	Status	Impact	Notes
A	Terminal B	Terminal B redevelopment of the Central Terminal Building (CTB). Construction expected to include the demolition of the existing terminal and associated infrastructure. Construction is for a new 35 gate terminal.	08/04/2015 to 11/07/2021	In Progress	<div></div>	The ZA ramp area is not available for use during phase 1, which is about 2 years long and began late in 2016. ZA is now decommissioned. New deicing areas have been relocated in front of the American hangars. Scheduled to open 11 of 18 gates by October, 2018.
B	TWYs M & Z	Portions of TWYs M and Z will be taken to support new construction of terminal C.	07/24/2017 to 03/19/2022	In Progress	<div></div>	In support of Terminal C redevelopment. TWY M closed to wingspan over 118ft, until Jan 2020.
C	Terminals C & D	Terminals C & D redevelopment. Construction includes demolition of the existing terminals and reconstruction. Construction is for a 37 gate terminal.	08/01/2017 to 01/12/2027	In Progress	<div></div>	Construction includes new main terminal. Terminal C & D is approx. 38% of LGA passenger traffic (275 daily departures).

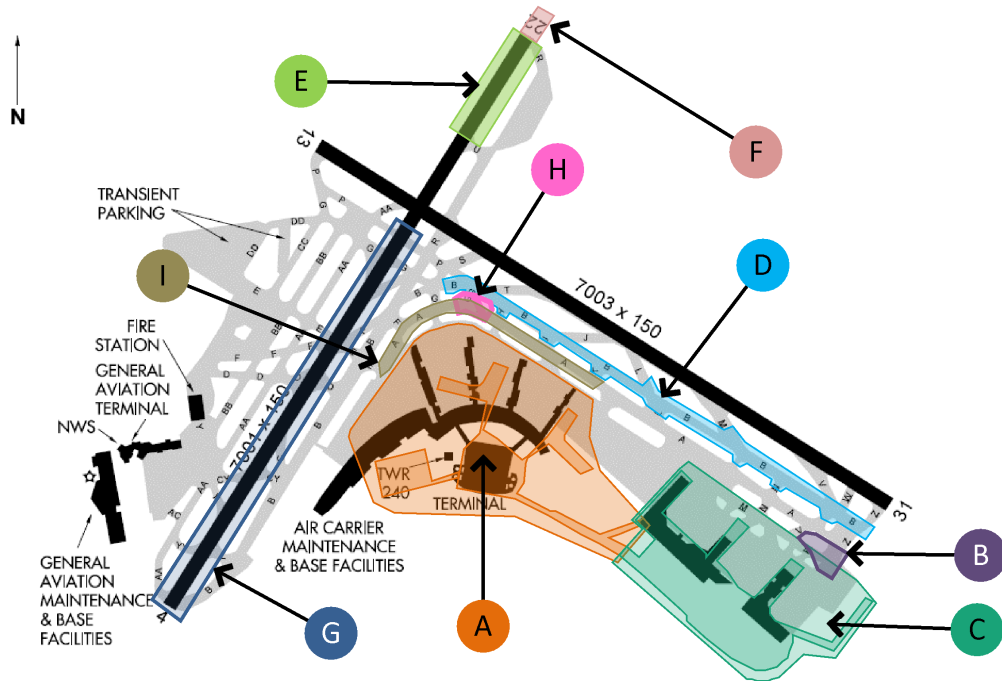

		2018						2019												2020												2021					
	Project	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN
D	TWY B																																				
E	RWY 4/22 Deck																																				
F	RWY 22 North End																																				

	Project	Description of Work	Estimated Dates	Status	Impact	Notes
D	TWY B	TWY B closed for rehabilitation. Milling and paving in sections. Includes new LED lighting upgrades.	04/06/2018 to 11/30/2018	In Progress		Construction will be completed in sections over 14 weekends. Each section requires 2 weekend closures for 36 hours. Resurfacing completed, lighting installation remains.
E	RWY 4/22 Deck	Runway 4/22 deck rehabilitation.	June 2019 to September 2019	Upcoming		The resurfacing of Runway 4/22 will be completed using night and weekend closures to minimize the effect on capacity. Tentative start date: June 2019.
F	RWY 22 North End	RWY 22 Deck extension.	June 2019 to August 2019	Upcoming		RWY 22 Deck extension to support a more stable RWY 4 localizer signal. Tentative start date: June 2019

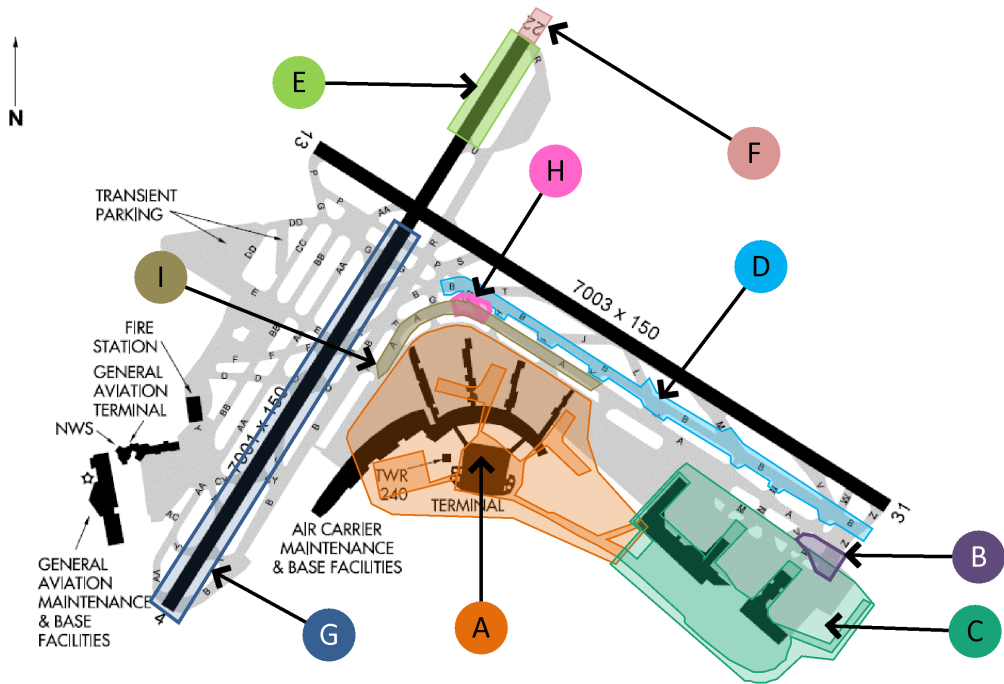

		2018						2019												2020												2021					
	Project	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN
G	RWY 4/22																																				
H	TWY A Drainage																																				
I	TWY A																																				

	Project	Description of Work	Estimated Dates	Status	Impact	Notes
G	RWY 4/22	RWY 4/22 closed for rehabilitation. Mill and overlay of runway deck wearing course, and concrete panel replacement. Resurfacing RWY 4/22 from the approach end of RWY 4 to the RWY intersection. Includes all RWY crossings and exits.	04/01/2019 to 04/01/2021	Upcoming	■	Multi-phased project. The majority will be completed during weekend closures. The RWY closures required for this project will be scheduled during nighttime, and during scheduled weekend closures to minimize impacts. Tentative start date: April 2019.
H	TWY A Drainage	Taxiway A closed for installation of new 72' drain line across TWY A to the Central Terminal Building (CTB) concourse C.	Summer 2019 to Fall 2019	Upcoming	■	TWY A closed from TWY J to TWY G, Also TWYs GG and H closed between TWYs A and B, for up to 8 weeks.
I	TWY A	TWY A closed for rehabilitation. Resurfacing TWY A between TWY E and TWY K.	April 2020 to July 2020	Upcoming	■	Tentative start date: April 2020
