

**ORDER**

6820.12

**PROJECT IMPLEMENTATION PLAN  
FOR VHF OMNIDIRECTIONAL RANGE ((VOR))  
AND DISTANCE MEASURING EQUIPMENT ((DME))**



**April 25, 1991**

**U.S. DEPARTMENT OF TRANSPORTATION  
FEDERAL AVIATION ADMINISTRATION**

**Distribution:** A-W(NN/NA/HT/SM/NS/TR/ES/LG)-33; A-Y(DE)-3;  
A-Z-11; A-X(AF/AT/RS)-33; A-FAF-0 (LTD)

**Initiated By: ANN-1 30**


## 6820.12

6820.12

[illegible]

## FOREWORD

This order transmits the project implementation plan (PIP) for the VHF Omnidirectional Range (VOR) /Distance Measuring Equipment (DME) systems. It provides guidance and direction for the orderly implementation of VOR/DME at 70 sites. The procedures and responsibilities in this order were developed using current agency directives. This order establishes program management, project implementation, and defines responsibilities governing the activities of organizations. This order also identifies and describes specific events and activities to be accomplished in order to implement the VOR/DME systems.



Rodman Gill  
Program Director for  
Navigation and Landing



TABLE OF CONTENTS

	<u>Page No.</u>
CHAPTER 1. GENERAL	1
1. Purpose	1
2. Distribution	1
3. Authority to Change This Order	1
4.-19. Reserved	1
CHAPTER 2. PROJECT OVERVIEW	3
20. Synopsis	3
21. Purpose	3
22. History	3
23.-29. Reserved	3
CHAPTER 3. PROJECT DESCRIPTION	5
30. Functional Description	5
Figure 3-1. VOR/DME Facility	6
Figure 3-2. RMMS Basic Configuration	10
31. Physical Description	11
32. System Requirements	12
33. Interfaces	14
34.-39. Reserved	14
CHAPTER 4. PROJECT SCHEDULE AND STATUS	15
40. Project Schedules and General Status	15
41. Milestone Schedule Summary	15
42. Interdependencies and Sequence	15
43.-49. Reserved	15
Table 4-1. VOR/DME Schedule	16
CHAPTER 5. PROJECT MANAGEMENT	17
50. Project Management, General	17
51. Project Contacts	18
52. Project Coordination	18
53. Project Responsibility Matrix	22
54. Project Managerial Communications	22
55. Implementation Staffing	23
56. Planning and Reports	23
57. Applicable Documents	23
Figure 5-1. Project Responsibility Matrix	24
58.-59. Reserved	25

Page No.

CHAPTER 6.	PROJECT FUNDING	27
60.	Project Funding Status, General	27
61.	Regional Funding	27
62.	Additional Funding	27
63:-69.	Reserved	27
CHAPTER 7.	DEPLOYMENT	29
70.	General Deployment Aspects	29
	Table 7-1. DRR Schedule	29
71.	Site Preparation	29
72.	Delivery	29
73.	Installation Plan	29
74.-79.	Reserved	30
CHAPTER 8.	VERIFICATION	31
80.	Factory Verification	31
81.	Checkout	31
82.	Contractor Integration Testing	31
83.	Contractor Acceptance Inspection ((CAI))	31
84.	FAA Integration Testing	31
85.	Shakedown and Changeover	32
86.	Joint Acceptance Inspection (JAI)	32
87:-89.	Reserved	33
CHAPTER 9.	INTEGRATED LOGISTICS SUPPORT	35
90.	Maintenance Concept	35
91.	Training	35
92.	Support Tools and Test Equipment	35
93.	Supply Support	35
94.	Vendor Data and Technical Manuals	35
95.	Equipment Removal	36
96.	Facilities	36
97:-99.	Reserved	36
APPENDIX 1.	VOR/DME DELIVERY LOCATIONS	1

## CHAPTER 1. GENERAL

1 **PURPOSE.** This order presents overall guidance and direction for the orderly implementation of the VHF Omnidirectional Range (~~VOR~~) Distance Measuring Equipment (~~DME~~).. The purpose of this project implementation plan (PIP) is to set forth FAA management direction and the technical approach for implementing the ~~VOR/DME~~ portion of the National Airspace System (~~NAS~~).. This order has been coordinated with cognizant FAA headquarters organizations and with regional offices. It will be used by the project office, in the office of the Program Director for Navigation and Landing (ANN), to provide general guidance to all parties having responsibilities in this implementation and it will be updated periodically to reflect current status as progress occurs.

2. **DISTRIBUTION.** This order is being distributed to branch ~~level~~ in the offices of the Program Directors for Navigation and Landing and Automation, and Training and Higher Education, the Systems Maintenance, **NAS** Transition and Implementation, Air Traffic Plans and Requirements, Flight Standards, and the Logistics Services; branch level to the FAA Logistics Center at the Aeronautical Center; director level at the FAA Technical Center; branch level to the regional Airway Facilities, Air Traffic, and Flight Standards divisions; and a limited distribution to all Airway Facilities field offices.

3 **AUTHORITY TO CHANGE THIS ORDER.** This order may only be changed by the Program Director for Navigation and Landing. Requests for changes to this document should be directed to the Manager, Navigation and Landing Engineering Division, ~~ANN-100~~, FAA Headquarters, **800** Independence Avenue, **S.W.**, Washington, DC ~~20591~~.

**4.019. RESERVED.**





## CHAPTER 2. PROJECT OVERVIEW

**20 SYNOPSIS.** The VOR/DME Program is an element of the Capital Investment Plan ((CIP)) to expand the en route navigation capability to satisfy new operational requirements that have arisen in various geographic areas and are required to improve the air route structure for more efficient movement of air traffic into and around major hub airports. The current program entails the initial contract award for a firm quantity of **40 VOR/DME** systems with options for an additional **30** systems and **30** Doppler VOR conversion kits to be exercised when funding becomes available. The equipment specification requires that these systems will be fully compliant with Interface Control Document ((ICD)) **NAS-MD-790**, Remote Maintenance Monitoring Interface Control Document, and will interface directly with the maintenance processor subsystem ((MPS))..

**21. PURPOSE.** VOR/DME is the national and international standard for providing distance and azimuth en route navigation signals to properly equipped aircraft operating in the **NAS** as well as in international airspace. The radiated signals from the VOR/DME provide the aircraft with distance and bearing information to the VOR/DME facility.

**22. HISTORY.** From 1982 through 1989, the FAA replaced **950 vacuum-tube** type VOR and VOR/TACAN ((VORTAC)) systems with solid-state equipment which has embedded remote maintenance monitoring ((RMM)) and control capabilities. The RMM associated with this equipment is not compatible with the requirements of **NAS-MD-790** and thus is not able to interface directly with the MPS at the Air Route Traffic Control Center ((ARTCC)).. It was initially determined that due to the large existing number of systems ((950)), that the new procurement should require compatibility between the new systems and the existing **FA-9996** second generation VOR-VORTAC systems. When this concept was advertised to industry, it became immediately apparent that protests, with substantial merit, based on the competitive advantage of the previous manufacturer/s of the second generation systems would be rendered that would seriously jeopardize the program schedule. The decision was then made to revise the equipment specification to create a wholly competitive situation by requiring a system that included a remote monitoring subsystem ((RMS)) function that is totally **NAS-MD-790** compliant. The specification was revised to delete the compatibility requirement and a request for proposals ((RFP)) was released on September **21, 1989**, and a contract was awarded to Wilcox Electric, Inc., on September **28, 1990**..


**23.429. RESERVED.**



## CHAPTER 3. PROJECT DESCRIPTION

**30. FUNCTIONAL DESCRIPTION.** The functional relationships of the major VOR/DME units are shown in figure 3-1. The facility central processing unit ((FCPU)) and battery charger power supply ((BCPS)) are indicated as shared units between the VOR and the DME as they indeed are; however, they are integral units of the VOR. The VOR broadcasts an omnidirectional signal containing fixed reference phase and variable phase signal components that vary in phase relationship (0 to 360 degrees) to each other as a direct function of the azimuthal position of the aircraft receiving antenna with respect to the facility. The aircraft receiver compares the phase relationship of the component signals and provides the variation in phase to the cockpit deviation indicator ((CDI)) as the azimuth bearing to the facility. The VOR azimuth information is accurate to within  $\pm 1.3$  degrees as verified by flight inspection. The VOR also provides a 1020 Hz Morse code identification signal alternating with a voice identification signal. The identification signal is removed when the VOR is shut down for maintenance or is otherwise out of service. The DME receives pulse coded interrogation signals of the correct frequency and spacing from the aircraft and after a fixed reply time delay ((50 u sec)), transmits reply pulses of the proper frequency and pulse pair spacing. The aircraft receiver measures the round-trip transit time from interrogation to receipt of the reply pulses (compensating for the fixed reply delay) and converts the time interval to slant range distance in nautical miles for readout on the cockpit instrument display panel. Additionally, the DME receives a timing identification signal from the VOR and transmits one 1350 Hz Morse code identification cycle following every three VOR identification cycles. The DME distance information is accurate to within  $\pm 0.5$  nautical miles or  $\pm 3.0$  percent of the distance, whichever is greater. The VOR/DME system includes the units shown in figure 3-1. These units are described in the following subparagraphs.

a. **VOR Transmitter.** The VOR transmitter operates in the frequency range of 108 to 118 MHz with 50 kHz spacing between channels. The transmitter provides at least 150 watts of carrier power to the antennas. The transmitter carrier output is amplitude modulated by: (1) 9960 Hz  $\pm 480$  Hz, which when detected by the frequency discriminator circuit in the aircraft receiver, produces the 30 Hz fixed phase reference signal, (2) voice signals of 300 through 3000 Hz, and (3) 1020 Hz identification signal.

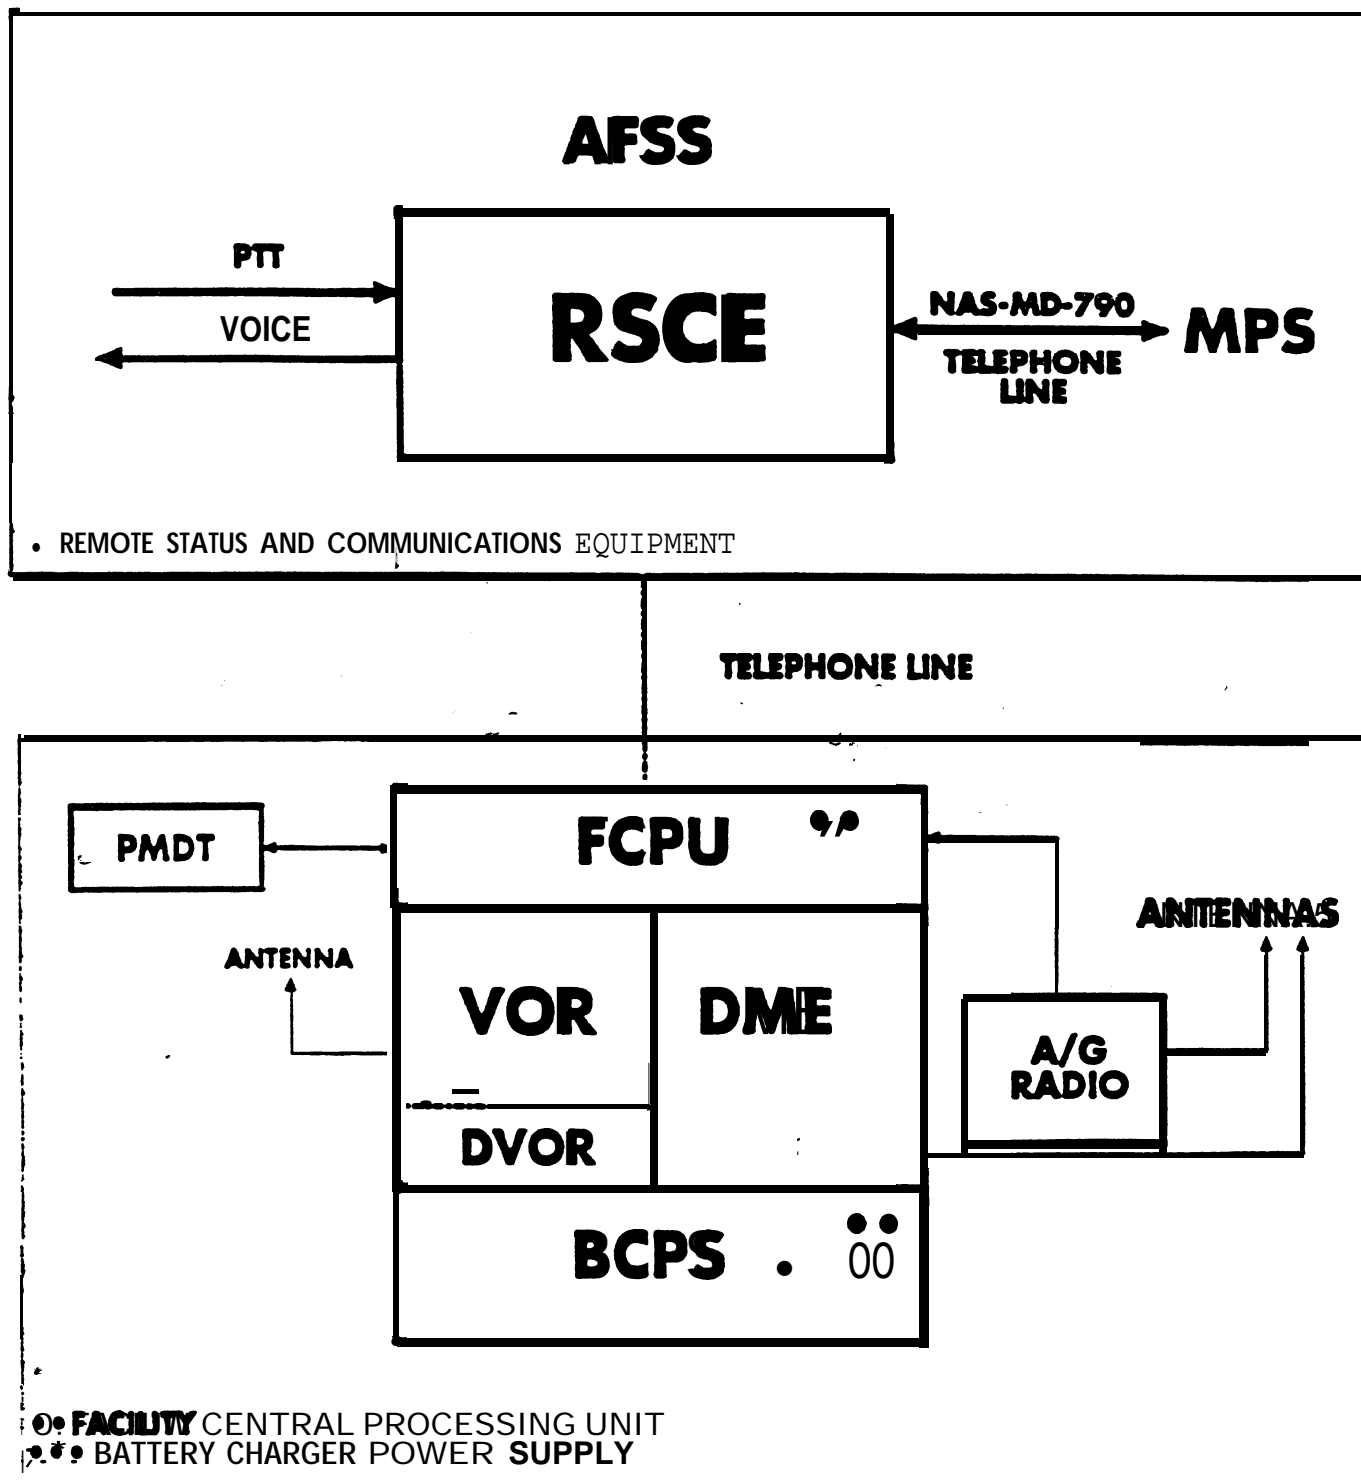

The transmitter includes the ~~goniometer~~ assembly used (1) to generate the 9960 Hz frequency modulated (FM) subcarrier signal which is used to amplitude modulate the carrier and (2) to produce two radio-frequency (RF) double sideband suppressed carrier outputs which are 30 Hz removed (30 Hz above and below) from the carrier signal. The sideband signals are fed to the four ~~alford~~ loop antenna array and when detected and demodulated, produce the 30 Hz variable signal. Additionally, the transmitter includes the identification ~~oscillator/keyer~~ unit.

b VOR Monitor. The VOR monitor receives an input signal from one of the 16 monitor antennas which are mounted on the periphery of the VOR counterpoise. The signal is fed to the monitor through the ground check switch which provides the capability of using independent signals from all of the monitor antennas for purposes of conducting a complete 16 point automatic ground check of the VOR. The automatic ground check is completely software/firmware controlled and is conducted not less than once every 15 minutes. The monitor contains built-in test equipment (BITE) which enables it to verify the accuracy of the VOR radiated signal against internal standards. The monitor shall detect faults and initiate alarm action if any of the following parameters are outside of tolerance:

- (1) Azimuth.
- (2) FM subcarrier modulation percent.
- (3) 30 Hz reference (AM) modulation percent.
- (4) FM subcarrier frequency deviation.
- (5) Identification code.
- (6) Field intensity.

The monitor alarm control circuit is such that both monitors must indicate an alarm prior to initiation of alarm and shutdown action. If the alarm results in shutdown of the VOR, there is an auto-reset circuit which will attempt three times to reset the system and continue normal operation if there are no more than three alarms within any 15-minute period. If a fourth alarm occurs during any 15-minute period, no further auto-resets are attempted. The time intervals for auto-resets are established at 20 seconds, 32 seconds, and 105 seconds following the initial alarm, assuming that none of the reset attempts are successful.

c. Facility Central Processing Unit (FCPU).. The VOR FCPU provides the RMS functions for the VOR/DME as defined in ICD NAS-MD-790,, NAS-MD-792,, Operational Requirements for the Remote Maintenance Monitoring System (RMMS),, and NAS-MD-793,, Remote Maintenance Monitoring System Functional Requirements for the Remote Monitoring Subsystem (RMS).. It provides local and remote adjustment, testing, and control capabilities of the VOR/DME equipment through appropriate equipment and external interfaces. Additionally, it manages voice and data communications between the VOR/DME equipment units and the remote status communications equipment (RSCE) and data communications between the VOR/DME equipment and the MPS..

d Battery Charger Power Supply (BCPS).. The BCPS receives its primary power from a nominal 120/240 volt, 60 Hz, three-wire, single phase alternating current (AC) power source. The BCPS provides all of the direct current (DC) power required for operation of the VOR and DME equipment and that which is required to charge and provide equalize and float voltage to the Government furnished battery bank. The power required for the DME final amplifier is permitted to be derived from the primary AC power. In the event of a failure of the primary AC power, the BCPS provides the DC voltages from the battery- bank and an alternate source of AC power from the batteries through a DC to AC inverter..

e. DME Transponder/Receiver Unit. The transponder/receiver operates on two discrete, paired frequencies in the range of 962 to 1213 mHz.. It contains the circuitry to receive and decode interrogation signal pulses and in response thereto, radiate a properly coded reply pulse pair after a specific reply delay time. The transponder will also produce and radiate random pulse pairs sufficient-in number to maintain a minimum output pulse count of  $1350 \pm 150$  pulse pairs. Additionally, the transponder will produce and radiate International Morse Code identification signals in response to a timing signal from the VOR.. The unit contains a **duplexer** which permits simultaneous operation of the receiver and transponder on a single antenna. The transponder is capable of being set up for two different peak power levels of 1000 watts or 100 watts depending on the facility requirements.

f DME Monitor. The monitor is designed to provide full-time, automatic monitoring of the transponder/receiver unit through the use of BITE. It contains an internal interrogation signal generator which in addition to producing on-channel interrogation pulse pairs, produces pulse pair outputs for test purposes of  $\pm 200$  Hz and  $\pm 900$  Hz from the on-channel frequency.

The BITE within the monitor shall be used for normal **monitoring** of the operating transponder and receiver and to provide testing for alarm limit certification upon command from the **FCPU**. The monitor will verify correctness and initiate alarm action if any of the following parameters are outside of tolerance:


- (1) Reply delay.
- (2) Output pulse spacing.
- (3) Receiver sensitivity.
- (4) Transponder output pulse rate.
- (5) Transponder power output.
- (6) Identification.
- (7) Radiated power level.

The **DME** control circuitry is the same as the **VOR** in that it **requires** both monitors to be in alarm before alarm and shutdown action is initiated. The **DME** also contains the automatic reset circuitry described under paragraph 31b for the **VOR** monitor.

g. Remote Status and Communications Equipment ((RSCE)). See figure 3-2. The **RSCE** is located at the local automated flight service station (**AFSS**) and is used to provide **VOR/DME** operational status information and two-way audio communications capability to the **AFSS** operations personnel. It additionally provides a data interface between the **VOR/DME** facility and the **MPS** at the controlling **ARTCC**. The **RSCE** includes the following equipment subassemblies:

(1) Communications units. The communications unit provides two-way voice communications between the **VOR** facility and the **AFSS**. It enables the flight service specialist to voice modulate the **VOR** transmitter by the use of a push-to-talk signal to the **VOR** which removes the **VOR** voice identification signal and replaces it with that of the specialist. It also provides the signal path of the remote communications outlet (**RCO**) receiver voice from the **VOR** site to the **AFSS** operations room speakers.

(2) RSCE processing unit. The **RSCE** processing unit separates the **VOR/DME** operational status information from the data being transmitted to the **MPS** and provides the status information to the **VOR/DME** status unit. The unit will also provide buffer and processing action in collecting input data at

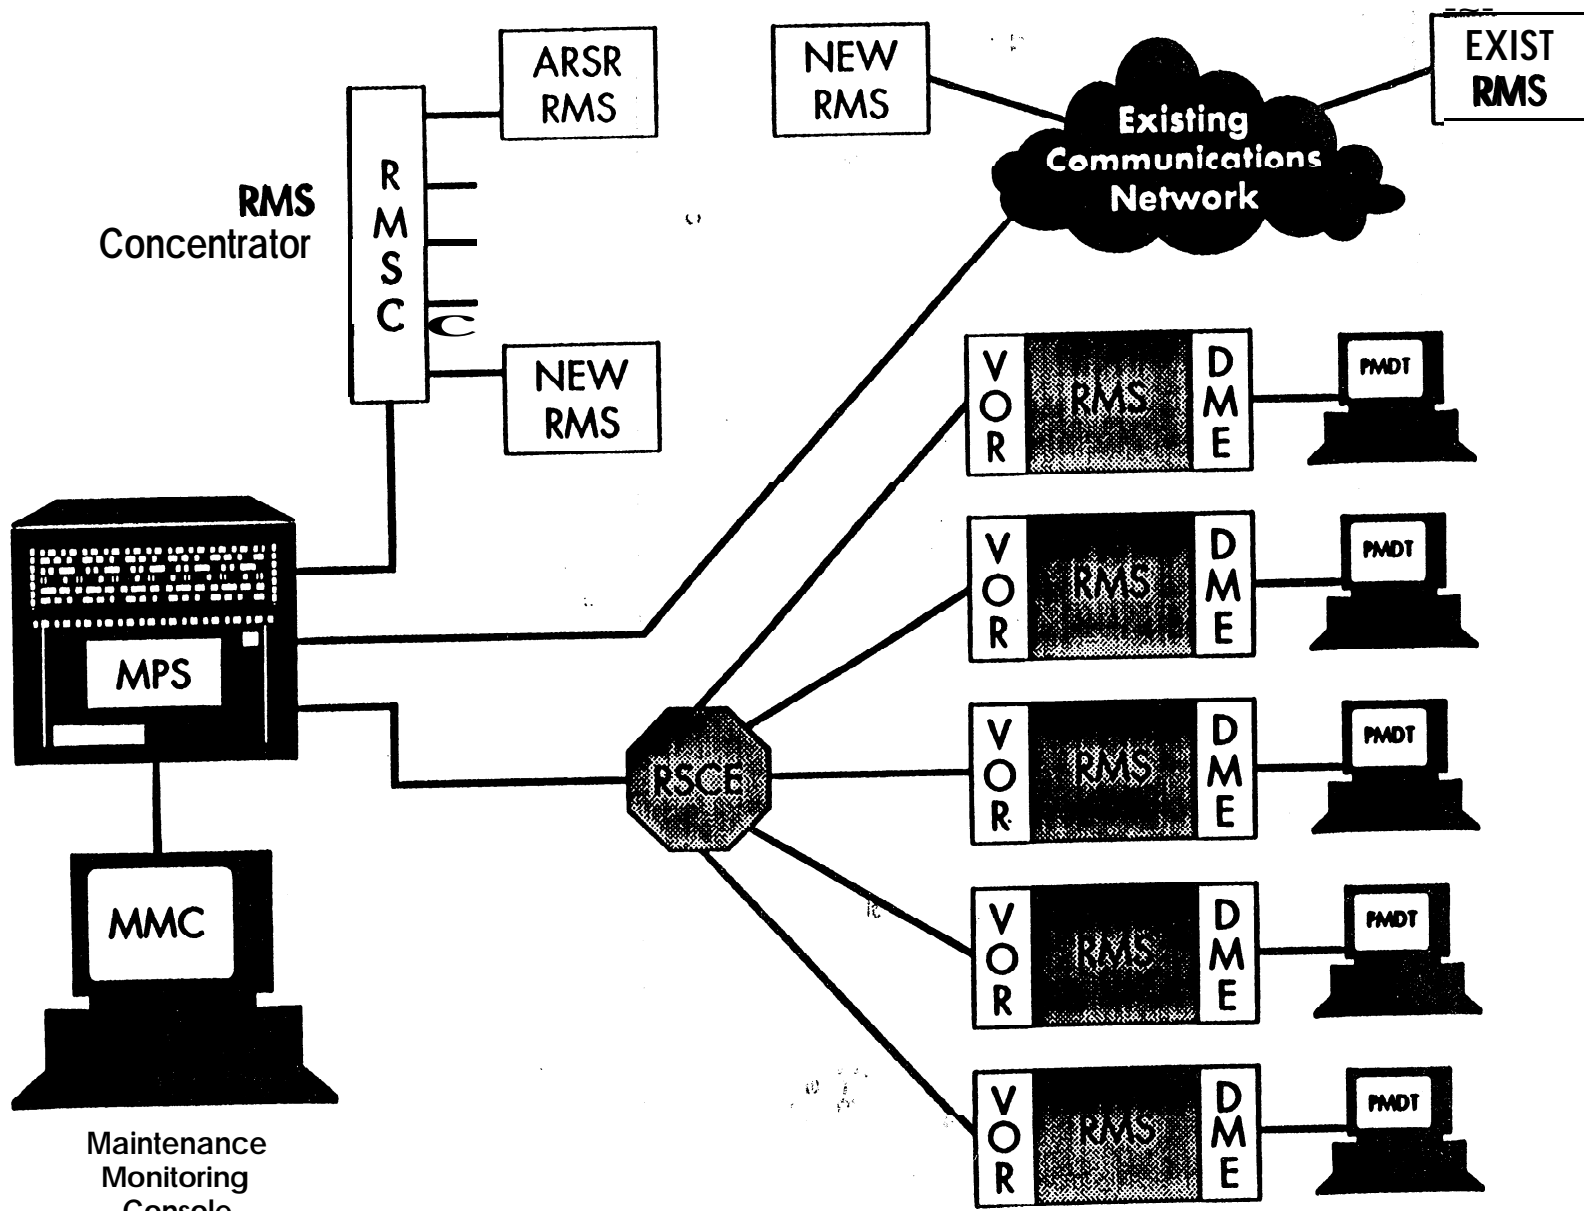

2095/O/H/040591-1/32



differing rates from the **VOR/DME FCPU** and the **MPS** and will buffer the received data to a higher or lower rate as appropriate.

((3)) **VOR/DME status unit.** The **VOR/DME** status unit will be installed in a console in the **AFSS** operations room that may be **remoted** up to **200** feet from the **RSCE**. The status unit will provide the following functions:

- (a) Visual indication of the status of the **VOR** and **DME** systems by the use of red **ALARM** and green **NORMAL** lights.
- ((b)) Visual indication of the monitor in **BY PASS**.
- ((c)) An aural indication of a **VOR** or **DME** alarm.
- ((d)) A momentary aural alarm silence switch.
- ((e)) A momentary push button to test the operability of all lamps.

**31. PHYSICAL DESCRIPTION.** The **VOR/DME** equipment will be housed **in not** more than three aluminum or steel cabinets designated to be installed inside a Government furnished shelter. The cabinets will include a grounding-type convenience outlet mounted on the bottom front of the cabinet. The cabinets will have two top openings with removable cover plates for cable entrance and egress. The openings will be designed to accommodate standard two and one-half inch electrical metallic tubing (EMT) to be furnished by the Government. The cabinets are designed to provide maximum accessibility to all units, modules, assemblies or subassemblies from the front, side, top, or rear of the cabinet by the use of swing-out or pull-out chassis, pull-out drawers, hinged cabinet or equivalent means. Major assemblies or units will be designed for complete removal from the cabinet without disassembly. Cable retractors and circuit extenders will be provided for module operation in the open position. A circuit board extractor or circuit board handles will be provided for ease in removal of circuit boards from their connectors. The extender boards or cables are intended for the accomplishment of detailed trouble shooting only. Normal functional checks of the equipment can be made through the provision of significant test points which are readily accessible to allow testing without interruption of operation. All of the **VOR/DME** adjustments required for operation and maintenance and all indications resulting from such adjustment will be accessible locally via the **FCPU** to portable maintenance data terminal ((**PMDT**)) interface or remotely from the **MPS**. The **PMDT** interface will be available on the front panel of the equipment cabinet containing the **FCPU**. The **RSCE**, located in the **AFSS** equipment room, is designed for

installation in a standard **19-inch** cabinet rack. The equipment is chassis mounted on a rack panel and requires an E panel (**8 23/32"** high) space in an existing equipment rack. The input and output connections are on the rear of the chassis. The **VOR/DME** status unit is to be installed in an existing operations console in the **AFSS** operations room. The status unit is a panel mounted **chassis** with **removable rear** cover designed to be mounted on the console within a rectangular cut-out no more than 3 inches wide and 5 inches high. Facilities for connecting the status unit to the **RSCE** are provided by a recessed male connector on the rear of the chassis. The status unit receives its operating power requirements through the **RSCE** interconnecting cable.

**32. SYSTEM REQUIREMENTS** The **VOR/DME** requirements include power, siting, shelter, and operational needs. System reliability and maintainability are design requirements of the equipment specification and will be demonstrated prior to full field deployment.

a. Power. The **VOR/DME** system operates from a nominal **120/240** volt, **60** Hz, three-wire, single phase AC power source. The input power requirements are conservatively estimated to be less than **2500** watts. The commercial power system will be supported with a Government furnished back-up battery bank designed to provide **uninterruptable** power for a minimum of 4 hours in the event of failure of the primary power. Upon restoration of the primary power, the batteries will be recharged from a **50** percent' discharge state to full charge in less than **24 hours**. Electrical work will be in accordance with specification **FAA-C-1217e**.

b. Siting The siting of a **VOR/DME** facility is a very **complex** procedure and must include aspects in addition to the electromagnetic propagation of the **VOR/DME** signals. The siting requirements for **VOR** are somewhat more stringent than those of the **DME** and will usually determine the final site selection. In addition to the basic requirement for a relatively flat or downward sloping surface extending outward in all directions from the **VOR** site that is devoid of natural or man-made reflecting surfaces, consideration must also be given to the site acquisition costs, proximity of an acceptable primary power source, results of environmental impact studies and other such factors. A complete coverage of the **VOR/DME** siting requirements is presented in Order **6820.10**, **VOR**, **VOR/DME** and **VORTAC** Siting Criteria, that must be used for this purpose.

c. Shelter. The **VOR/DME equipment** shelter is to be furnished by the **Government**. The regional Airway Facilities' division will be **responsible** for **providing** the shelters which

will be made available from a Washington office open-ended ~~requirements contract~~. The shelter contractor will be ~~responsible~~ for erecting the shelter and counterpoise on the foundations provided by the Government's site construction contractor. New construction utilizing the Washington office ~~standard~~ shelters will be required for the establish projects ~~whereas~~ the existing shelters may be reused for the replacement projects ~~if the~~ responsible region determines that the shelter is fully acceptable. The Air Traffic Control Tower/Facilities Program, ~~ANS-240~~, is in the process of preparing a national ~~standard~~ for the VOR/DME equipment shelters that will be used for all new shelters. The standard is expected to be published no later than the end of May 1991..

d Operational Needs. In order to interface the VOR/DME site with the AFSS and thence to the MPS location, a Government furnished dedicated four-wire telephone line must be provided. The telephone lines will be private line, data voice-grade circuits that will be unity gain and will be furnished with OdB transmission level point ((TLP)) at the send and receive interface. The contractor is to deliver the ICD in accordance with ~~NAS-MD-790~~ within 12 months after contract ~~award~~. The ICD will define all pertinent information required to interface the VOR/DME RMS with the MPS.. After the ICD has been validated and before field deployment of the VOR/DME systems, the interim monitor and control software ((IMCS)) program needs to -be loaded into the MPS.. Without an operational VOR/DME IMCS program residing in the MPS,, remote monitor and control functions will not be operational.

e. Electromagnetic Interference. Conducted emission, conducted susceptibility, radiated emission, and radiated susceptibility levels on incoming AC power leads, interconnecting leads, radiated signals, antenna leads and control lines, as applicable, shall not ~~exceed~~ the limits defined in ~~MIL-STD-461~~, Electromagnetic Emission and Susceptibility Requirements for the Control of Electromagnetic Interference, as specified in the equipment specification, ~~FAA-E-2678C~~ VOR/DME Equipment Specification.

f Reliability. The VOR/DME equipment reliability criteria are depicted below.

Equipment	Mean Time Between Failures ((MTBF))
VOR	7,500 Hours
DME	5,000 Hours
RSCE	20,000 Hours

g Maintainability. The VOR/DME mean time to repair ((MTTR)) shall be equal to or less than 30 minutes. The specified repair time shall include diagnostic time, removal of the failed line

replaceable unit ((**LRU**)), replacement, and installation of the new **LRU** including any adjustments or data loading necessary to initialize the **LRU** and all adjustments required to return the **VOR/DME** to normal operation.

**33. INTERFACES.** The following interfaces are required for the **VOR/DME** system.

a. **FCPU to RSCE.** The **FCPU** to **RSCE** interface is in accordance with **EIA** standard **RS-232**, wired as synchronous data terminal equipment ((**DTE**)). It will interface through a contractor furnished commercially available voice over data modem system with the Government furnished four-wire telephone line and will operate at a minimum rate of **1200** baud. This interface will be fully compatible with **NAS-MD-790**.

b. **FCPU to PMDT.** The **FCPU** to the **PMDT** interface is in accordance with **EIA** standard **RS-232**, wired as synchronous data communications equipment ((**DCE**)). The **PMDT** interface will automatically adjust to baud rates of **2400**, **4800**, and **9600**.

c. **RSCE to MPS.** The **RSCE** to **MPS** interface is in accordance with **EIA** standard **RS-232**, wired as synchronous data equipment. It will interface through a Government furnished commercially available data modem to the Government furnished four-wire telephone line. The data rate on this interface will automatically adjust to baud rates of **2400**, **4800**, and **9600**. The interface will be fully compliant with **NAS-MD-790**.

d. **RSCE to FCPU.** The **RSCE** to **FCPU** interface shall be identical to the **FCPU** to **RSCE** addressed in paragraph **33a**.

e. **RSCE to Communications Unit ((CU)).** An interface will be provided by the contractor for the transfer of status data and voice communications between these two units.

f. **CU to AFSS Operations Room.** A multi-pair audio cable will be provided by the Government to interface the **CU** to the **VOR/DME** status unit and the **AFSS** operations room console for two-way voice communications and for application of the **VOR** push-to-talk signal. The interconnect cable and connector types will be specified by the contractor.

**34.139. RESERVED.**

## CHAPTER 4.. PROJECT SCHEDULE AND STATUS

**40. PROJECT SCHEDULES AND GENERAL STATUS.** The **VOR/DME** program is a multiyear funded effort.. The **FY-89** and **FY-90** funding was sufficient to accommodate an initial award for a firm quantity of **40 VOR/DME** systems and to exercise one of three options for **10** additional **VOR/DME** systems, the training option and the option for **30** each Doppler **VOR** conversion kits. It is planned that the final two options for **20** systems will be exercised using **FY-92** funds (assuming they are approved by Congress).

**41. MILESTONE SCHEDULE SUMMARY.** The current project schedule is shown in Table 4-1,, **VOR/DME** Schedule. Project events are scheduled in relationship to the date of contract award. This table is not meant to be an all inclusive listing of all project milestones necessary for project completion but it does include the very major project requirements.

**42 INTERDEPENDENCIES AND SEQUENCE.** The total operational capability of the **VOR/DME** is dependent upon the loading of the **IMCS** program into the **MPS** at each of the controlling **ARTCC** locations as previously discussed in paragraph 32d.. The **ICD** required for this application is contractually scheduled for delivery **12** months after contract award; assuming that validation and acceptance of the **ICD** is completed in a reasonable period of time, programming of the **IMCS** should be completed in sufficient time to satisfy program requirements. The **VOR/DME** program is not dependent on any other programs.

**43.-49.. RESERVED.**

ACTIVITY/MILESTONE	CURRENT SCHEDULE
Contract Award	9/90
Master Test Plan (MTP) Approval	10/90
Project Implementation Plan (PIP) Approval	10/90
Post Award Conference	10/90
System Design Review	2/91
Contractor MTP	4/91
Preliminary Design Review	5/91
Initiate Deployment Readiness Review (DRR) Process	5/91
Convene DRR Team Meeting	7/91
Critical Design Review (CDR)	9/91
Interface Control Documentation (ICD)	9/91
Final Software Test Descriptions	11/91
Instruction Book Draft Manuscript	1/92
Final Hardware Test Procedures	5/92
Commence Factory Tests	6/92
Exercise Contract Option for 20 Additional Systems	6/92
Ship First Article to FAA Technical Center	8/92
Conduct Production Acceptance Test and Evaluation • Site Acceptance Test (PAT&E-SAT) at FAA Technical Center	9/92
Conduct Integration Test/System Level Test and Evaluation (IT/SLT&E)	10/92
Conduct Shakedown Test and Evaluation (ST&E)	11/92
Submit DRR Report	12/92
Deployment Decision	1/93
First Site Delivery	1/93
Conduct Joint Acceptance Inspection (JAI)	2/93
First Operational Readiness Demonstration (ORD) and Commission	3/93
Deliver 6 Production Systems Per Month	

## CHAPTER 5. PROJECT MANAGEMENT

**50 PROJECT MANAGEMENT,, GENERAL.** This chapter describes the organizations within the Office of the Associate Administrator for NAS Development (AND) that are directly responsible for the VOR/DME program management.

a. Associate Administrator. The Associate Administrator's office manages, directs, and executes the FAA's engineering and management activities related to facilities design, air navigation, landing aids, and air traffic control facilities and equipment to ensure that the NAS is efficient, economical, and responsive to operational needs.

b Navigation and Landing Program (ANN-This organization is the principal element within the Office of the Associate Administrator responsible for the development and implementation of systems, programs and facilities requirements for navigation and landing systems.

c. Navigation Program ((ANN-300)). This organization is the principal element of ANN-1 responsible for design, development and implementation responsibilities for all aids to navigation.

d VOR/DME Program. The VOR/DME project manager is supported by the matrix organization and is responsible for the management of the VOR/DME program from inception to facility commissioning. The project manager's responsibilities include:

((1)) Management.. Planning, scheduling, and managing the program from budget submission to development of procurement documentation through contract award, system deployment, and commissioning.

((2)) Logistics Support. Provides, in conjunction with the National Airspace Integrated Logistics Support (NAILS) Management Team ((NAILSMT)), technical guidance to define logistic support requirements, including provisioning, training and documentation, for the support of the VOR/DME program.

((3)) Technical Officer. Providing engineering support, advice, and consultation to the contracting officer during procurement and contract management.

((4)) Cost Data. Developing and providing cost data, controlling assigned funds, and adjusting program schedules, requirements, and objectives as required to complete the program.

((5)) Testing. Takes the lead in the review, coordination,

and approval of the contractor's proposed testing program. Coordinates with other responsible organizations in the development, reviews, and approval of test procedures designed to demonstrate total **NAS** deployment acceptability of the **VOR/DME** systems.

**51. PROJECT CONTACTS.** This paragraph lists **VOR/DME** project contacts and their routing symbols and telephone numbers.

- a. Program Director. **Rodman** Gill, ANN-1, **FTS-267-6531.**
- b. Program Manager. Charles **Ochoa**, ANN-300, **FTS-267-6600.**
- c. Project Manager. Charles Beam, ANN-130, **FTS-267-6589.**

**52. PROJECT COORDINATION.** The **VOR/DME** program requires coordination with other Washington office organizations, with regional airway facilities and logistics personnel, and with the prime contractor. Coordination with the organizations listed in the following subparagraphs is essential for proper management of the **VOR/DME** program.

a. Maintenance Engineering Division (**ASM-100**). **ASM-100** reviews procurement specifications to ensure the design meets the reliability and maintainability requirements and supports the general maintenance philosophy. **ASM-100** also develops maintenance standards and plans for implementation of maintenance concepts.

b. Maintenance Operations Division (**ASM-200**). **ASM-200** participates in the development and review of maintenance plans. In addition, **ASM-200** develops national Airway Facilities sector staffing standards for the **VOR/DME** program and validates maintenance staffing requirements. The program manager ensures the project is in conformance with staffing, training, certification policies, guidelines, and requirements.

c. Telecommunications Management and Operations Division **ASM-300**. **ASM-300** is responsible for the overall management of FAA telecommunications, both national and regional. They determine the general networking approach to satisfy all telecommunications needs and coordinate with regional TM&O organizations to implement the required networks or circuits.

d. Spectrum Engineering Division (**ASM-500**). **ASM-500** obtain; frequency authorization necessary to satisfy the requirements of the **NAS**. The division also provides engineering support to regional and field facilities in the resolution and prevention of RF interference to **NAS** facilities.



e. National Engineering Field Support Division (ASM-600). ASM-600 prepares the ST&E requirements and test plans and conducts the ST&E on the first VOR/DME system. After system deployment, they are responsible for national documentation, equipment instruction book changes, equipment modifications, and field engineering support.

f. NAS Support Division (ALG-200). ALG-200 develops, recommends, and issues agency procedures, standards, and policies for material supply and management and disposal of personal property, and acquisition, management, and disposal of real property.

g. Contracts Division (ALG-300). ALG-300 performs cost/price analyses of contractor's proposals and participates as member of the Source Evaluation Board. In addition, ALG-300 provides procurement support for the VOR/DME by planning, placing, and administering contracts for the VOR/DME equipment. ALG-300 also designates a contracting officer (CO) who is responsible for all contractual matters. The CO is the only individual authorized to approve contract changes impacting price, delivery, or schedule.

h. Industrial Division (ALG-400). ALG-400 performs factory inspection of the VOR/DME equipment. ALG-400 assigns a quality reliability officer (QRO) at the time the contract is awarded. The QRO is the FAA representative at the contractor's facility and is responsible for verifying quality control. The QRO is directed by FAA policy and procedure, and by the terms and conditions of the contract.

i. FAA Academy (AAC-900). AAC-900 provides maintenance training and coordinates with ASM-200 in the development of a training plan.

j. Technical Training Division (AHT-400). AHT-400 analyzes training proposals prepared by ASM-200 and initiates action to meet training requirements.

k. FAA Aviation Standards National Field Office. The FAA Aviation Standards National Field Office is responsible for conducting flight inspections of VOR/DME systems needed to accomplish the following functions.

(1) Determining if the operational status of a facility or system is in accordance with the established tolerances.

((2)) Certifying the facility or system for operational use in the **NAS** when all operational requirements have been met.

((3)) When applicable, ensuring that required Notices to Airmen ((NOTAMS)) are issued for any facility or system restriction.

1. Maintenance Processors Software Branch ((ANA-120)).  
**ANA-120** has the responsibility to develop a **VOR/DME RMS INCS** module.

m. Nails Program Division ((ANS-400)). **ANS-400** coordinates the development of an integrated logistics support plan for the **VOR/DME** acquisition.

n. FAA Logistics Center ((AAC-400)). **AAC-400** is responsible for providing spares inventory, FAA Logistics Center level repair, input and project coordination for support requirements such as provisional technical documentation and engineering drawings. They are responsible for timely coordination of **excessing** property and phaseout supply support from excess if needed.

o. FAA Regional Offices. The FAA regional offices, through established administrative structures, coordinate with all responsible parties to assure adequate funding, establish system commissioning/service availability dates, assign project field representatives and determine utility availability for the **VOR/DME** system. The regions also provide field engineering as **required** to support preparations for the installation of the **VOR/DME** equipment; order Government Furnished Material ((GFM)) for tools and test instruments to support the **VOR/DME** installation and acceptance; tailor installation drawings to be site specific; initiate work orders and travel authorization; and assign field personnel. The following regional offices are responsible for the coordination required to accomplish the functions listed in subparagraphs **52 (1)** and **(2)**.

((1)) Regional Airway Facilities Division.

(a) Installing facilities systems and equipment in accordance with established standards, specifications, and instructions.

(b) Notifying the appropriate sector that a project has been funded and issuing a projected implementation schedule.

((c)) Provide advance notification to the Logistics division of pending real estate site requirements, construction contract requirements, and real property requirements. Site acquisitions and construction contracts are often lengthy and laborious tasks requiring a substantial amount of time.

((d)) Providing the sector an opportunity to review and participate in project plans during **the** engineering phase **and** for furnishing the sector a copy of the engineering plans and contract documents.

((e)) Providing the sector a copy of the project work order at least **10** days before the start of project work.

((f)) Providing the appropriate facility reference data file ((**FRDF**)) information to the sector for inclusion in the **FRDF**. These data requirements will be established by the National Engineering Field Support Division, **ASM-600**, as part of ST&E.

((g)) Notifying the joint acceptance board chairman of when the facility will be ready for JAI, providing the sector all data necessary to **prepare** warranty failure reports on items failing prior to JAI, and **providing** regional Airway Facilities division representatives for participation in the JAI.

((h)) Establishing and maintaining a follow-up file for monitoring and clearing all JAI report exceptions, reviewing all JAI reports and follow-up reports for correctness, completeness, and proper distribution, taking appropriate and timely actions to clear JAI report exceptions, and identifying additional sources of funds or initiating budgetary action, as necessary, to clear exceptions.

## ((2)) Airway Facilities Sector.

(a) Reviewing contract documents and engineering plans during the engineering **phase** and providing comments to the regional Airway Facilities division.'

((b)) Providing personnel as required at appropriate ~~times throughout the~~ project to witness and/or participate in construction, installation, tune-up, tests, and **collection** of technical reference data.

((c)) Providing **a** representative to serve as the joint acceptance board chairperson and other qualified personnel for participation in the JAI, preparing and distributing the JAI report, and assuming maintenance responsibilities and

custodianship for facilities, systems, or equipment at the conclusion of JAI.

(d) Coordination and follow-up on exceptions after the JAI to include exceptions assigned to other organizations or to a contractor for clearance, clearing exceptions which have been assigned to the sector, reporting the clearance of exceptions, and reviewing all waived exceptions to determine if actions will impact sector operations or other organizations.

(e) Maintaining all equipment warranty information and reporting equipment failing under warranty.

(f) Receiving, storing, and shipping project materials and disposing of excess equipment and materials.

**53 PROJECT RESPONSIBILITY MATRIX.** Figure 5-1, Project Responsibility Matrix, illustrates the FAA organizations responsible for the implementation of each significant function of the VOR/DME project.

**54 PROJECT MANAGERIAL COMMUNICATIONS.** The VOR/DME project manager within ~~ANN-1130~~ is the focal point of all internal project communications. Organizations supporting the VOR/DME program will designate a representative to maintain communications with the Navigation ~~APME~~, ANN-1130, and the VOR/DME project manager. Supporting organizations maintain communications within the FAA but never directly with the contractor without the prior permission of the CO. The meetings listed in subparagraphs **54a- 54d** are the regularly scheduled project meetings.

a. The National Airspace Integrated Logistics Support (NAIS) Management Team Meeting. These meetings are held to ensure that there is an interrelated, unified, and iterative approach to the managerial and technical activities which support the NAS. During these meetings, issues affecting logistics management, maintenance planning, supply support, test and support equipment, manpower and training support, support facilities, technical data, and packing, handling, **storage** and transportation are discussed and resolved. These meetings can be held at the FAA headquarters, FAA Logistics Center, or at the contractor's facility on a semiannual basis.

b. Program/Project Status Review Board Meetings. These meetings are held on a monthly basis at FAA headquarters to discuss project status and to resolve problems and issues

151

effecting all phases of the project. These meetings will commence at time of contract award and will continue until system deployment has been completed.

c. Program Overview Meetings (POM).. The contractor shall conduct quarterly POM's at the contractor's facility beginning at the post award conference and ending at acceptance of the final system under contract. The purpose of the POM's shall be for the contractor to present a detailed contract status, to track outstanding action items, review potential and actual technical and programmatic problem areas and to evaluate performance with respect to program milestones presented in the Program Management Plan.

d. Technical Interchange Meetings (TIM), The Government may request a monthly TIM between the contractor and the technical officer or designated representatives. The purpose of these TIM's is to surface, discuss, and resolve through mutual agreement any technical, schedule, or programmatic issues associated with the VOR/DME contract.

55. IMPLEMENTATION STAFFING. There are no personnel requirements peculiar to the implementation phase of the VOR/DME project.

56. PLANNING AND REPORTS. None required.

57. APPLICABLE DOCUMENTS. The following documents have been referenced within this order.

a. FAA-E-2678c, VOR/DME Equipment Specification, August 7, 1989.


b. FAA-G-2100e, Specification, Electronic Equipment, General Requirements, March 11, 1987.

c. Order 6030.45, Facility Reference Data File, February 3, 1987.

d. Order 6820.10, VOR, VOR/DME, VORTAC Siting Criteria, April 17, 1986.

e. MIL-STD-461C, Electromagnetic Emission and Susceptibility Requirements for the Control of Electromagnetic Interference, August 4, 1986.

FIGURES-1. PROJECT RESPONSIBILITY MATRIX

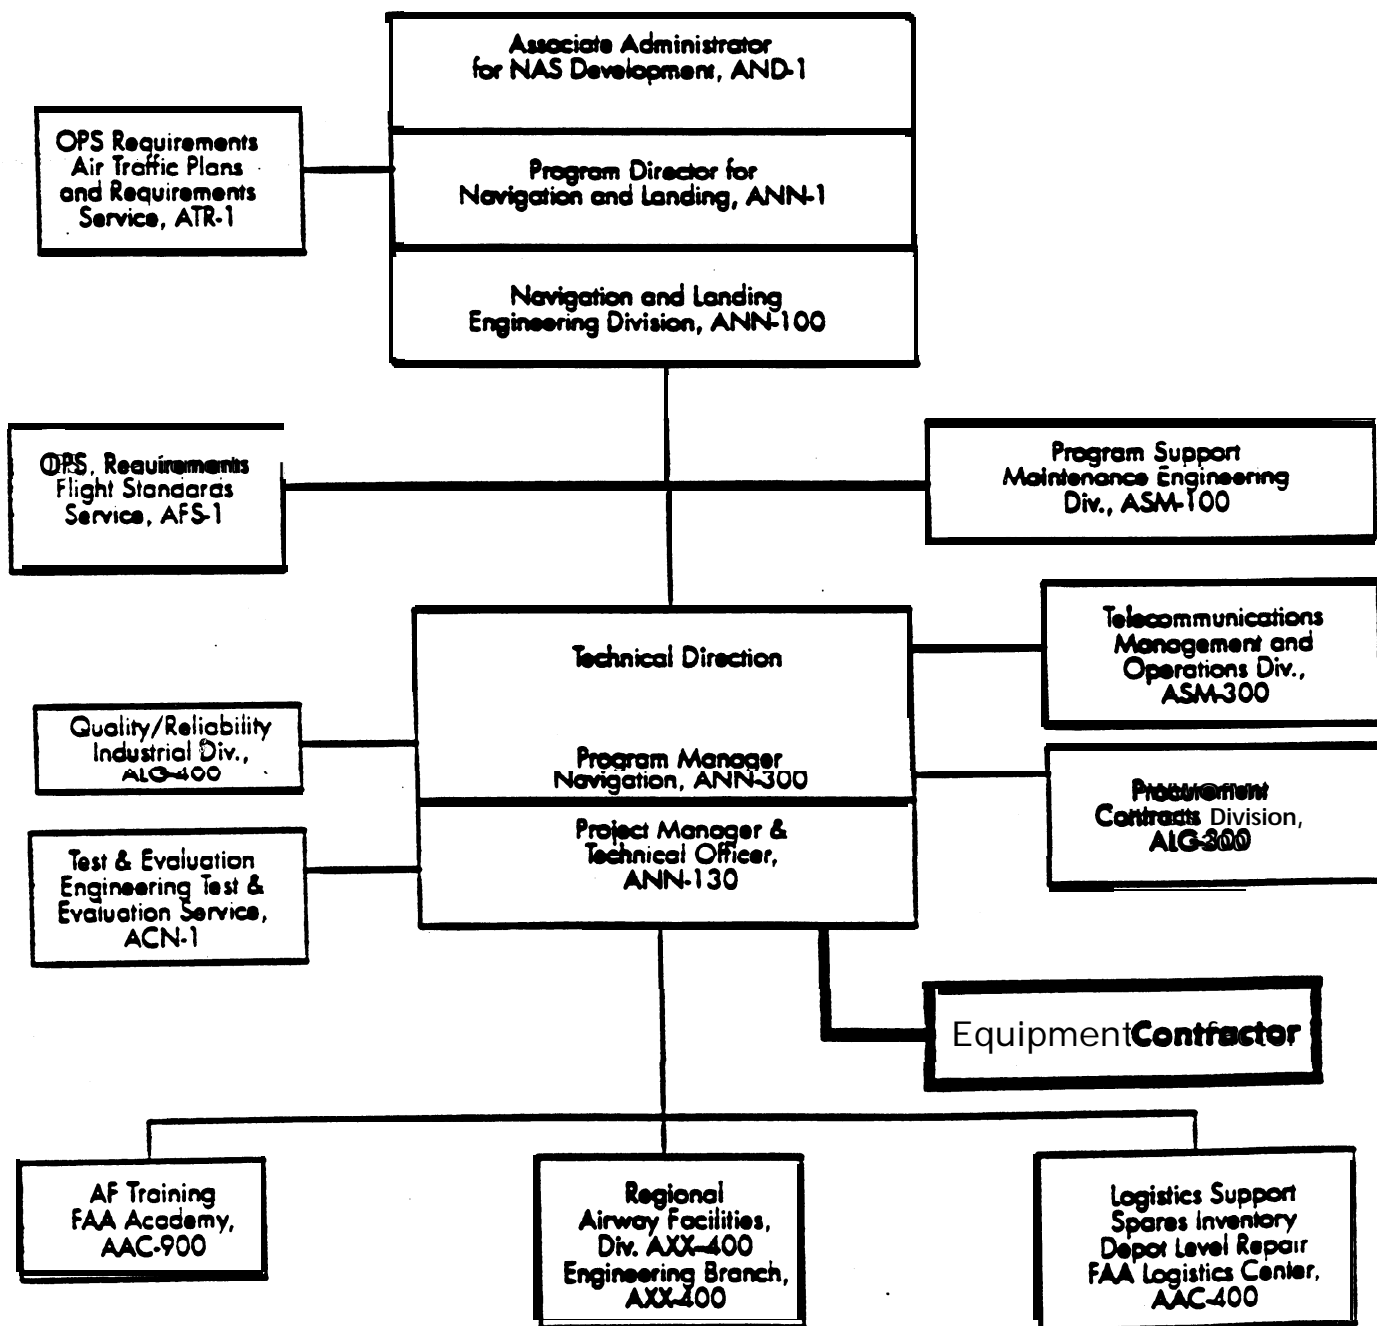

- I . site preparation
- I . system checkout
- I . joint acceptance inspection
- I . commissioning

- f. Remote Maintenance Monitoring System Interface Control Document, NAS-MD-790, June 10, 1986.
- g. Operational Requirements for the Remote Maintenance Monitoring System, NAS-MD-792, October 3, 1988.
- h. Functional Requirements for the Remote Maintenance Monitoring System, NAS-MD-793, February 28, 1988.
- i. FAA-D-2494/b, Technical Instruction Book Manuscript: Electronic, Electrical and Mechanical Equipment, Requirements for Preparation of Manuscript and Production of Books, March 14, 1984.
- j. Order 4800.2A, Utilization and Disposal of Excess and Surplus Personal Property, September 7, 1977.
- k. FAA-C-1217c, Electrical Work, Interior, September 30, 1968.
- l. EIA-RS-232-C, Industrial Standard, Interface Between Terminal Equipment and Data Communication Equipment Employing Serial Binary Data Interchange.

58.-59. RESERVED.





## CHAPTER 6. PROJECT FUNDING

**60. PROJECT FUNDING STATUS,, GENERAL.** Project funding for the ~~VOR/DME~~ program is a multiyear effort. The initial award for 40 systems used ~~FY-89~~ funds and the first of three options for 10 systems was exercised at time of contract award to Wilcox Electric, Inc., using ~~FY-90~~ funds. The remaining two options for 10 systems each will be exercised prior to July 1992 using ~~FY-92~~ funds assuming that these funds will be approved by Congress for the ~~FY-92~~ budget. The contract contains a provision which requires that the final option must be exercised within 2 years following the contract award.

**61. REGIONAL FUNDING.** The ~~program~~ funding includes those funds ~~toobe~~ provided to the regional Airway Facilities divisions for site acquisition, ~~construction,, installation,,~~ electronic tune-up, and flight inspection ~~costs,,~~ less the regional in-house labor costs.

**62. ADDITIONAL FUNDING.** Program funds are also provided for ~~in+house~~ engineering support and the costs associated with the first article installation and testing at the FAA Technical Center .

**63. ~~969.~~ RESERVED.**



## CHAPTER 7. DEPLOYMENT

**70 GENERAL DEPLOYMENT ASPECTS.** Deployment of the VOR/DME systems in accordance with the contract schedule requires that the first article system is to be shipped to the FAA Technical Center 22 months after contract award. Production delivery of six systems per month is scheduled to commence 26 months after contract award and to continue at that rate until all deliveries are complete. Delivery is specified to be F.O.B. destination to the site locations provided by the Government. Table 7-1 depicts the schedule for the DRR.

TABLE 7-1. DRR SCHEDULE

Initiate the DRR process	March 1991
Announce DRR Team Meeting	April 1991
Convene DRR Team Meeting	May 1991
Mid-Term Review	January 1992
Submit DRR Report	December 1992
DRR Excom Meeting	December 1992
-Deployment Decision	January 1993

**71 SITE PREPARATION.** The regional Airway Facilities divisions are responsible for required site preparation. Site preparation includes, but is not limited to, acquisition, by the regional Logistics division, by lease or purchase of the land required for the physical plant installation, providing appropriate commercial AC power, arranging for the lease of an acceptable four-wire telephone service from the VOR/DME site to the controlling AFSS, construction of the VOR/DME equipment shelter, and access road preparation.

**72. DELIVERY.** The first VOR/DME system is scheduled to be delivered to the test and evaluation site at the FAA Technical Center, Atlantic City, New Jersey, in August 1992 which is 22 months after the contract award. Production delivery is to commence 26 months after contract award at the rate of six systems per month and is to continue at that rate until all items on the contract have been delivered. The site delivery locations are as shown in appendix 1.

**73. INSTALLATION PLAN.** The installation and tune-up of the VOR/DME systems will be accomplished by the regions in accordance

with the installation section of the equipment instruction book. Standard ~~21X~~ 21" pre-cast concrete shelter with an independent 33 foot diameter counterpoise will be provided from a Washington office indefinite delivery/open ended requirements contract. The shelters will be set in place and the counterpoise will be erected by the shelter manufacturer on foundations provided by the Government. The standard drawings required for the shelter and counterpoise construction activities will be issued by ~~ANS-240.~~ Any questions on the shelter or counterpoise should be addressed to that office.

74.-79. RESERVED.

## CHAPTER 8. VERIFICATION

**80. FACTORY VERIFICATION.** The contractor will perform a series of ~~Government~~ approved tests in accordance with the requirements of the contract, the **VOR/DME** specification, **FAA-G-2100**, Electronic Equipment, General Requirements and other applicable documents prior to acceptance ~~of the~~ equipment by the **FAA**. The tests conducted will include design qualification, type, production, reliability, maintainability, and fail-safe tests that will demonstrate that all hardware, software, and all performance requirements are met **before** the FAA accepts a **VOR/DME** system from the contractor.

**81. CHECKOUT.** The first article **VOR/DME** system is to be shipped to ~~the~~ FAA Technical Center for installation and tune-up by the contractor in a Government furnished shelter using Government furnished **VOR** and **DME** antennas. This initial installation will be in a conventional **VOR** configuration. Following installation, tune-up and initial ground checks, the FAA will conduct a full commissioning type flight inspection. Of principal importance during the contractor conducted site acceptance testing is the interface of the **VOR/DME RMS** and the field support **MPS** at the FAA Technical Center and verification of the installation section of the equipment instruction book. During this testing, the **VOR/DME** system will be fully integrated with all internal and external interfaces including the remote status communication equipment (**RSCE**).

**82 CONTRACTOR INTEGRATION TESTING.** Following the checkout testing of paragraph **81**, the FAA integration testing of paragraph **84** and the shakedown testing of paragraph **85**, the contractor will convert the conventional **VOR** to the Doppler configuration and conduct checkout tests similar to those performed on the conventional system under paragraph **81**.

**83. CONTRACTOR ACCEPTANCE INSPECTION (CAI).** The requirements to be ~~satisfied~~ for final acceptance will be covered in the contractor prepared **MTP** and will be completed during the checkout and contractor integration testing of paragraphs **81** and **82**.

**84 FAA INTEGRATION TESTING.** The **ACN-210** Test Director will prepare test plans and procedures for the FAA integration testing, and evaluation (IT&E) to be completed at the FAA Technical Center. The IT&E will verify the technical performance of the **VOR/DME** system in a full field environment and with an operational **RSCE** and the field support **MPS** at the FAA Technical Center. At this time, the **IMCS** will have been baselined and will be resident on the FAA Technical Center **MPS**. The capability of the **VOR/DME** to properly interface with the **MPS** is critical to the

overall operation and maintenance of the systems in the **NAS**. The operation and maintenance of the **VOR/DME** system during the IT&E testing is the responsibility of the FAA.

**85. SHAKEDOWN AND CHANGEOVER.** The FAA Technical Center ST&E is the responsibility of **ASM-600** and will be conducted on the system installed at the FAA Technical Center. During system shakedown, tests are conducted to verify that the **VOR/DME** system, fully integrated in an operational environment, meets all operational requirements and is fully maintainable. System ST&E test activities will include accomplishment of the following:

a. Evaluation of the **RMS** diagnostic functions for effective system failure detection and acceptability of displayed operational data.

b. Verification of the instruction book procedures for routine and corrective maintenance.

c. Validation of the instruction book installation and tune-up procedures.

d. Verification of the system **RMS** functions from the remote **control** point using the maintenance data terminal (MDT) at the **MPS**.

**86 JOINT ACCEPTANCE INSPECTION (JAI).** A JAI will be completed prior to assumption of maintenance responsibility by the Airway Facilities Sector. The JAI, to be accomplished in accordance with Order **6030.45** will be completed following successful completion of the field shakedown test. The field shakedown test will be completed in accordance with the plans and procedures to be developed by **ASM-600**. The field shakedown test and the JAI, together, assure that the **VOR/DME** system complies with requirements in the following areas prior to final acceptance and commissioning.

a. Facility construction, equipment installation, and tune-up.

b. Facility/system/equipment performance including a successful flight inspection and reference ground check.

c. Facility technical performance documentation and maintenance reference data.

d. Facility logistics supports.

e. Facility/system training support.

4/25/91

6820.12

f. Availability of acceptable system/equipment instruction books.

87.-89. RESERVED.





## CHAPTER 9. INTEGRATED LOGISTICS SUPPORT

**90. MAINTENANCE CONCEPT.** The maintenance concept for the VOR/DME systems shall consist of both site and FAA Logistics Center repair. Maintenance technicians will replace failed LRU and, may perform limited corrective and preventative maintenance repair functions, as required, onsite. The maintenance technicians will replace the faulty LRU and send the repairable LRU to the FAA Logistics Center for exchange and repair (E&R). The FAA Logistics Center will either repair the defective LRU in-house or have it repaired under an equipment repair support contract.

**91. TRAINING.** The initial training for the VOR/DME systems will be conducted by the equipment contractor in accordance with the training program option in the contract which was exercised at the time of contract award. The training program requires that the contractor conduct five classes, two of which involve system repair to the component level with the balance (three) providing training for repair to the LRU level. Regional office personnel from the seven receiving-regions will be scheduled to attend the early LRU level classes together with technicians and engineers from the receiving sectors. An option for an additional five classes to be conducted by the contractor remains to be exercised, if required.

**92 SUPPORT TOOLS AND TEST EQUIPMENT.** The contractor shall identify all required special and common tools and test equipment including card extenders, jigs, fixtures, automated test equipment (ATE), and related software and material handling equipment required for performing preventative and corrective maintenance at any level. The contractor shall provide those items identified as unique to the VOR/DME system testing and repair requirements and the Government will provide the balance either onsite or at the work center or FAA Logistics Center, as appropriate.

**93 SUPPLY SUPPORT.** The FAA Logistics Center is responsible for providing supply support for the VOR/DME systems. The contractor will furnish spare parts peculiar, as identified during the provisioning process, to the FAA Logistics Center and will furnish site spare printed circuit boards and modules on the basis of one set of spares for each three systems under contract.

**94 VENDOR DATA AND TECHNICAL MANUALS.** Instruction books for the VOR/DME systems will be provided in accordance with Specification FAA-D-2494/b. The draft manuscript prepared by the contractor, is submitted to the FAA for review and approval. After FAA approval, the contractor submits a camera-ready copy to

the FAA for final printing of a quantity sufficient to provide two copies for each system plus a significant number for regional and Washington offices and for stock quantities at the **FAA** Logistics Center.

**95** **EQUIPMENT REMOVAL.** Any surplus material removed during the installation of the **VOR/DME** systems shall be disposed of in accordance with Order **4800.2A**, Utilization And Disposal Of Excess and Surplus Personal Property.

**96.** **FACILITIES.** Not applicable.

**97.099.** **RESERVED.**

4/25/91

6820.12

APPENDIX 1. VOR/DME  
DELIVERY LOCATIONS

Appendix 1

<u>REGION</u>	<u>LOCATION</u>	<u>STATE</u>	<u>IDENT</u>	<u>SCHEDULE</u>
1	AC Oklahoma City	OK	<del>AAC-440</del>	NOV 92
2	AC Oklahoma City	OK	<del>AAC-9940</del>	NOV 92
3	AC Oklahoma City	OK	<del>ASM-600</del>	NOV 92
4	SW <del>Bartlesville</del>	OK	BVO	NOV 92
5	NM Glen Elk (Denver)	co	TBD	NOV 92
6	NM Wiggins	co	TBD	NOV 92
7	AL Barter Island	AK	BTI	DEC 92
8	SW Columbus	NM	CUS	DEC 92
9	SW White Lake	LA	LLA	DEC 92
10	AL Point Heiden.	AK	PTH	DEC 92
11	GL <del>Kenosha</del>	WI	ENW	DEC 92
12	so Georgetown	BH	MYGG	DEC 92
13	GL Mount Pleasant	MI	MOP	JAN 93
14	WP Mammoth Lakes	CA	MMH	JAN 93
15	NM Badger Mountain	WA	WA1	JAN 93
16	SW Marvel	AR	AR1	JAN 93
17	so San Salvador	BH	MYSM	JAN 93
18	GL La Crosse	WI	LSE	JAN 93
19	WP Payson	AZ	AZ2	FEB 93
20	NM Chemult	OR	OR1	FEB 93
21	SW Ozona	TX	TX2	FEB 93
22	CE Ogallala	NE	OGA	FEB 93
23	GL Springfield	OH	SGH	FEB 93
24	NM Omak	WA	004	FEB 93
25	SW Uvalde	TX	TX1	MAR 93
26	CE Broken Bow	NE	CUZ	MAR 93
27	GL Burlington	WI	007	MAR 93
28	NM <del>Glendive</del>	MT	MT1	MAR 93
29	SW Cypress	LA	TBD	MAR 93
30	GL <del>Kankakee</del>	IL	IKK	MAR 93
31	SW Stamford	TX	TX3	APR 93
32	NM <del>Mg.</del> Reservoir ( <del>Hailey</del> )	ID	003	APR 93
33	SW cocos	LA	KA1	APR 93
34	so <del>Destin/Walton</del> ( <del>Eglin</del> )	FL	TBD	APR 93
35	NM Sand Springs	MT	MT2	APR 93
36	CE <del>Concordia</del>	KS	CJP	APR 93
37	GL <del>Racine</del>	WI	HRK	MAY 93
38	NM <del>Whidbey</del> Island	WA	NUW	MAY 93
39	NM Brigham City	UT	002	MAY 93
40	WP <del>Inyokern</del>	CA	IYK	MAY 93
41	GL <del>Baudette</del>	MN	BDE	MAY 93
42	CE Marshalltown	IA	MIW	MAY 93
43	GL <del>Ely</del>	MN	ELO	JUN 93
44	CE Gordon	NE	CQT	JUN 93
45	GL Gaylord	MI	GLR	JUN 93

APPENDIX 1. VOR/DME  
DELIVERY LOCATIONS

Appendix 1

<u>REGION</u>	<u>LOCATION</u>	<u>STATE</u>	<u>IDENT</u>	<u>SCHEDULE</u>
46 CE	Muscataine	IA	RTY	JUN 93
47 GL	Hillview	IL	IL4	SUN 93
48 GL	Manistiquie	MI	ISO	JUN 93
49 so	Great Inagua	BH	MYIG	JUL 93
50 CE	Braymer	MO	BQS	JUL 93
51 GL	Evansville	IL	51S	JUL 93
52 GL	Buffalo	SD	BUA	JUL 93
53 WP	Gila Bend	AZ	GBN	JUL 93
54 CE	West Plains	MO	HUW	JUL 93
55 SW	East Bernard	TX	001	AUG 93
56 so	Sinca	GA	TBD	AUG 93
57 GL	Roseau	MN	ROX	AUG 93
58 WP	Quail Mesa	AZ	2L3	AUG 93
59 CE	Thedford	NE	TDD	AUG 93
60 so	Shine	NC	xxx	AUG 93
61 WP	Prescott	AZ	PRC	SEP 93
62 CE	Orleans	NE	VOS	SEP 93
63 GL	Cleveland	OH	CLE	SEP 93
64 so	Selma	AL	CAQ	SEP 93
65 SW	Austin	TX	AUS1	SEP 93
66 SW	Austin	TX	AUS2	SEP 93
67 AC	FAA Logistics Center			OCT 93
68 AC	FAA Logistics Center			OCT 93
69 AC	FAA Logistics Center			OCT 93
70 AC	FAA Logistics Center			OCT 93



