


				2	201	8				2019						2020											2021													
	Project	JUL	AU	G SE	PC	OCT	NOV	DEC	JAN	I FE	вМ	AR A	PR N	MAY	JUN	JUL	AUG	SEI	00	TNO	OV [DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MA	R API	R MA	AY JUN
Α	TWY C																																							
В	TWY S																																							
С	TWY D (Center)																																							

	Project	Description of Work	Estimated Dates	Status	Impact	Notes
Α	TWY C	TWY C closed for construction between TWYs U and AA.	05/24/2018 to 07/17/2018	Complete		Expect increased airport surface congestion. GDP, GS, CFR, Metering, and MIT possible. Arrival and Departure delays may exceed 30 minutes during periods of peak demand.
В	TWY S	TWY S closed for construction, between TWY T1 and TWY T2.	06/06/2018 to 01/16/2020	In Progress		
С	TWY D (Center)	TWY D closed for construction, between TWY R and T.	09/17/2018 to Mar 2 019 TBD	In Progress		Limited impact for taxiing aircraft. Increased surface congestion during periods of peak demand.

IATA Level 2

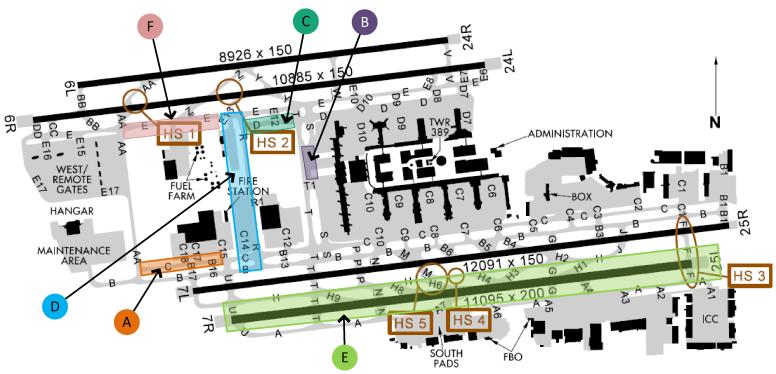

			20	18			2019						2020											2021								
	Project	JUL AU	G SEP	OCT	NOV DEC	JAN	FEB M	AR APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR [MAY	JUN J	UL AL	IG SEP	OCT	NOV	DEC	JAN	FEB	MAR AI	PR MA	Y JUN
D	TWY C14																															
E	RWY 7R/25L,TWY H																															
F	TWY D (West)																															

ľ		Project	Description of Work	Estimated Dates	Status	Impact	Notes
	D		New TWY C14 between TWY E and TWY C and parallel to TWY R.	January 2019 to March 2020	Upcoming		New taxiway construction. Capacity will be reduced with limited impact.
	Е	RWY 7R/25L,TWY H	Runway and taxiway closure for reconstruction.	01/15/2020 to 05/15/2020	Upcoming		Runway closure will occur in two phases.
	F		New TWY D, closed area for surface construction from TWY C14 to TWY AA.	Winter 2021 to Winter 2022	Upcoming		New taxiway construction. Capacity will be reduced with limited impact. Expected start date: Q1-2021.
