

Flight Procedures Cover Page	Task Action: FLIGHT CHECK	Task Type: Textual DP	Estimated Chart Date: 09/05/2024	APWS Task ID: 107A53199D374363B415084DCCC66029	APWS Project ID: EED7133EEAE049D796909AFE753EA525
Procedure: TAKEOFF MINIMUMS AND OBSTACLE DP AMDT 3A		Enroute: NO	Specialist: Mendenhall, Christopher		Agreement Number:
Airport ID: KJER			Airport City: JEROME		State: ID
Facility ID:	Facility Type:	Flight Inspection Remark Type: New FC Slot			
Procedure Comments: ACTIVE DATA USED FOR KJER ADJUSTED RWY 09 TAKEOFF MINIMUMS CLEAR NOTAM FDC 4/3407 CONTACT: DAVE DANNER 405-954-5077 05/23/24: THIS IS AN UPDATED COPY OF THE FORM DEVELOPED ON 04/03/24. 1. TEXTUAL DEPARTURE PROCEDURE RWY 9 CHANGED FROM CLIMB HEADING 086.07 TO 5300 BEFORE PROCEEDING ON COURSE TO CLIMBING RIGHT TURN HEADING 110.07, CLIMBING TO 5000 BEFORE PROCEEDING ON COURSE - PER FLIGHT INSEPCTION. QUALITY 23 CHECKED					

FIPC BASIC FORM									
PROCEDURE: TAKEOFF MINIMUMS AND OBSTACLE DP AMDT 3A				AIRPORT NAME: JEROME COUNTY		AIRPORT ID: KJER		SPECIAL CONTROL NO: SP-05-198-24	
FAC ID: KJER			CITY: JEROME			ST: ID		ORIG CHART DATE: 09/05/2024	
DFL TYPE: PROC/T	THIRD PARTY: ☐ YES	EST. TIME ON SITE: 0.4	REIMB. NUMBER:		PTS TASK ID: 107A53199D374363B415084DCCCC66029				
PREFLIGHT NOTES									
REVIEWER: troy e devine						DATE: 07/12/2024			
COMMENTS:						CHECK ONE: ☒ FLT CK REQ ☐ NFCR ☐ REJECT			
								YES	NO
						CPV COMPLETE?		X	
PROCEDURE RESULTS									
INSPECTION DATE: 07/12/2024		CREW #: VN502	N #: N72	INSTRUMENT PROCEDURE STATUS: ☒ SAT ☐ SAT W/CHANGES ☐ UNSAT			ARINC CODING: ☐ SAT ☐ SAT/GOLD ☐ UNSAT		
FLIGHT INSPECTOR SIGNATURE: troy e devine @ 07/12/2024 16:42			PRINTED NAME: DEVINE, TROY ELLEN				NOTAM INITIATED? ☐ YES ☒ NO		
FLIGHT INSPECTOR REMARKS: SP-05-198-24, JEROME COUNTY (JER) JEROME, ID, Amdt 3A ODP, CLIMBING RT TURN TO 110* ADDED, FLOWN SAT.									
IN-FLIGHT OBSTACLE REPORT									
OBSTRUCTION ID #:	COORDINATES OR LOCATION:		GNSS ALTITUDE (MSL):		BAROMETRIC ALTITUDE (MSL):		HEIGHT ABOVE GROUND LEVEL:		



23334

OLD

L30

OLD



TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)

IDAHO FALLS, ID

IDAHO FALLS RGNL (IDA)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

AMDT 5 03JAN19 (19003) (FAA)

TAKEOFF MINIMUMS:

Rwy 17, NA - Environmental.

DEPARTURE PROCEDURE:

Rwys 3, 35, all aircraft departing 210° CW 040° climb on course, all others climbing left turn direct IDA VOR/DME thence...**Rwy 21**, all aircraft departing 210° CW 020° climb on course, all others climbing right turn direct IDA VOR/DME thence...

...Continue climb in IDA VOR/DME holding pattern (hold south, left turn, 019° inbound) to cross IDA VOR/DME at or above MEA for route of flight.

TAKEOFF OBSTACLE NOTES:

Rwy 3, pole 1039' from DER, 758' left of centerline, 42' AGL/4762' MSL.**Rwy 35**, vehicle on traverse way 410' from DER, 581' right of centerline, 4742' MSL.

Trees beginning 882' from DER, 503' right of centerline, up to 48' AGL/4769' MSL.

Pole 1034' from DER, 715' left of centerline, 37' AGL/4762' MSL.

JACKSON, WY

JACKSON HOLE (JAC)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

AMDT 6 10JUN04 (04162) (FAA)

DEPARTURE PROCEDURE:

Rwy 1, use GEYSER DEPARTURE.**Rwy 19**, use TETON DEPARTURE.

JEROME, ID

JEROME COUNTY (JER)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

AMDT 3 30JAN20 (20030) (FAA)

TAKEOFF MINIMUMS:

Rwy 9, 500-1% or std. w/min. climb of 450' per NM to 4700.

DEPARTURE PROCEDURE:

Rwy 9, climb heading 086° to 5300 before proceeding on course.**Rwy 27**, climb heading 266° to 4800 before proceeding on course.

TAKEOFF OBSTACLE NOTES:

Rwy 9, vegetation 140' from DER, 500' left of centerline, 10' AGL/4076' MSL.

Transmission line 600' from DER, 425' right of centerline, 33' AGL/4085' MSL.

Poles beginning 1052' from DER, 338' right of centerline, up to 35' AGL/4088' MSL.

Pole 1260' from DER, 298' right of centerline, 34' AGL/4090' MSL.

Pole 1432' from DER, 364' left of centerline, 33' AGL/4106' MSL.

Sign 1473' from DER, 548' left of centerline, 40' AGL/4119' MSL.

Tree and pole beginning 1651' from DER, 612' left of centerline, up to 39' AGL/4125' MSL.

Tree and building beginning 2084' from DER, 174' left of centerline, up to 41' AGL/4133' MSL.

Tree 2442' from DER, 101' left of centerline, 44' AGL/4137' MSL.

Pole 3699' from DER, 622' left of centerline, 37' AGL/4167' MSL.

Pole 3804' from DER, 33' left of centerline, 33' AGL/4169' MSL.

Pole 3858' from DER, 253' right of centerline, 37' AGL/4173' MSL.

Irrigation system 4752' from DER, 518' left of centerline, 12' AGL/4175' MSL.

Trees beginning 1 NM from DER, 2159' left of centerline, up to 50' AGL/4257' MSL.

Tree 1.1 NM from DER, 2277' left of centerline, 50' AGL/4260' MSL.

Tree 1.1 NM from DER, 2316' left of centerline, 50' AGL/4263' MSL.

Tree 1.2 NM from DER, 2356' left of centerline, 50' AGL/4266' MSL.

Tree 1.2 NM from DER, 2395' left of centerline, 50' AGL/4273' MSL.

Tree 1.2 NM from DER, 2434' left of centerline, 50' AGL/4279' MSL.

Tree 1.3 NM from DER, 2474' left of centerline, 50' AGL/4286' MSL.

Tree 1.3 NM from DER, 2513' left of centerline, 50' AGL/4299' MSL.

Trees beginning 1.3 NM from DER, 2253' left of centerline, up to 50' AGL/4306' MSL.

Tower and trees beginning 1.4 NM from DER, 2292' left of centerline, up to 250' AGL/4533' MSL.

Tree 1.4 NM from DER, 2670' left of centerline, 50' AGL/4283' MSL.

Rwy 27, fence beginning abeam DER, 440' left of centerline, up to 4' AGL/3969' MSL.

23334

TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)





NW-1


L30

30 NOV 2023 to 28 DEC 2023

30 NOV 2023 to 28 DEC 2023

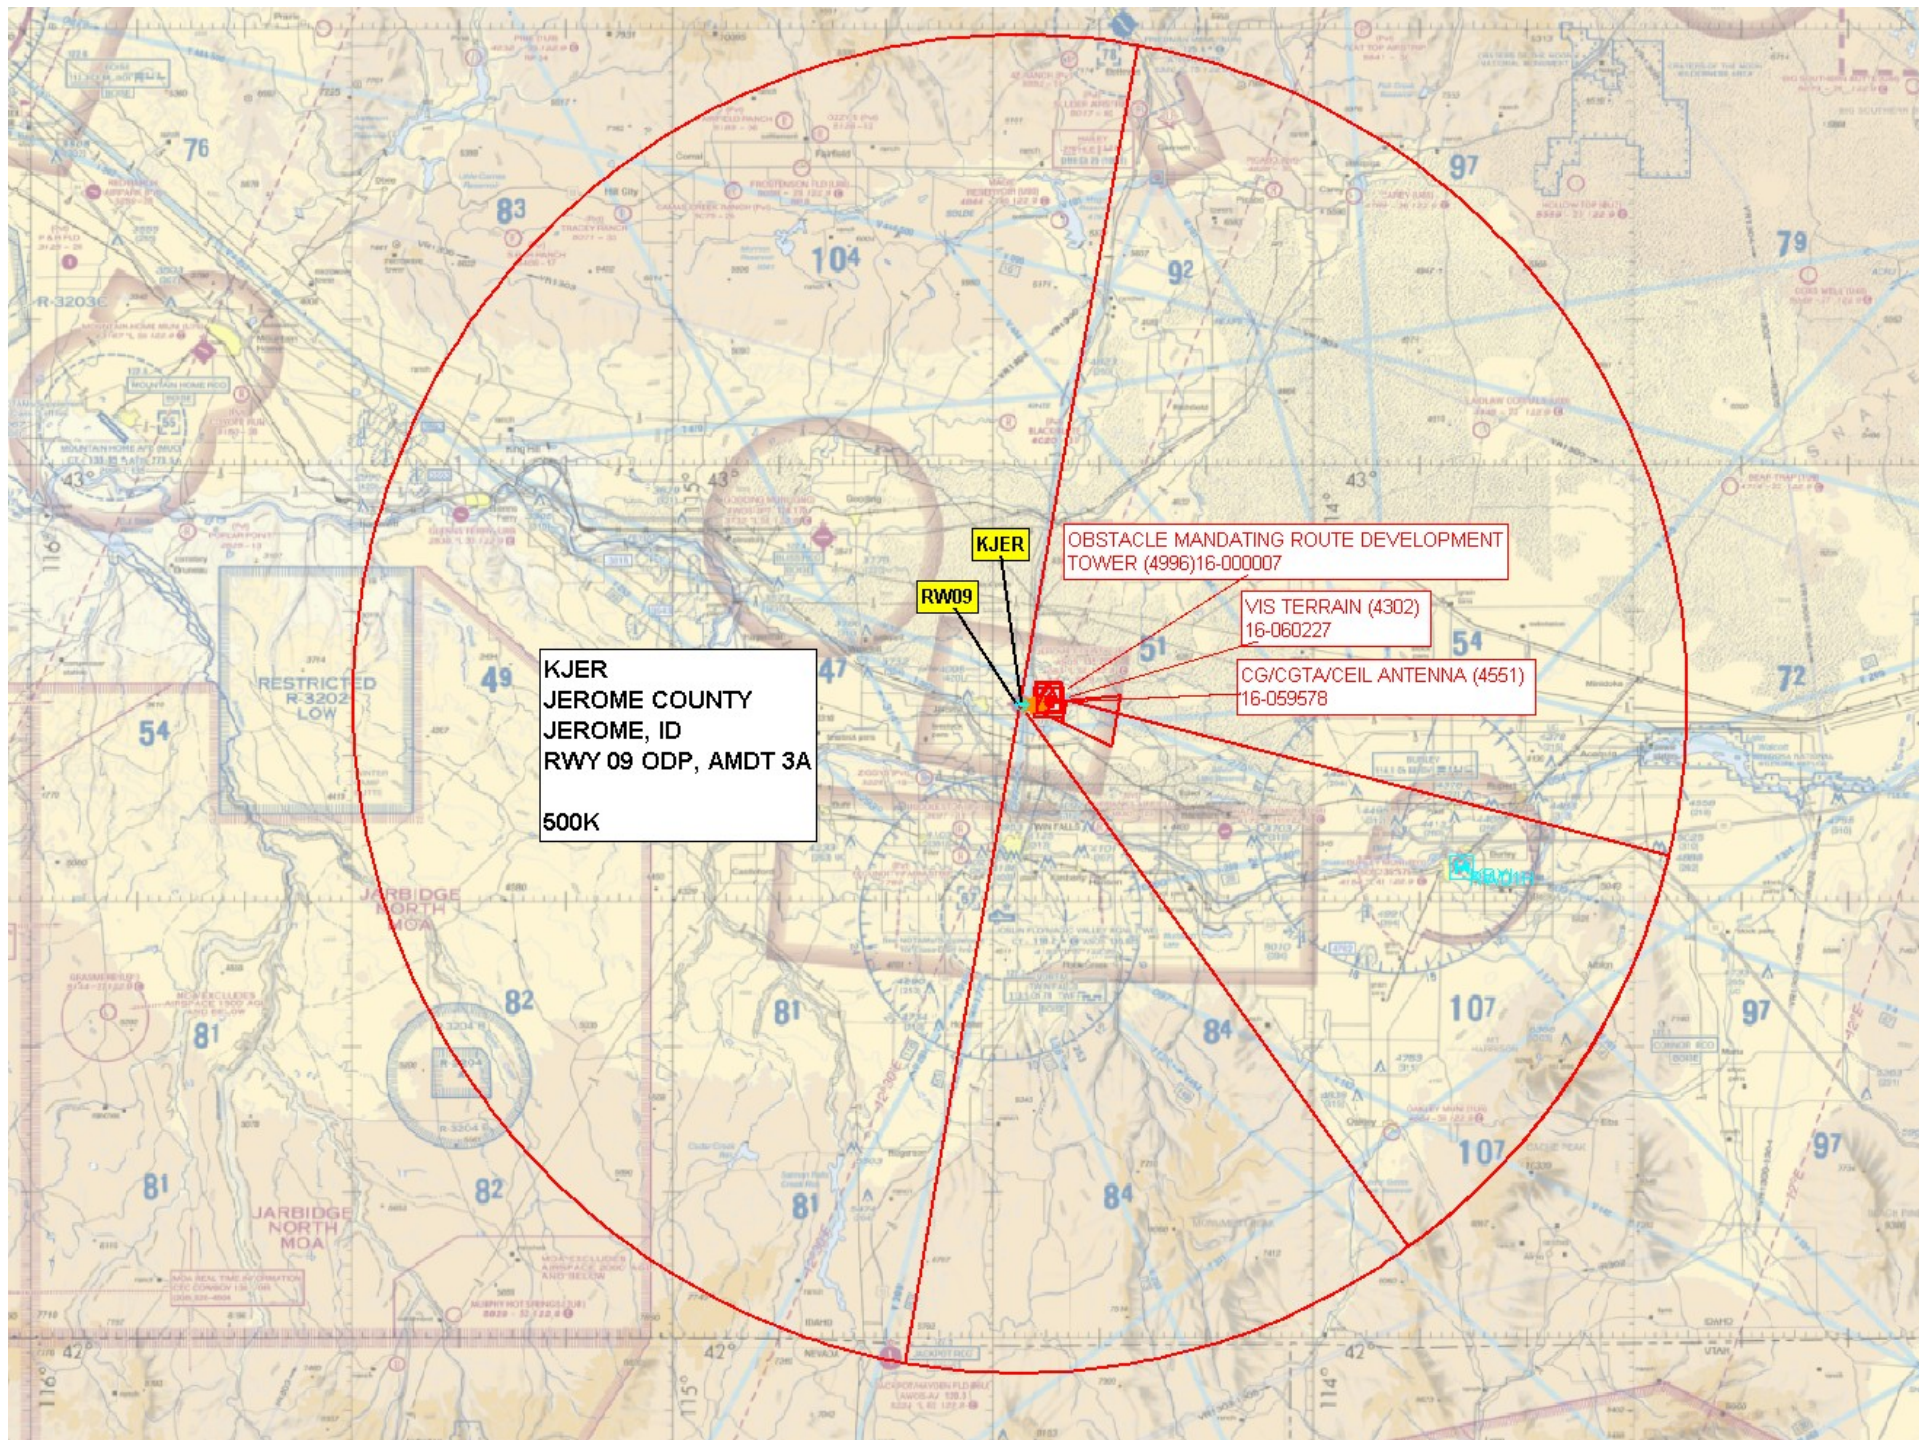

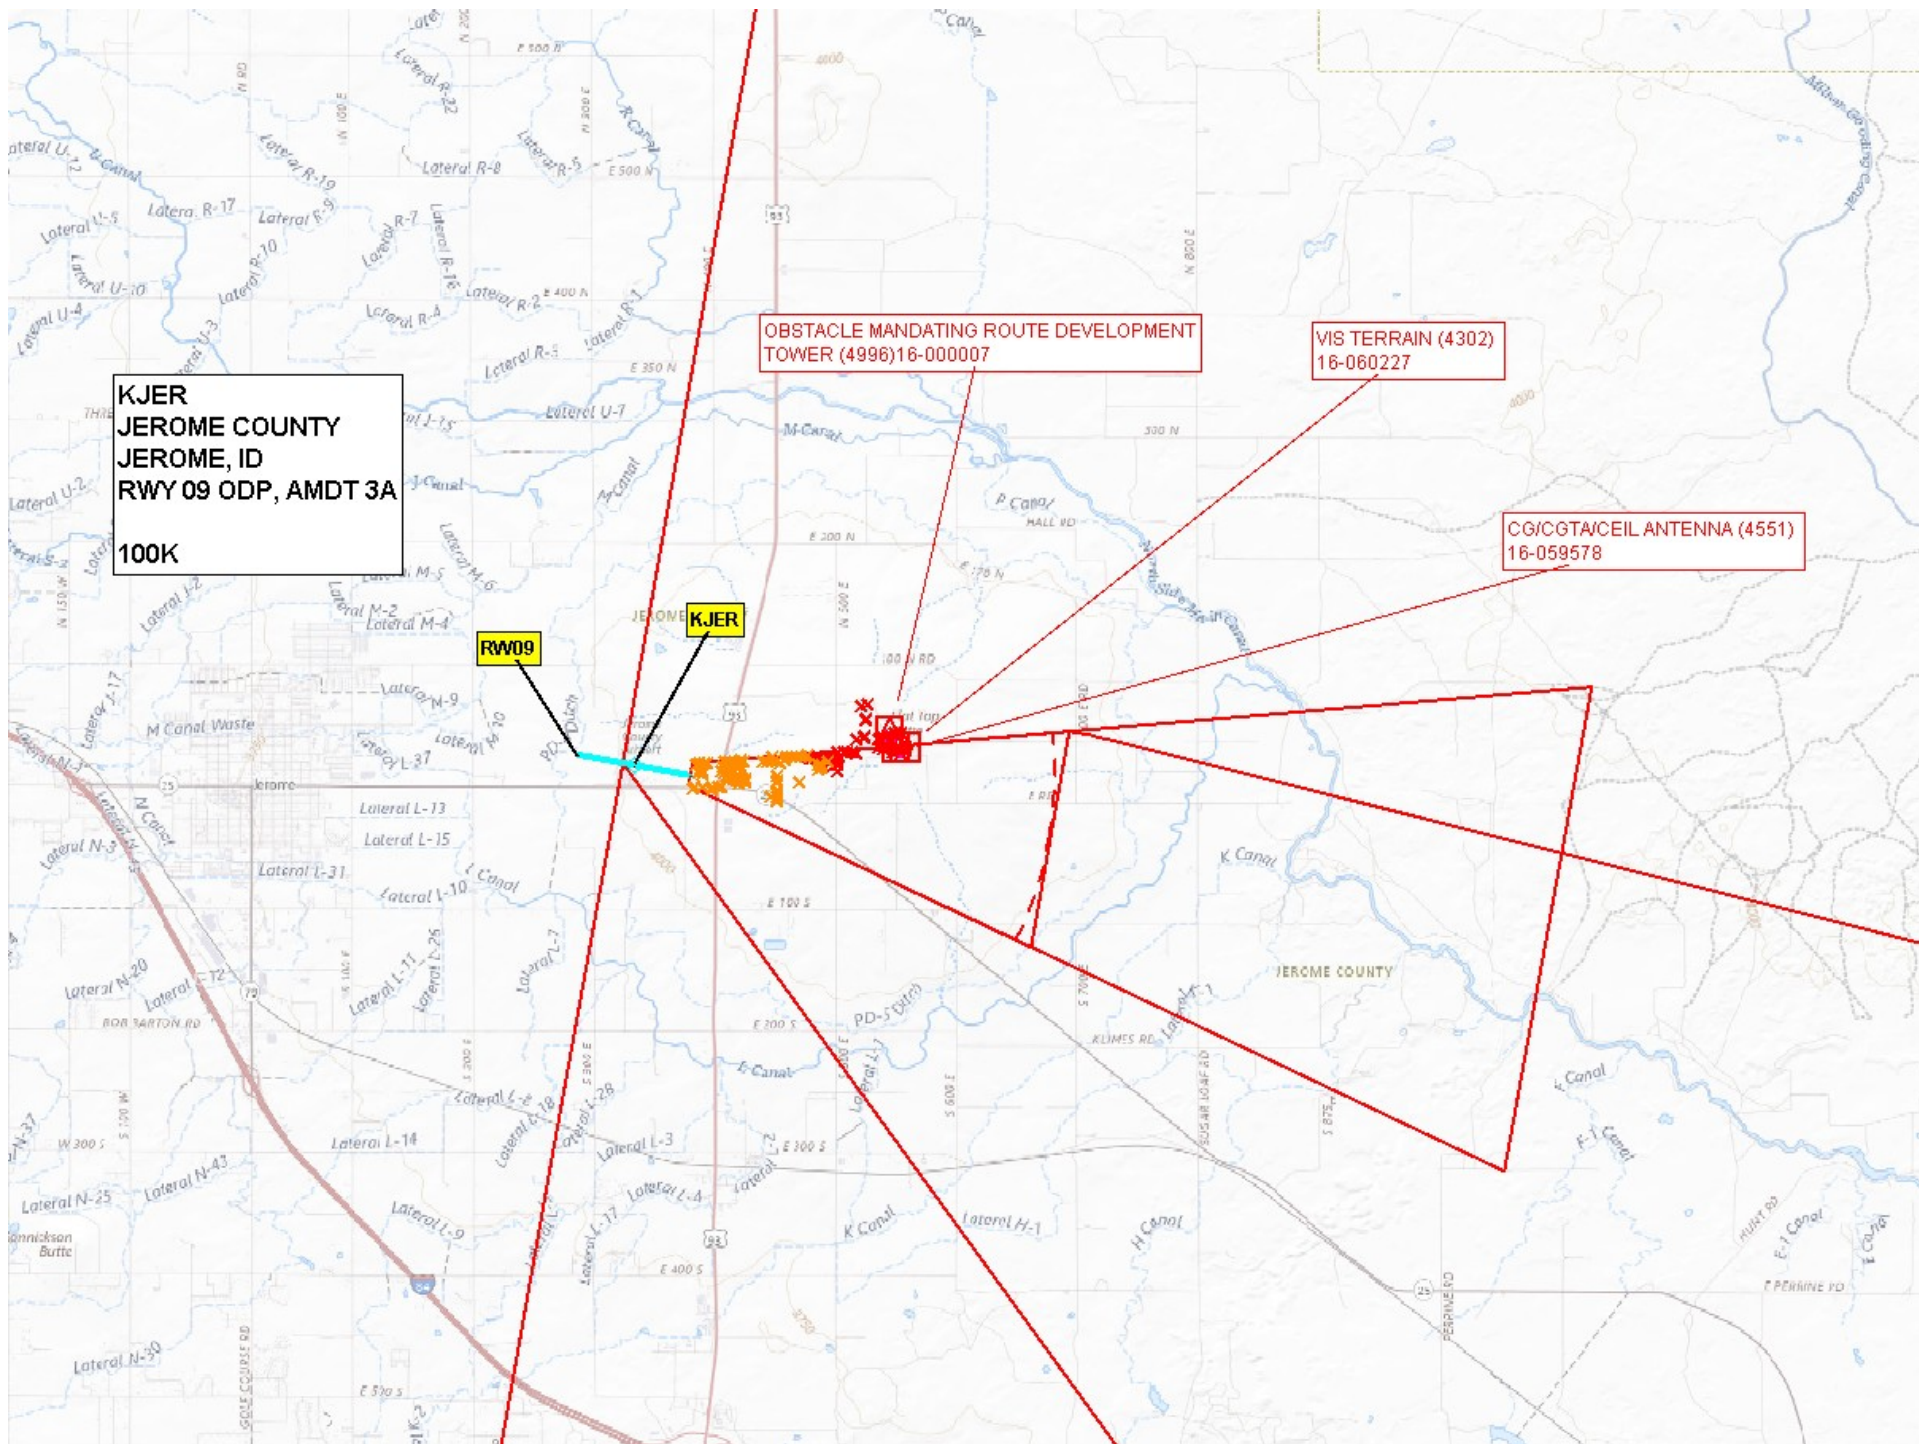

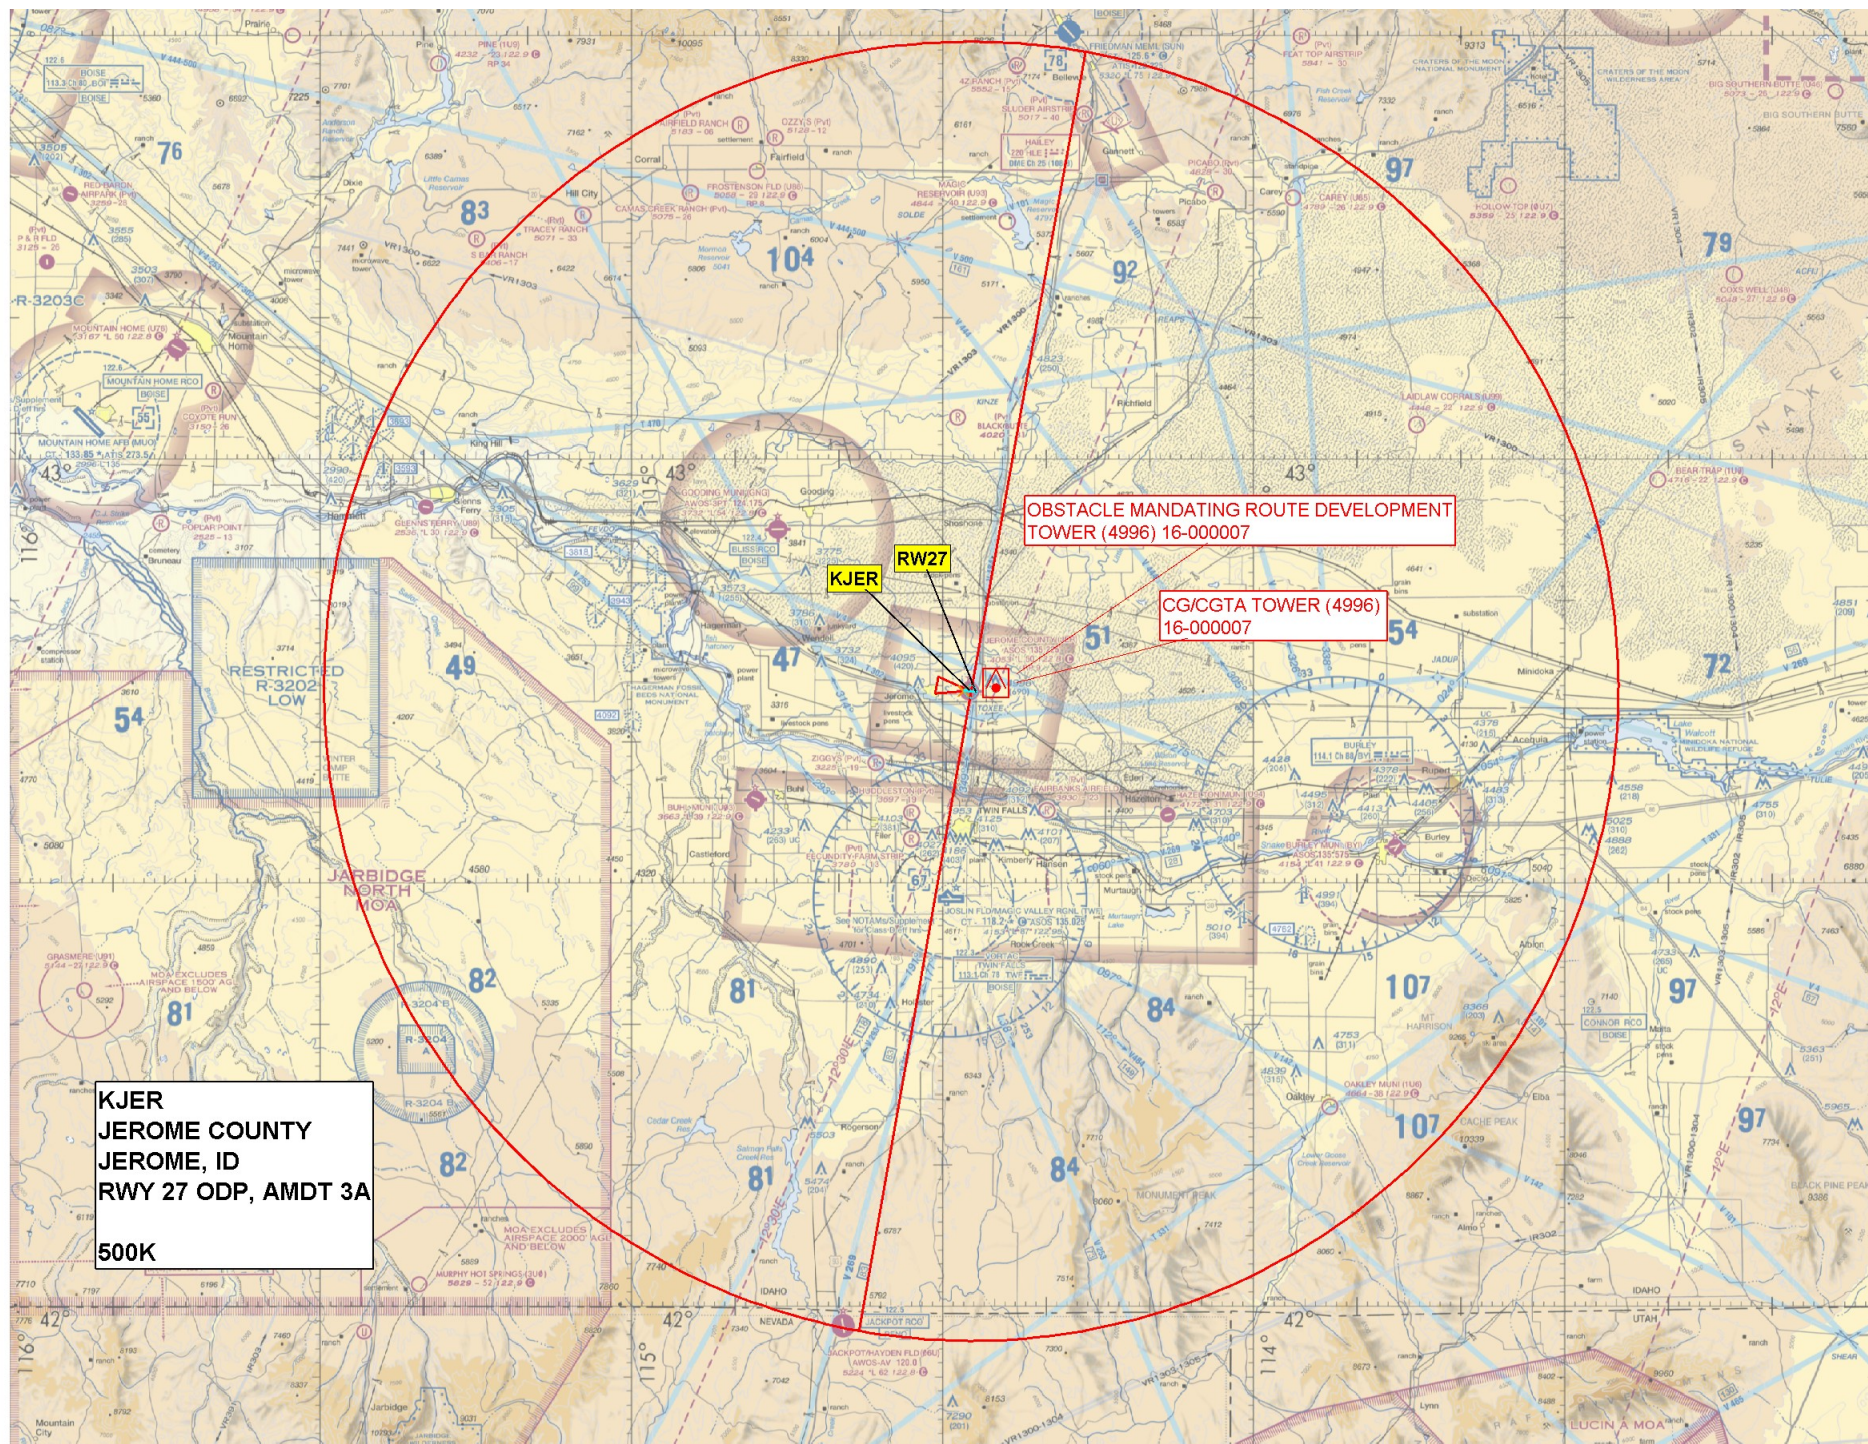

KJER
JEROME COUNTY
JEROME, ID
RWY 27 ODP, AMDT 3A
500K

OBSTACLE MANDATING ROUTE DEVELOPMENT
TOWER (4996) 16-000007

CG/CGTA TOWER (4996)
16-000007

KJER
JEROME COUNTY
JEROME, ID
RWY 27 ODP, AMDT 3A

100K

OBSTACLE MANDATING ROUTE DEVELOPMENT
TOWER (4996) 16-000007

CG/CGTA TOWER (4996)
16-000007

KJER

RW27

93

25

JE

