

Flight Procedures Cover Page	Task Action: FLIGHT CHECK	Task Type: Textual DP	Estimated Chart Date: 06/12/2025	APWS Task ID: 17C3DF64C1BE481F82FBFEDEBACA8232	APWS Project ID: AA692F4383FA45CC9C5D100CB12DEB7C
Procedure: TAKEOFF MINIMUMS AND OBSTACLE DP AMDT 2B		Enroute: NO	Specialist: Feronti, Tia		Agreement Number:
Airport ID: KIMM			Airport City: IMMOKALEE		State: FL
Facility ID:	Facility Type:	Flight Inspection Remark Type: New FC Slot			
Procedure Comments: CLEARS NOTAM 3/0365. UPDATED TAKEOFF OBSTACLE NOTES. CONTACT DAVID DANNER, AJV-A421, 405-954-5077. QUALITY 21 CHECKED					

FIPC BASIC FORM						
PROCEDURE: TAKEOFF MINIMUMS AND OBSTACLE DP AMDT 2B			AIRPORT NAME: IMMOKALEE RGNL		AIRPORT ID: KIMM	SPECIAL CONTROL NO: AP-03-097-25
FAC ID: KIMM		CITY: IMMOKALEE			ST: FL	ORIG CHART DATE: 06/12/2025
DFL TYPE: PROC/T	THIRD PARTY: ☐ YES	EST. TIME ON SITE: 0.4	REIMB. NUMBER:	PTS TASK ID: 17C3DF64C1BE481F82FBFEDEBACA8232		
PREFLIGHT NOTES						
REVIEWER:					DATE:	
COMMENTS:					CHECK ONE: ☐ FLT CK REQ ☐ NFCR ☐ REJECT	
						YES NO
					CPV COMPLETE?	X
PROCEDURE RESULTS						
INSPECTION DATE: 04/10/2025	CREW #: VN426	N #: N69	INSTRUMENT PROCEDURE STATUS: ☒ SAT ☐ SAT W/CHANGES ☐ UNSAT		ARINC CODING: ☐ SAT ☐ SAT/GOLD ☐ UNSAT	
FLIGHT INSPECTOR SIGNATURE: robert e williams @ 04/10/2025 20:14			PRINTED NAME: WILLIAMS, ROBERT EMIL			NOTAM INITIATED? ☐ YES ☒ NO
FLIGHT INSPECTOR REMARKS: Immokalee RGNL, Immokalee, FL, ODP, Amdt 2B. SAT						
IN-FLIGHT OBSTACLE REPORT						
OBSTRUCTION ID #:	COORDINATES OR LOCATION:	GNSS ALTITUDE (MSL):	BAROMETRIC ALTITUDE (MSL):	HEIGHT ABOVE GROUND LEVEL:		

TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)

24361

IMMOKALEE, FL

IMMOKALEE RGNL (IMM)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES
AMDT 2A 13SEP18 (18256) (FAA)

TAKEOFF MINIMUMS:

Rwy 18, 300-2¼ or std. w/min. climb of 230' per NM to 420, or alternatively, with std. takeoff minimums and a normal 200' per NM climb gradient, takeoff must occur no later than 2200' prior to DER.

TAKEOFF OBSTACLE NOTES:

Rwy 9, tree 58' from DER, 445' left of centerline, 46' MSL.

Trees beginning 166' from DER, 408' left of centerline, up to 47' MSL.

Tree 1129' from DER, 299' left of centerline, 37' AGL/67' MSL.

Rwy 18, apt sign, REIL beginning 27' from DER, 116' left of centerline, up to 2' AGL/34' MSL.

REIL 38' from DER, 115' right of centerline, 1' AGL/34' MSL.

Buildings beginning 253' from DER, 475' left of centerline, up to 51' MSL.

Tree 1180' from DER, 767' left of centerline, 63' MSL.

Tree 1242' from DER, 620' left of centerline, 66' MSL.

Tree 1309' from DER, 814' left of centerline, 69' MSL.

Tower 1.7 NM from DER, 2983' right of centerline, 297' AGL/322' MSL.

Communication twr 1.7 NM from DER, 2996' right of centerline, 285' AGL/311' MSL.

Rwy 27, fence 4' from DER, 472' right of centerline, 7' AGL/41' MSL.

Apt sign 33' from DER, 467' left of centerline, 3' AGL/38' MSL.

Tree 231' from DER, 486' right of centerline, 60' MSL.

Tree 308' from DER, 425' right of centerline, 61' MSL.

Trees beginning 393' from DER, 340' right of centerline, up to 63' MSL.

Trees beginning 505' from DER, 286' right of centerline, up to 30' AGL/68' MSL.

Tree 719' from DER, 624' left of centerline, 45' AGL/80' MSL.

Tree 769' from DER, 527' left of centerline, 81' MSL.

Tree, pole beginning 870' from DER, 258' left of centerline, up to 54' AGL/89' MSL.

Tree 967' from DER, 363' right of centerline, 33' AGL/70' MSL.

Pole 1029' from DER, 670' right of centerline, 71' MSL.

Tree, pole beginning 1053' from DER, 49' right of centerline, up to 45' AGL/76' MSL.

Rwy 36, trees beginning 265' from DER, 383' left of centerline, up to 63' MSL.

Trees beginning 355' from DER, 306' left of centerline, up to 30' AGL/68' MSL.

Tree 400' from DER, 232' right of centerline, 16' AGL/51' MSL.

Trees beginning 446' from DER, 209' right of centerline, up to 18' AGL/53' MSL.

INVERNESS, FL

INVERNESS (INF)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES
ORIG 05APR12 (12096) (FAA)

TAKEOFF MINIMUMS:

Rwy 1, 300-1½ or std. w/min. climb of 420' per NM to 500.

TAKEOFF OBSTACLE NOTES:

Rwy 1, terrain beginning 110' from DER, 27' left of centerline, up to 49' MSL.

Terrain beginning 137' from DER, 238' right of centerline, up to 49' MSL.

Trees beginning 110' from DER, 293' left of centerline, up to 100' AGL/149' MSL.

Vehicles on roadway 598' from DER, across centerline, up to 15' AGL/65' MSL.

Trees beginning 785' from DER, on centerline, up to 100' AGL/149' MSL.

Tower 5479' from DER, 1312' left of centerline, up to 220' AGL/279' MSL.

Tower 5764' from DER, 1596' left of centerline, up to 164' AGL/250' MSL.

Trees beginning 164' from DER, 238' right of centerline, up to 100' AGL/149' MSL.

Rwy 19, trees beginning 340' from DER, 239' left of centerline, up to 100' AGL/169' MSL.

Trees beginning 793' from DER, 596' right of centerline, up to 100' AGL/189' MSL.

Trees beginning 2066' from DER, on centerline, up to 100' AGL/209' MSL.

Trees beginning 2523' from DER, 274' right of centerline, up to 100' AGL/209' MSL.

TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)


24361

SE-3


23 JAN 2025 to 20 FEB 2025

23 JAN 2025 to 20 FEB 2025


KIMM
IMMOKALEE RGNL
IMMOKALEE, FL
ODP
AMDT 2A
1:100,000
RWY 09

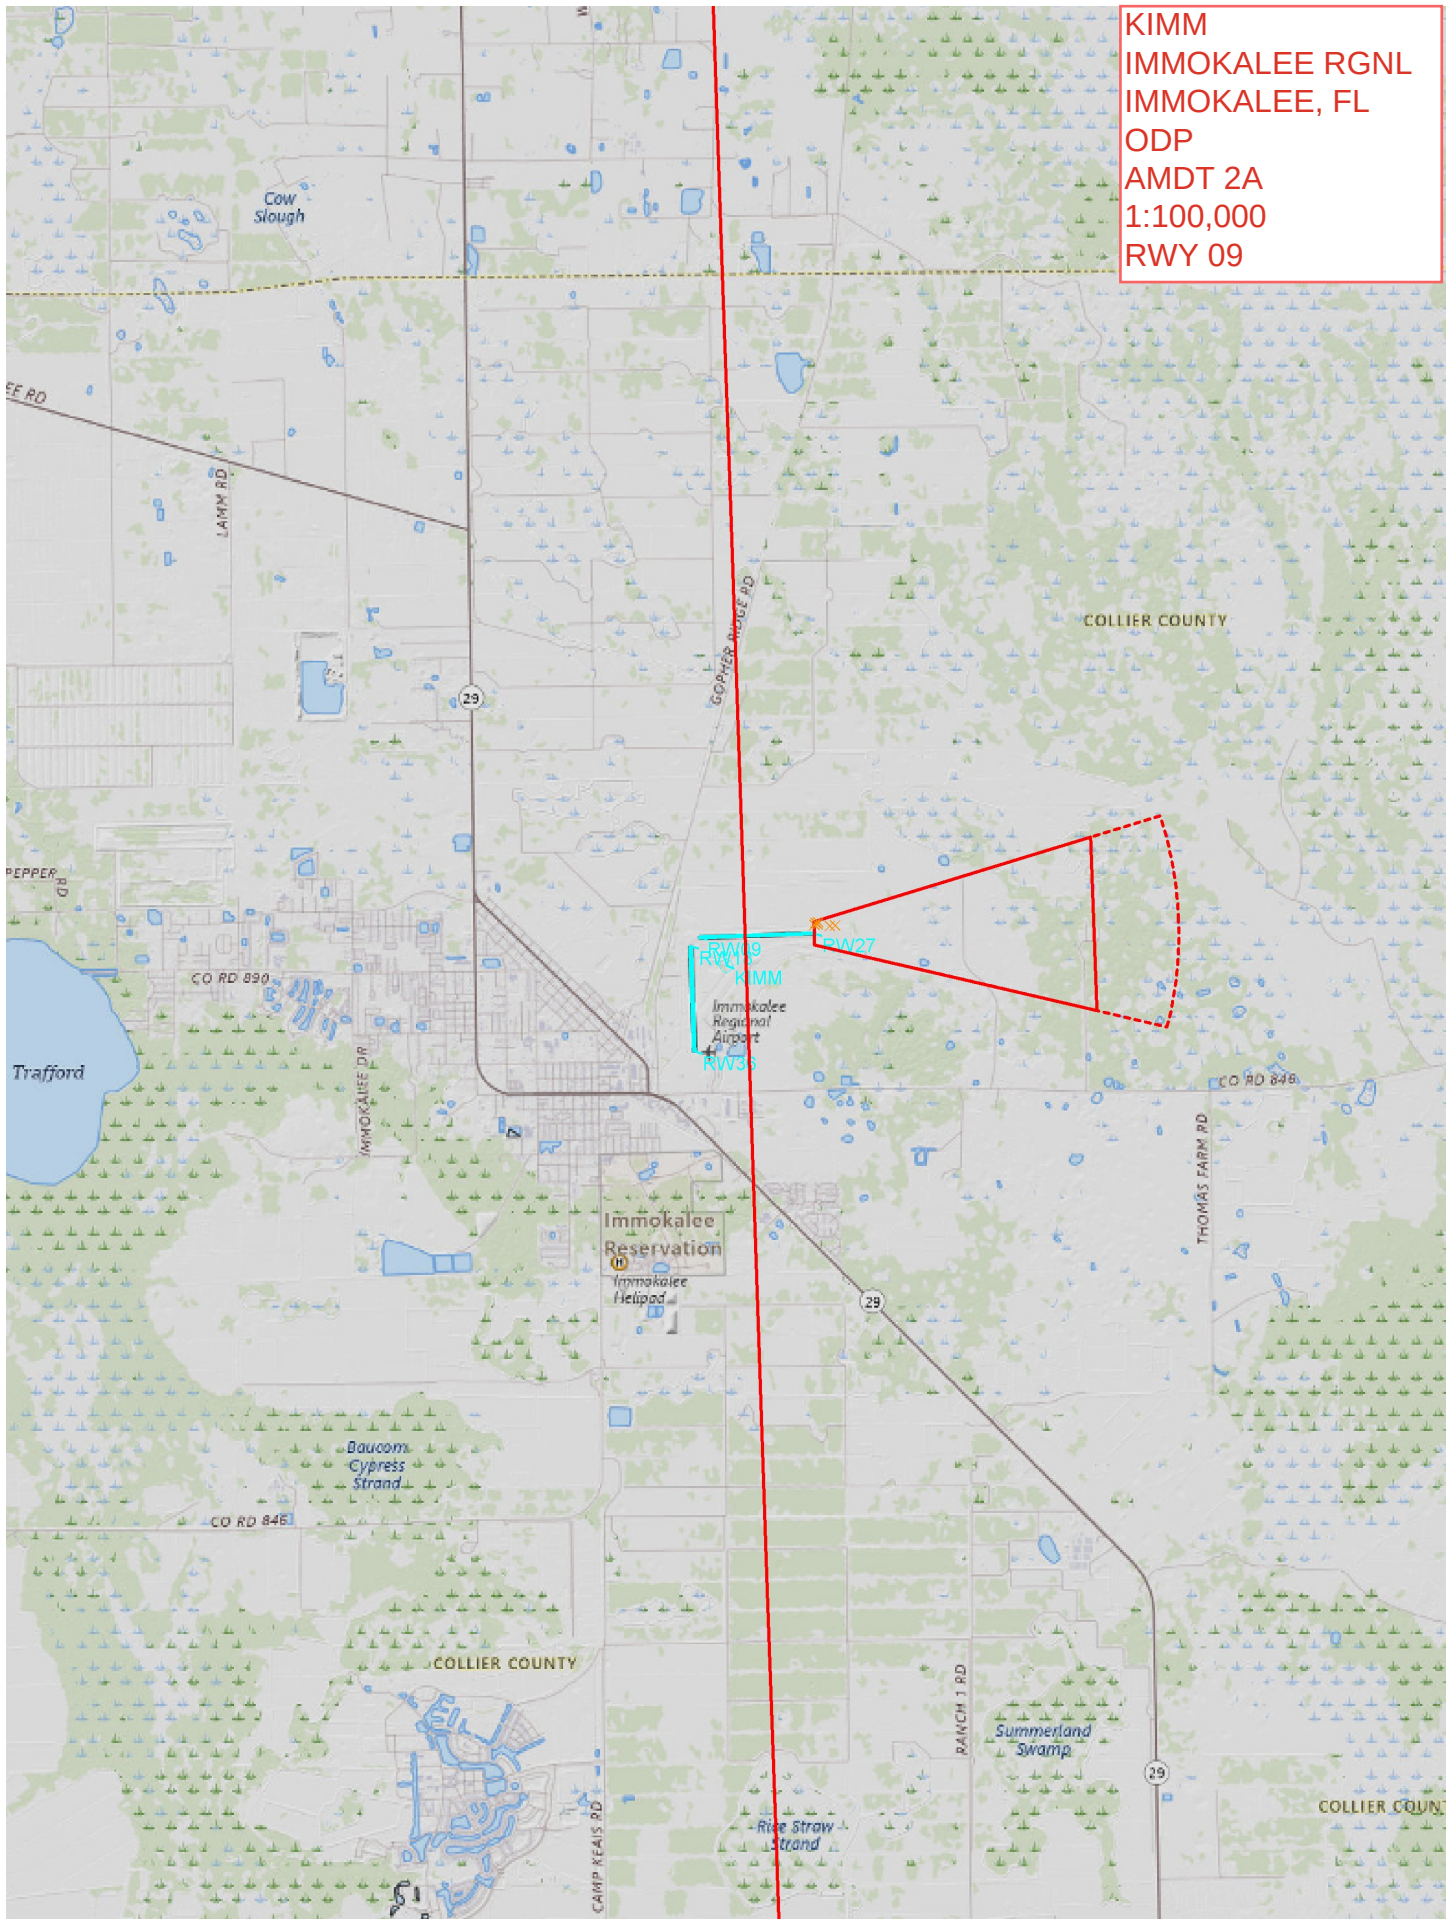

KIMM
IMMOKALEE RGNL
IMMOKALEE, FL
ODP
AMDT 2A
1:100,000
RWY 18

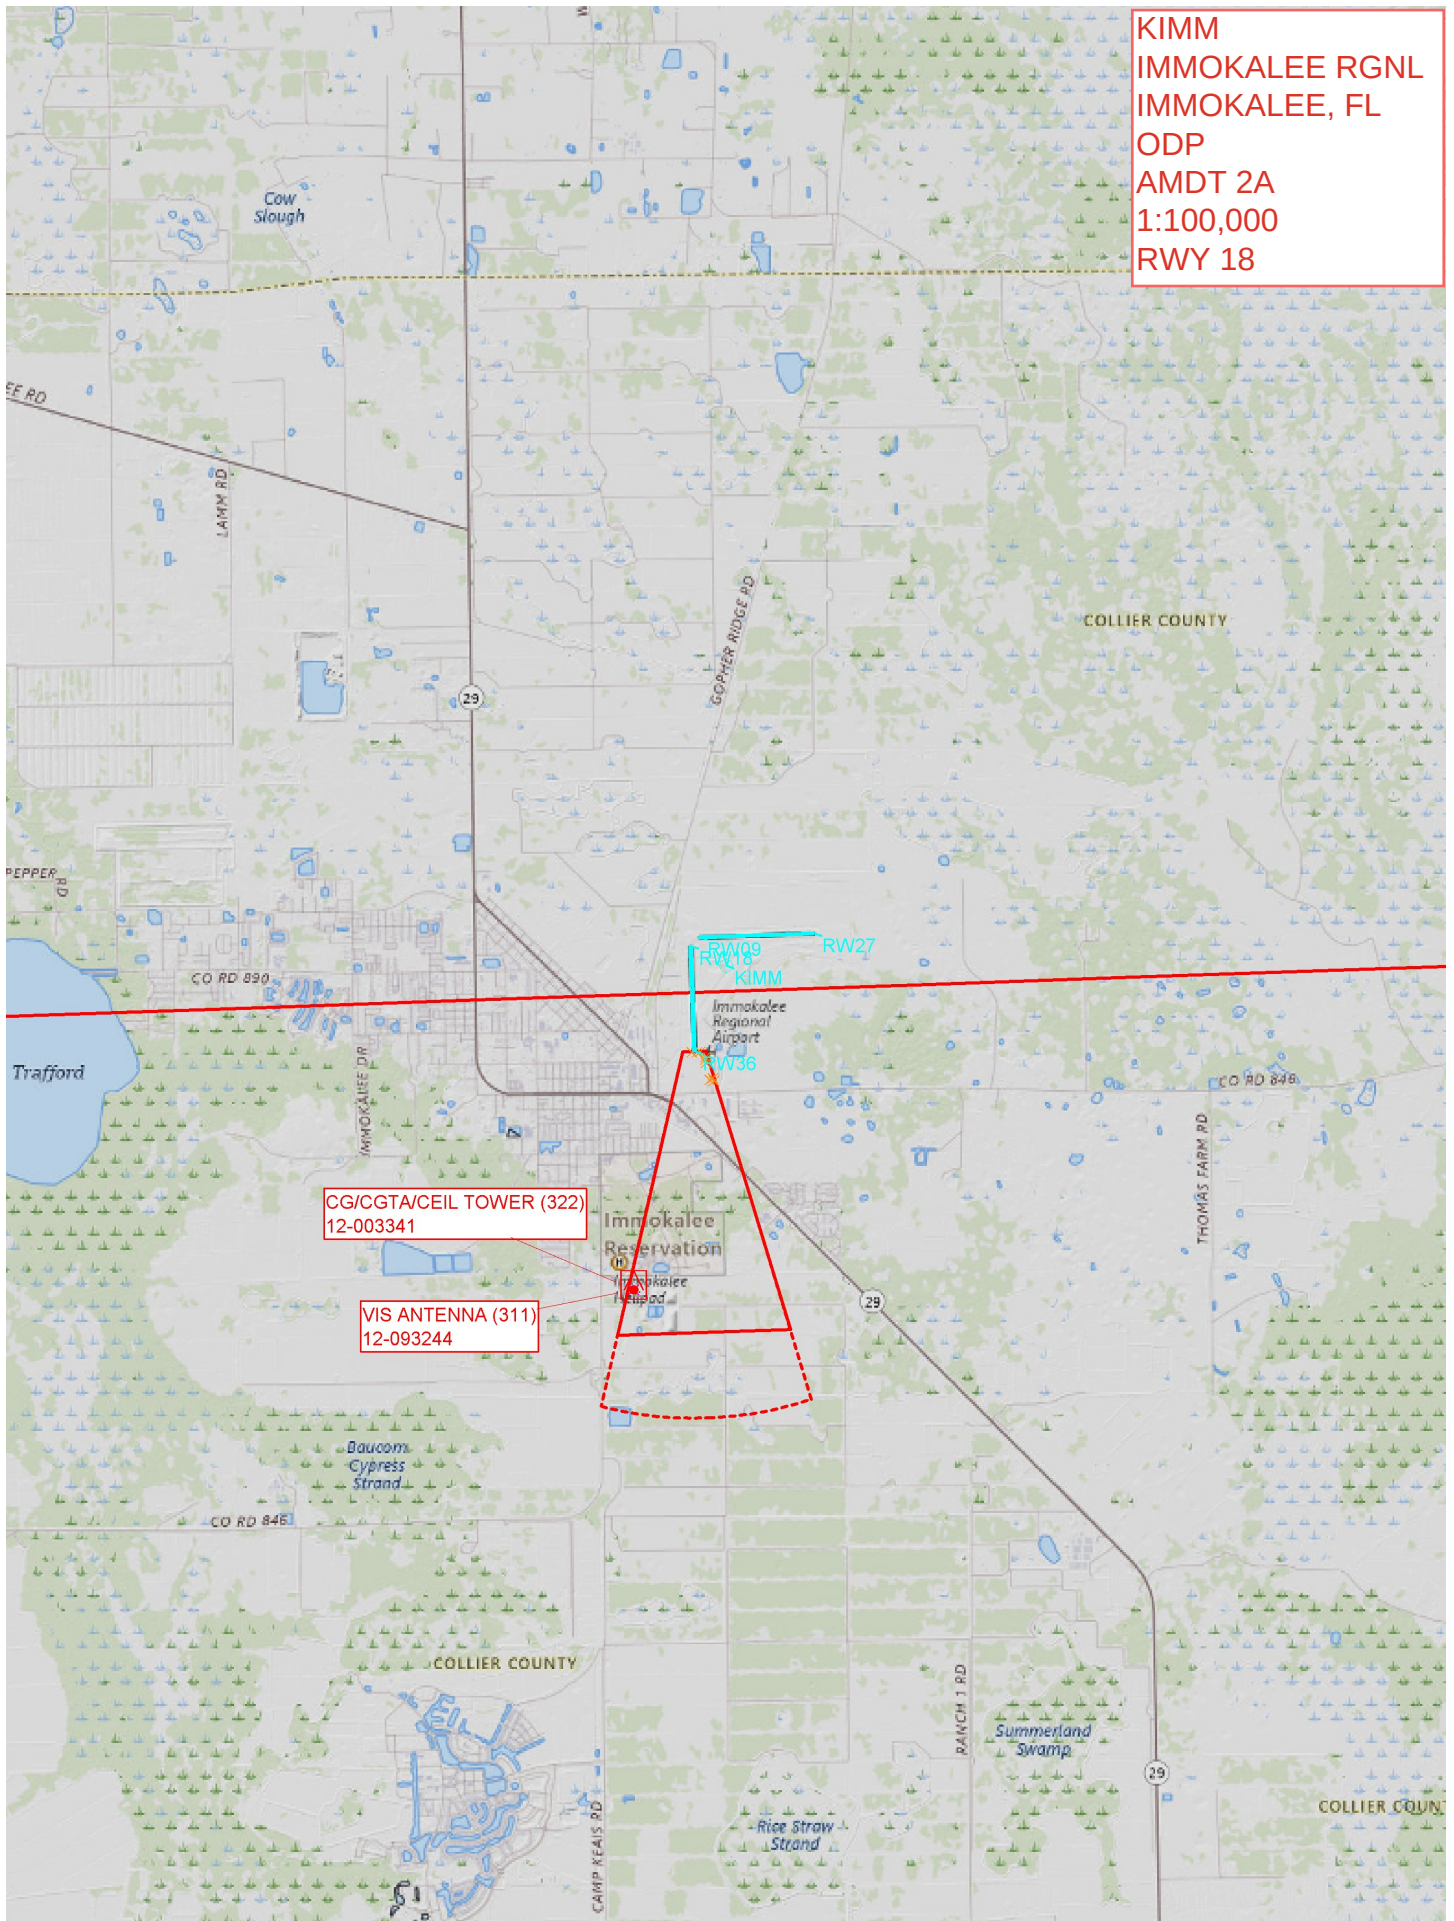

KIMM
IMMOKALEE RGNL
IMMOKALEE, FL
ODP
AMDT 2A
1:100,000
RWY 27

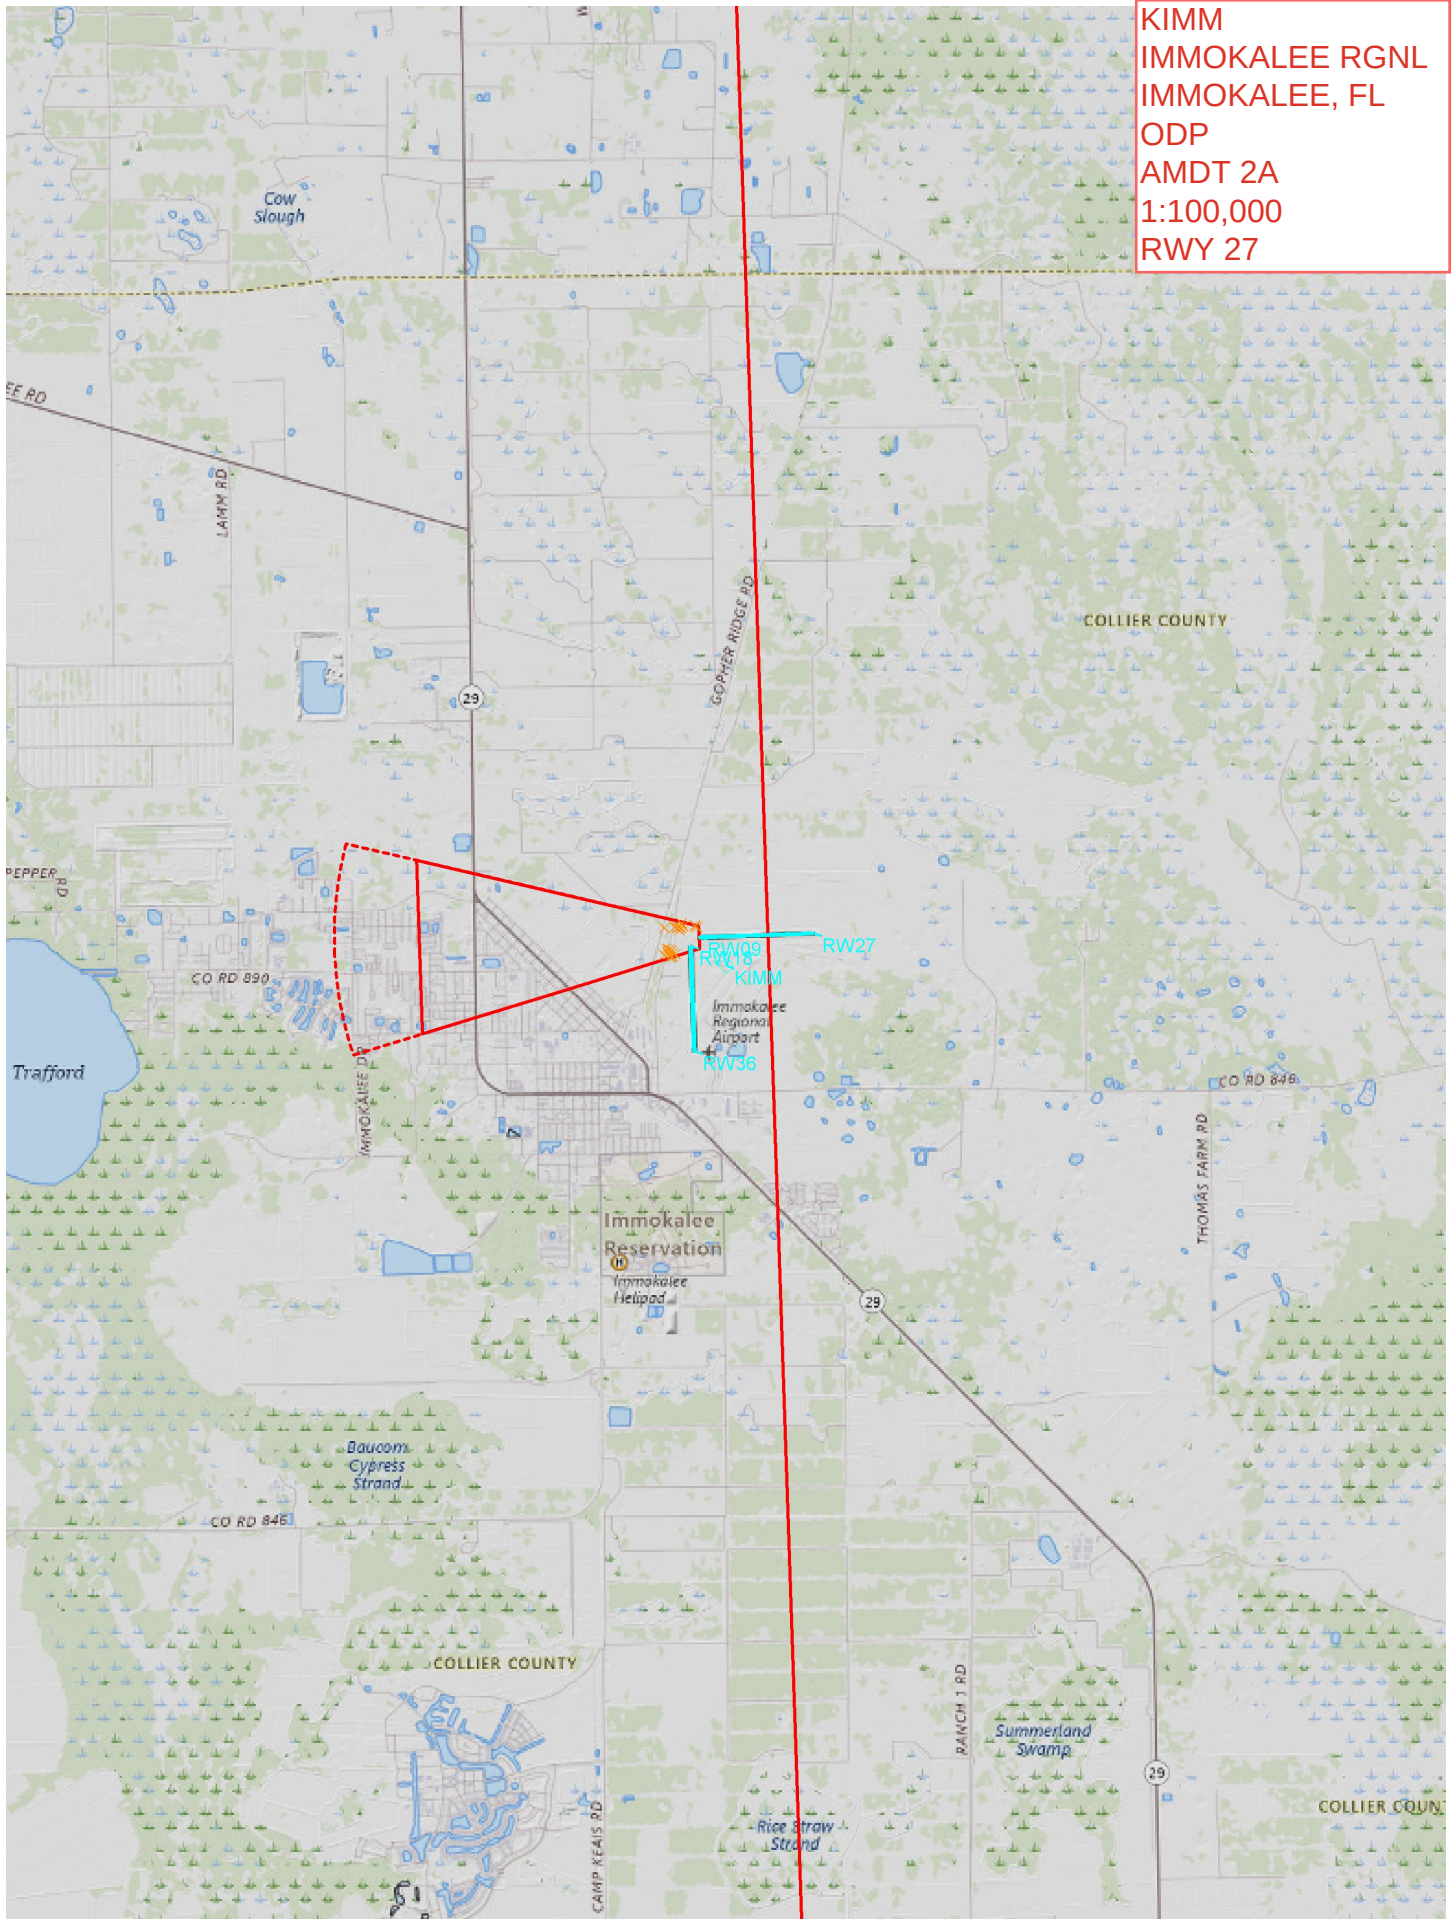

KIMM
IMMOKALEE RGNL
IMMOKALEE, FL
ODP
AMDT 2A
1:100,000
RWY 36

