

Flight Procedures Cover Page	Task Action: FLIGHT CHECK	Task Type: IAP	Estimated Chart Date: 03/24/2022	APWS Task ID: 47A5DBF3B12B4457B521EDFD35455E71	APWS Project ID: 06BE0008BAEF46E59006AAA4C53DF2CE
Procedure: RADAR 1 AMDT ORIG-A		Enroute: NO	Specialist: Young, Silvia		Agreement Number:
Airport ID: KVUJ			Airport City: ALBEMARLE		State: NC
Facility ID:	Facility Type:	Flight Inspection Remark Type: New FC Slot			
Procedure Comments: ACTIVE DATA USED FOR KVUJ AIRPORT RWY 22L AND VUJ PAR. CANCEL NOTAM 1/1096 UPON PUBLICATION. NEW CTRL OBST: 691 TREE (37-112067) 352551N/0800814W. CONTACT JON DENTON 405.954.5467. 12/22/2021 					

FIPC BASIC FORM						
PROCEDURE: RADAR 1 AMDT ORIG-A			AIRPORT NAME: STANLY COUNTY		AIRPORT ID: KVUJ	SPECIAL CONTROL NO: AP-03-093-23
FAC ID: VUJ		CITY: ALBEMARLE			ST: NC	ORIG CHART DATE: 08/10/2023
DFL TYPE: PROC/A	THIRD PARTY: ☐ YES	EST. TIME ON SITE: 0.4	REIMB. NUMBER:	PTS TASK ID: 47A5DBF3B12B4457B521EDFD35455E71		
PREFLIGHT NOTES						
REVIEWER: robert e williams					DATE: 08/31/2023	
COMMENTS: Ground evaluation of amended procedure, Stanly County, Albemarle, NC, RADAR ONE, Original A. Changed controlling obstacle from one AAO to another raising mins 132 feet. None of the changes made in the updated copy require airborne evaluation.					CHECK ONE: ☐ FLT CK REQ ☒ NFCR ☐ REJECT YES NO CPV COMPLETE? X	
PROCEDURE RESULTS						
INSPECTION DATE: 08/31/2023	CREW #: VN426	N #:	INSTRUMENT PROCEDURE STATUS: ☒ SAT ☐ SAT W/CHANGES ☐ UNSAT		ARINC CODING: ☐ SAT ☐ SAT/GOLD ☐ UNSAT	
FLIGHT INSPECTOR SIGNATURE: robert e williams @ 08/31/2023 08:35			PRINTED NAME: WILLIAMS, ROBERT EMIL			NOTAM INITIATED? ☐ YES ☒ NO
FLIGHT INSPECTOR REMARKS:						
IN-FLIGHT OBSTACLE REPORT						
OBSTRUCTION ID #:	COORDINATES OR LOCATION:	GNSS ALTITUDE (MSL):	BAROMETRIC ALTITUDE (MSL):	HEIGHT ABOVE GROUND LEVEL:		

RADAR INSTRUMENT APPROACH MINIMUMS

ALBEMARLE, NC
STANLY COUNTY (VUJ)
RADAR-1 128.325 307.8 

Orig, 22JUN17 (19059) (FAA)

ELEV 609

	<u>RWY</u>	<u>GS/TCH/RPI</u>	<u>CAT</u>	<u>DH/</u> <u>MDA-VIS</u>	<u>HAT/</u> <u>HAA</u>	<u>CEIL-VIS</u>
PAR	22L	3.0°/40/767	ABCD	784-¾	200	(200-¾)

Procedure NA when control tower closed.

BEAUFORT, SC
BEAUFORT EXECUTIVE (ARW)
RADAR-1 125.125 292.125  NA

Amdt 3A, 10MAY07 (20310) (FAA)

ELEV 10

	<u>RWY</u>	<u>GP/TCH/RPI</u>	<u>CAT</u>	<u>DA/</u> <u>MDA-VIS</u>	<u>HAT/</u> <u>HAA</u>	<u>CEIL-VIS</u>	<u>CAT</u>	<u>DA/</u> <u>MDA-VIS</u>	<u>HAT/</u> <u>HAA</u>	<u>CEIL-VIS</u>
ASR	25		ABC	440-1¼	430	(500-1¼)				
CIRCLING	ALL RWY		AB	500-1¼	490	(500-1¼)	C	500-1½	490	(500-1½)

Use Beaufort MCAS/Merritt Field altimeter setting.
When Beaufort Class D not in effect, procedure NA.


09 SEP 2021 to 07 OCT 2021

09 SEP 2021 to 07 OCT 2021

RADAR INSTRUMENT APPROACH MINIMUMS

KVUJ
STANLY COUNTY
ALBEMARLE, NC
PAR FINAL
1:100,000


PAR
MA Sloped Surface
TREE (691) 37-112067

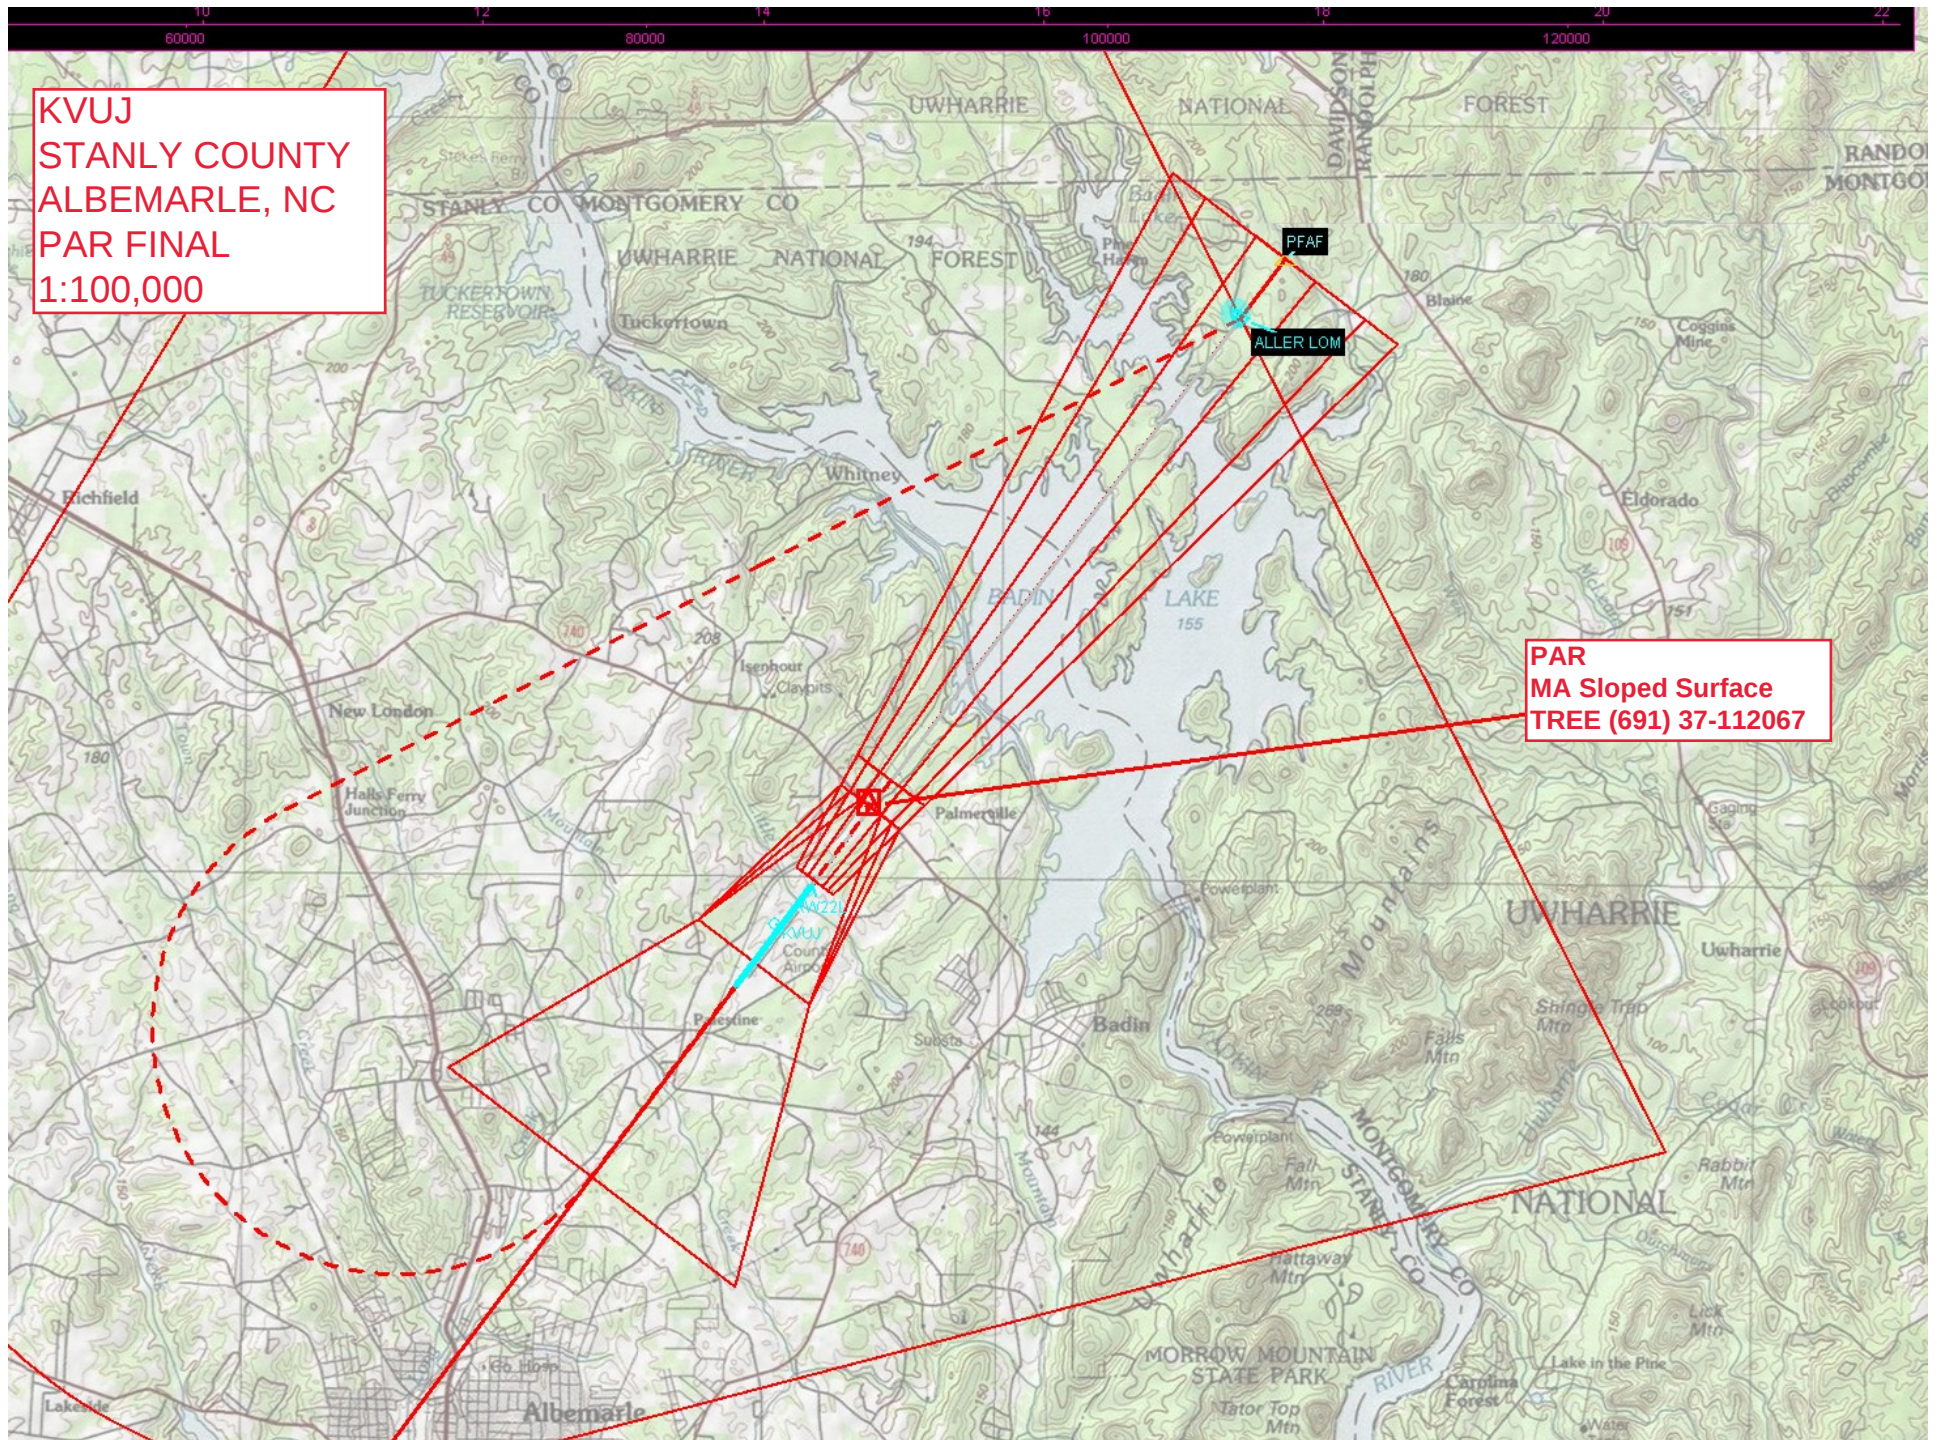

KVUJ
STANLY COUNTY
ALBEMARLE, NC
ALT MA
1:100,000

PAR
Alt MA Sloped Surface
TREE (691) 37-112067

Alt Missed Level Surface
TOWER (1064) 37-000246

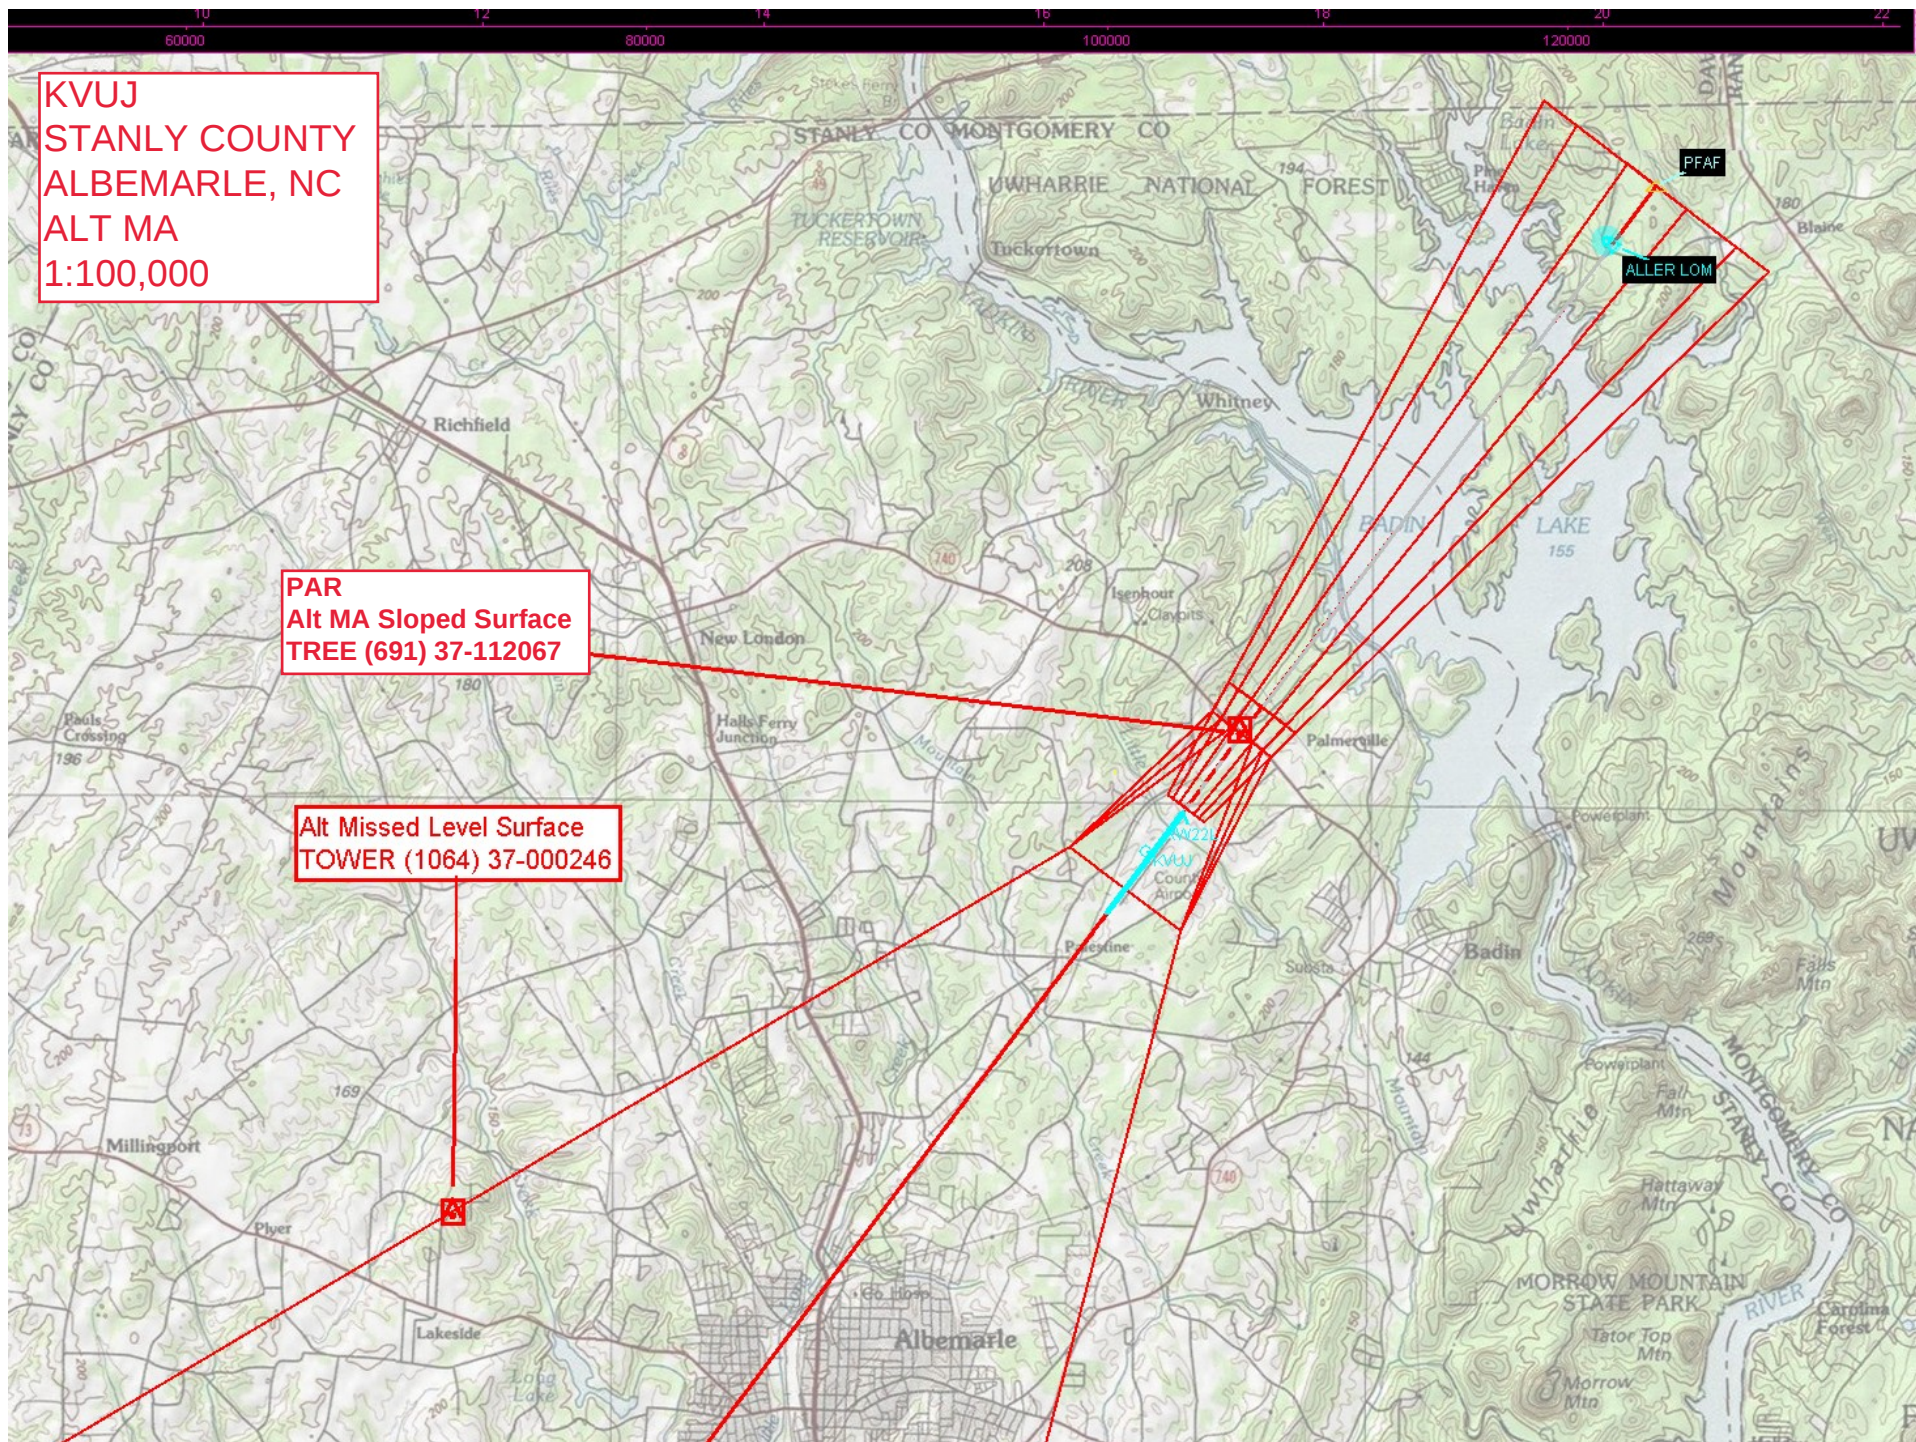

KVUJ
STANLY COUNTY
ALBEMARLE, NC
ALT MA
1:500,000

PAR
Alt MA Sloped Surface
TREE (691) 37-112067

Alt Missed Level Surface
TOWER (1064) 37-000246

