

Flight Procedures Cover Page	Task Action: FLIGHT CHECK	Task Type: Textual DP	Estimated Chart Date: 08/07/2025	APWS Task ID: C8C5786B780C4D65B3B7AD186B1CF700	APWS Project ID: 0F54D63579A24F328B97C7386EC5453C
Procedure: TAKEOFF MINIMUMS AND OBSTACLE DP AMDT 3		Enroute: NO	Specialist: Dugan, Joshua		Agreement Number:
Airport ID: KEZS			Airport City: SHAWANO		State: WI
Facility ID:	Facility Type:	Flight Inspection Remark Type: New FC Slot			
Procedure Comments: UPDATED LOW CLOSE IN OBS AND TAKEOFF MINIMUMS CLEARs NOTAM FDC 3/6732 CONTACT ERIC SUSKI AJV-A431 405-954-7331 05/19/25: THIS IS A CORRECTED COPY OF THE FORM APPROVED ON 4/24/25. TEXTUAL DEPARTURE: ADDED BEFORE PROCEEDING ON COURSE. QUALITY 16 CHECKED QUALITY 23 CHECKED					

FIPC BASIC FORM						
PROCEDURE: TAKEOFF MINIMUMS AND OBSTACLE DP AMDT 3			AIRPORT NAME: SHAWANO MUNI		AIRPORT ID: KEZS	SPECIAL CONTROL NO: BP-04-083-25
FAC ID: KEZS		CITY: SHAWANO			ST: WI	ORIG CHART DATE: 08/07/2025
DFL TYPE: PROC/T	THIRD PARTY: ☐ YES	EST. TIME ON SITE: 0.4	REIMB. NUMBER:	PTS TASK ID: C8C5786B780C4D65B3B7AD186B1CF700		
PREFLIGHT NOTES						
REVIEWER: scott wiebe					DATE: 04/22/2025	
COMMENTS:					CHECK ONE:	
					☒ FLT CK REQ ☐ NFCR ☐ REJECT	
						YES
					CPV COMPLETE?	
					X	
PROCEDURE RESULTS						
INSPECTION DATE: 04/22/2025	CREW #: VN219	N #: N83	INSTRUMENT PROCEDURE STATUS: ☒ SAT ☐ SAT W/CHANGES ☐ UNSAT		ARINC CODING: ☐ SAT ☐ SAT/GOLD ☐ UNSAT	
FLIGHT INSPECTOR SIGNATURE: scott wiebe @ 04/22/2025 22:22			PRINTED NAME: WIEBE, GREGORY SCOTT			NOTAM INITIATED? ☐ YES ☒ NO
FLIGHT INSPECTOR REMARKS:						
IN-FLIGHT OBSTACLE REPORT						
OBSTRUCTION ID #:	COORDINATES OR LOCATION:	GNSS ALTITUDE (MSL):	BAROMETRIC ALTITUDE (MSL):	HEIGHT ABOVE GROUND LEVEL:		



24361

TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)



SALEM, IL

SALEM-LECKRONE (SLO)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

AMDT 7 10JAN13 (13010) (FAA)

TAKEOFF MINIMUMS:

Rwy 18, 300-1¼ or std. w/min. climb of 291' per NM to 900' MSL.

DEPARTURE PROCEDURE:

Rwy 18, Climb heading 181° to 1900 before turning east.

TAKEOFF OBSTACLE NOTES:

Rwy 18, trees beginning 272' from DER, left and right of centerline, up to 100' AGL/635' MSL.

Antenna tower 1.0 NM from DER, 257' right of centerline, 200' AGL/739' MSL.

Tower 1.0 NM from DER, 126' left of centerline, 188' AGL/724' MSL.

Rwy 36, trees beginning 59' from DER, 249' right of centerline, up to 20' AGL/588' MSL.

SAVANNA, IL

TRI-TOWNSHIP (SFY)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

ORIG-A 12AUG21 (21224) (FAA)

TAKEOFF MINIMUMS:

Rwy 13, 400-2¼ or std. w/min. climb of 208' per NM to 1100.

TAKEOFF OBSTACLE NOTES:

Rwy 13, vehicle on road 20' from DER, 352' left of centerline, 627' MSL.

Tree 99' from DER, 71' right of centerline, 616' MSL.

Tree 104' from DER, 281' left of centerline, 635' MSL.

Trees, vehicle on road, agriculture equipment beginning 199' from DER, 25' left of centerline, up to 638' MSL.

Tree 278' from DER, 346' right of centerline, 627' MSL.

Tree 454' from DER, 0' of centerline, 628' MSL.

Tree 651' from DER, 40' right of centerline, 630' MSL.

Tree 720' from DER, 152' right of centerline, 631' MSL.

Tree 2.1 NM from DER, 3451' left of centerline, 947' MSL.

Rwy 31, vehicle on road 7' from DER, 421' right of centerline, 622' MSL.

Vehicle on road beginning 10' from DER, 168' right of centerline, up to 627' MSL.

Trees, vehicle on road beginning 132' from DER, 114' left of centerline, up to 638' MSL.

Tree 173' from DER, 545' right of centerline, 639' MSL.

Trees, vehicle on road beginning 282' from DER, 117' right of centerline, up to 666' MSL.

Trees beginning 693' from DER, 160' left of centerline, up to 640' MSL.

Trees beginning 793' from DER, 4' right of centerline, up to 676' MSL.

Tree 1005' from DER, 768' left of centerline, 641' MSL.

Tree 1050' from DER, 114' left of centerline, 652' MSL.

Trees beginning 1126' from DER, 314' left of centerline, up to 679' MSL.

Trees beginning 1557' from DER, 223' left of centerline, up to 688' MSL.

Trees beginning 1702' from DER, 38' right of centerline, up to 679' MSL.

Trees beginning 1733' from DER, 28' left of centerline, up to 689' MSL.

SHAWANO, WI

SHAWANO MUNI (Ezs)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

AMDT 2A 03APR14 (14093) (FAA)

TAKEOFF MINIMUMS:

Rwy 12, 600-3 or std. w/ min. climb of 329' per NM to 1600.

Rwy 17, 300-2 or std. w/ min. climb of 245' per NM to 1200.

Rwy 30, 300-1½ or std. w/ min. climb of 248' per NM to 1100.

TAKEOFF OBSTACLE NOTES:

Rwy 12, tower 2.3 NM from DER, 3006' right of centerline, 222' AGL/1240' MSL.

Multiple trees beginning 1700' from DER, 389' left to 2432' right of centerline, up to 100' AGL/1149' MSL.

Rwy 17, multiple trees beginning 1710' from DER, 2951' left to 1292' right of centerline, up to 100' AGL/1059' MSL.

Elevator 5839' from DER, 738' right of centerline, 149' AGL/979' MSL.

Rwy 30, multiple trees beginning 649' from DER, 1052' left to 1117' right of centerline, up to 100' AGL/929' MSL.

Vehicle on road 538' from DER, crossing left to right 17' AGL/826' MSL.

Water tank 1.1 NM from DER, 1310' right of centerline, 175' AGL/1019' MSL.

Rwy 35, ships 1007' from DER, left to right of centerline, up to 60' AGL/869' MSL.

Vehicle on road 580' from DER, left to right of centerline, up to 15' AGL/824' MSL.

Multiple trees beginning 2200' from DER, 724' left of centerline, up to 100' AGL/909' MSL.

26 DEC 2024 to 23 JAN 2025

26 DEC 2024 to 23 JAN 2025




24361

TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)





EC-3

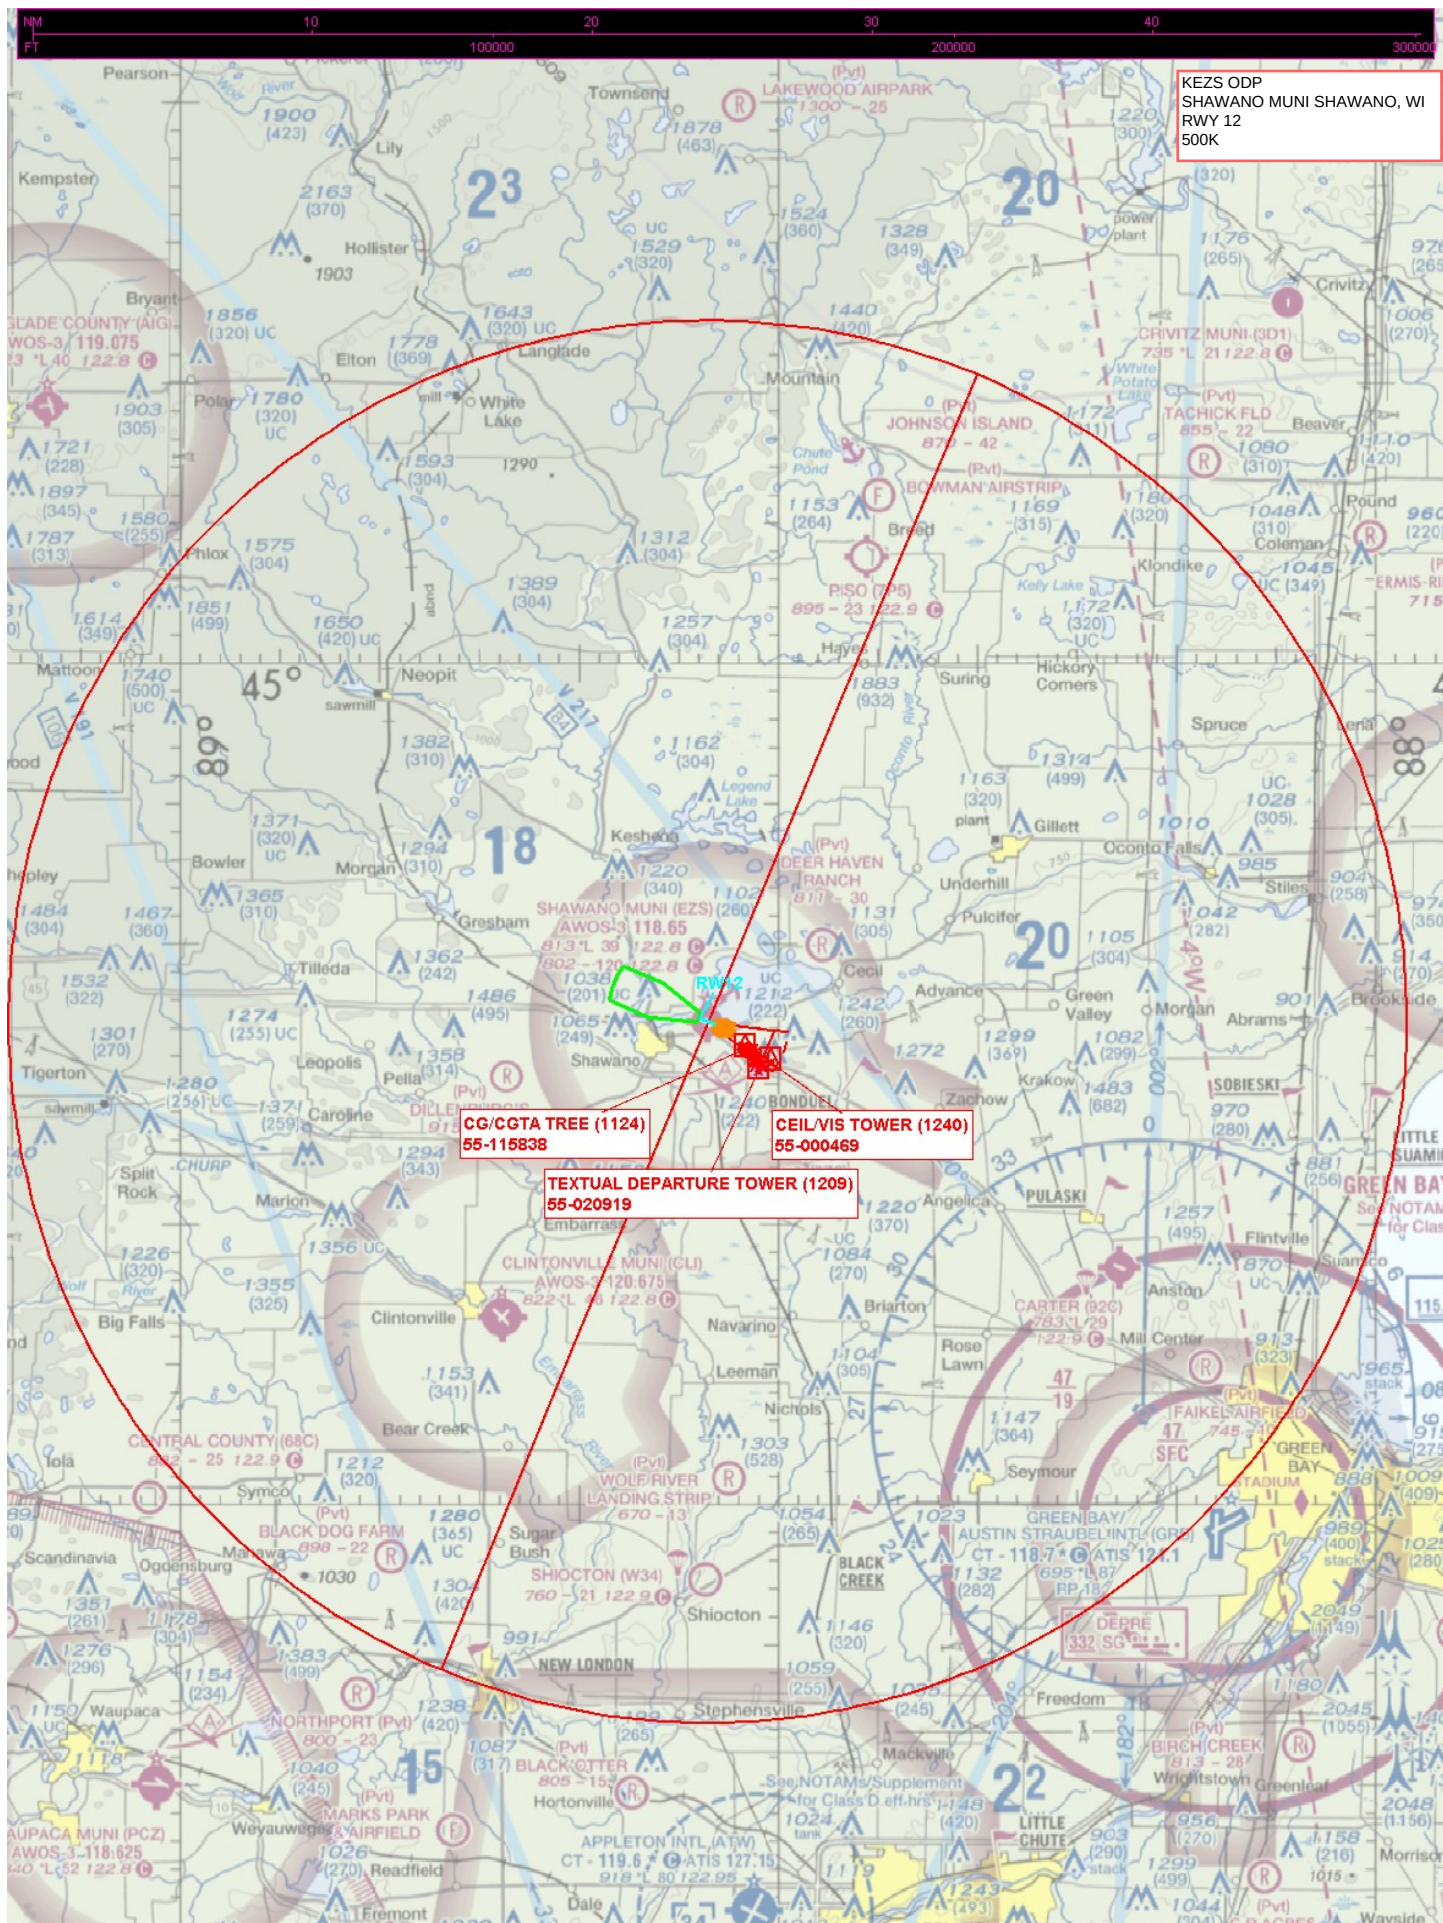



KEZS ODP
SHAWANO MUNI SHAWANO, WI
RWY 12
100K

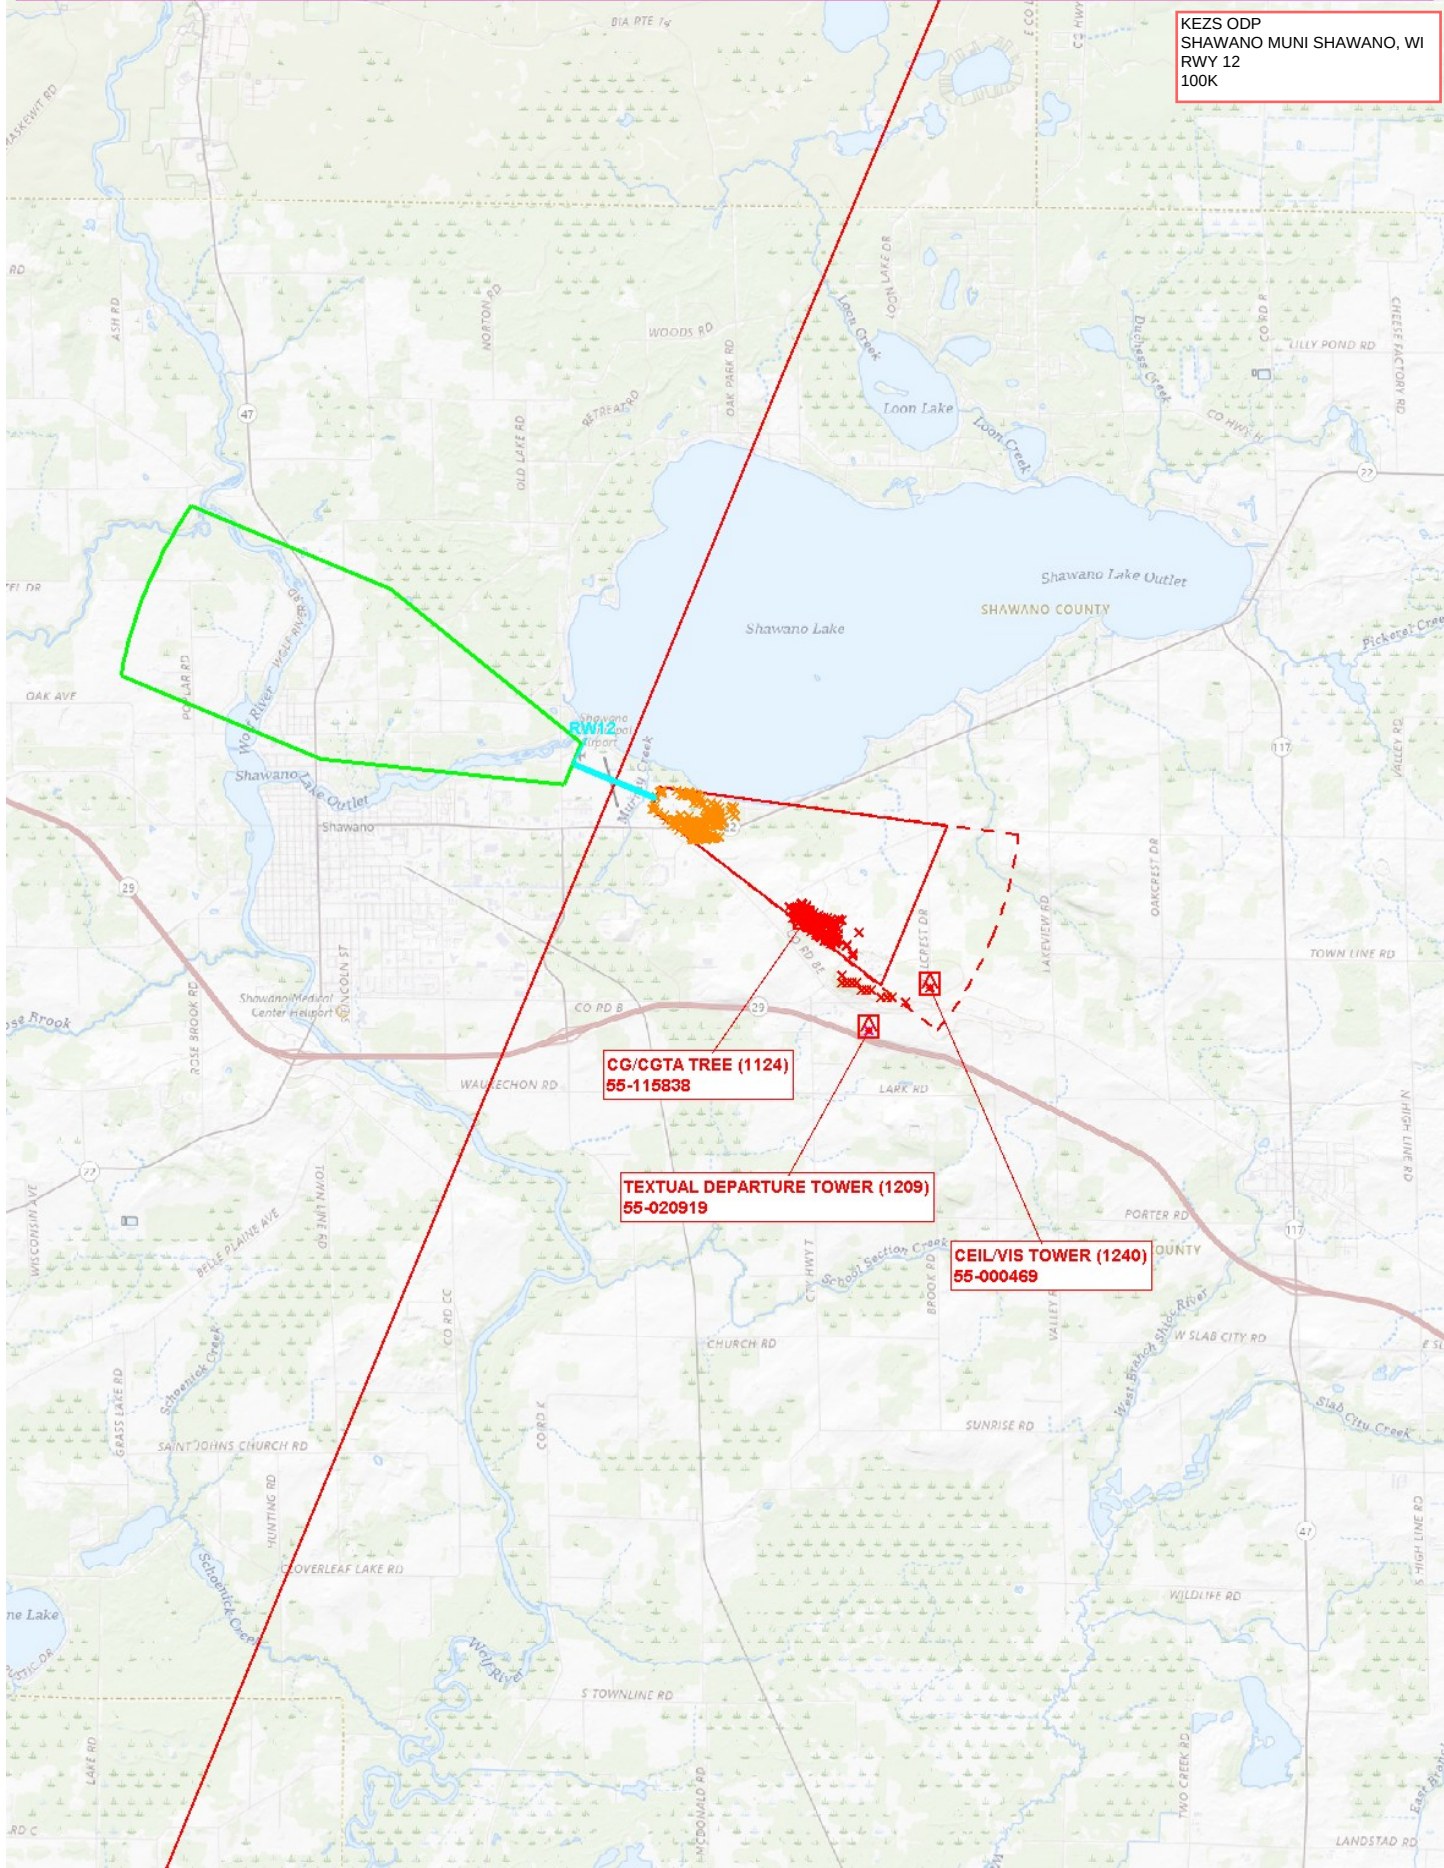

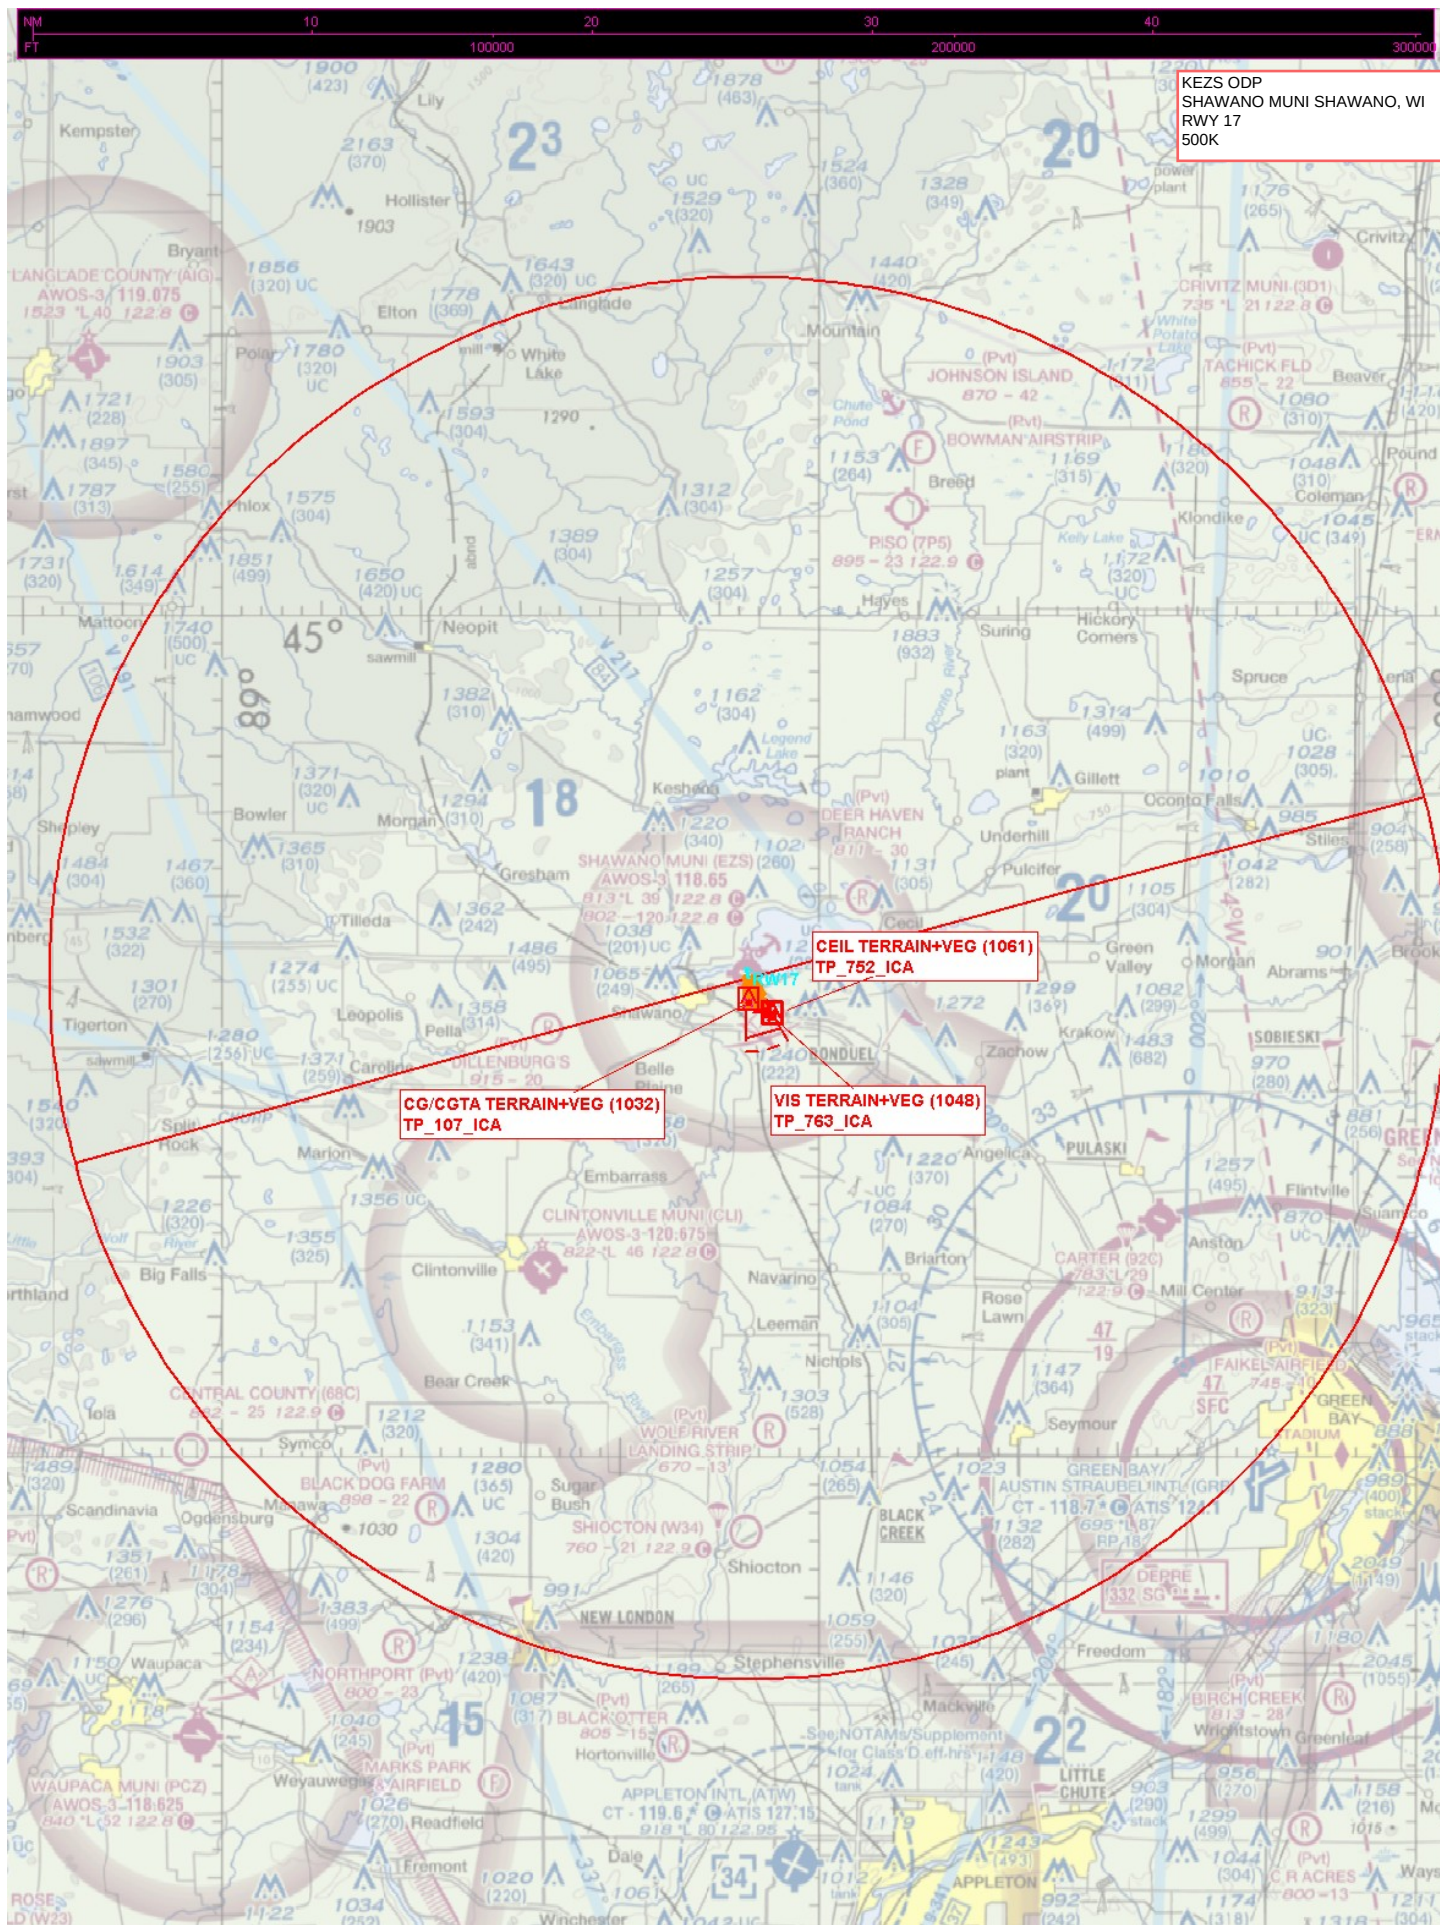


KEZS ODP
SHAWANO MUNI SHAWANO, WI
RWY 17
500K

CEIL TERRAIN+VEG (1061)
TP_752_ICA

CG/CGTA TERRAIN+VEG (1032)
TP_107_ICA

VIS TERRAIN+VEG (1048)
TP_763_ICA

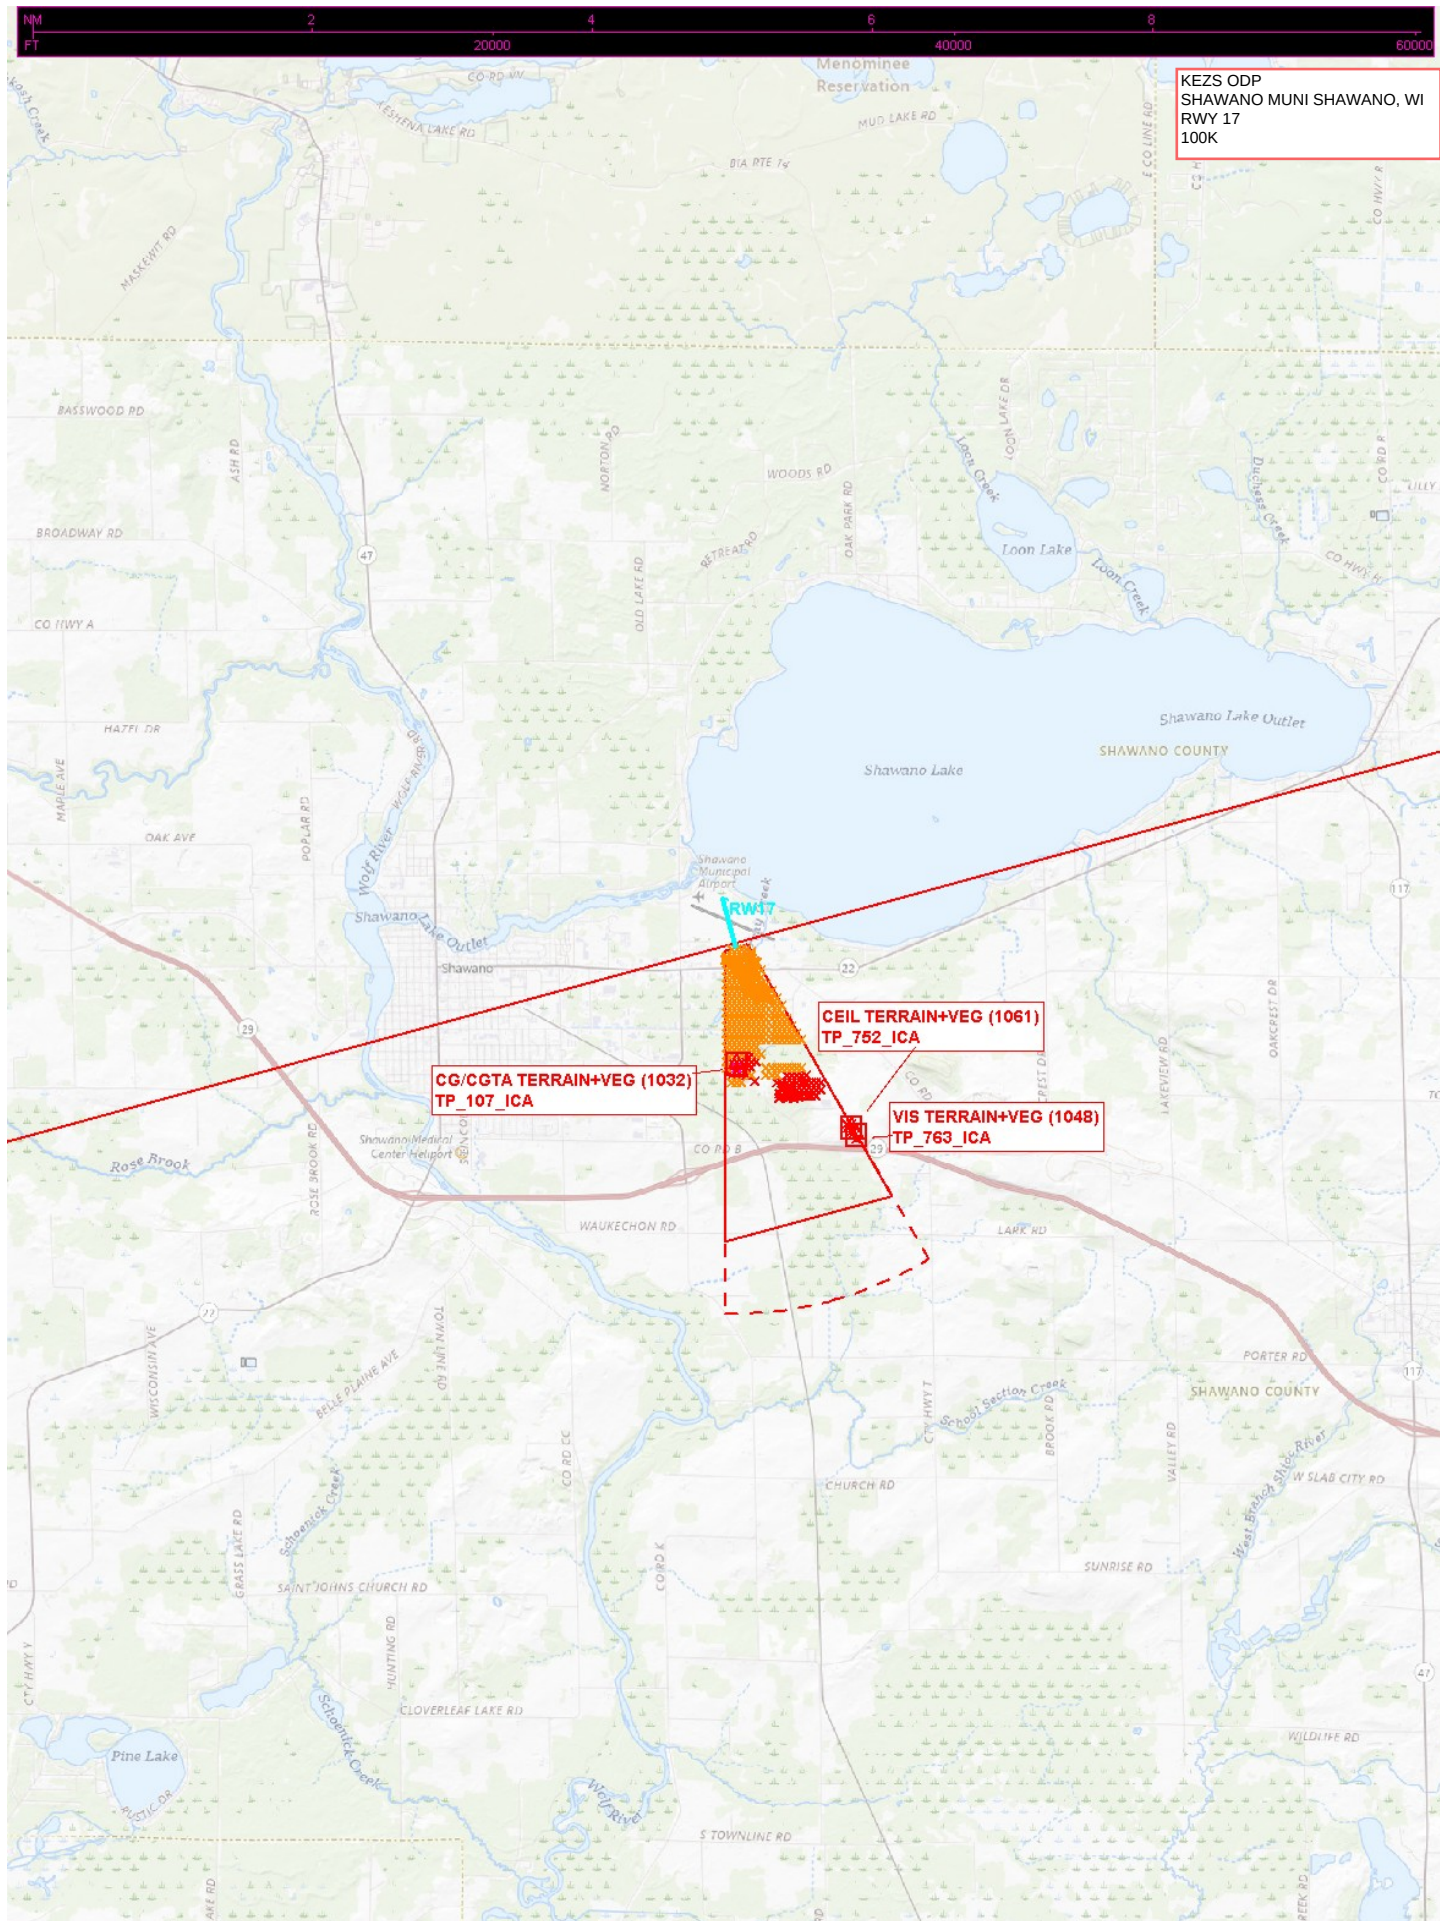



KEZS ODP
SHAWANO MUNI SHAWANO, WI
RWY 17
100K

CG/CGTA TERRAIN+VEG (1032)
TP 107 ICA

CEIL TERRAIN+VEG (1061)
TP 752 ICA

VIS TERRAIN+VEG (1048)
TP 763 ICA

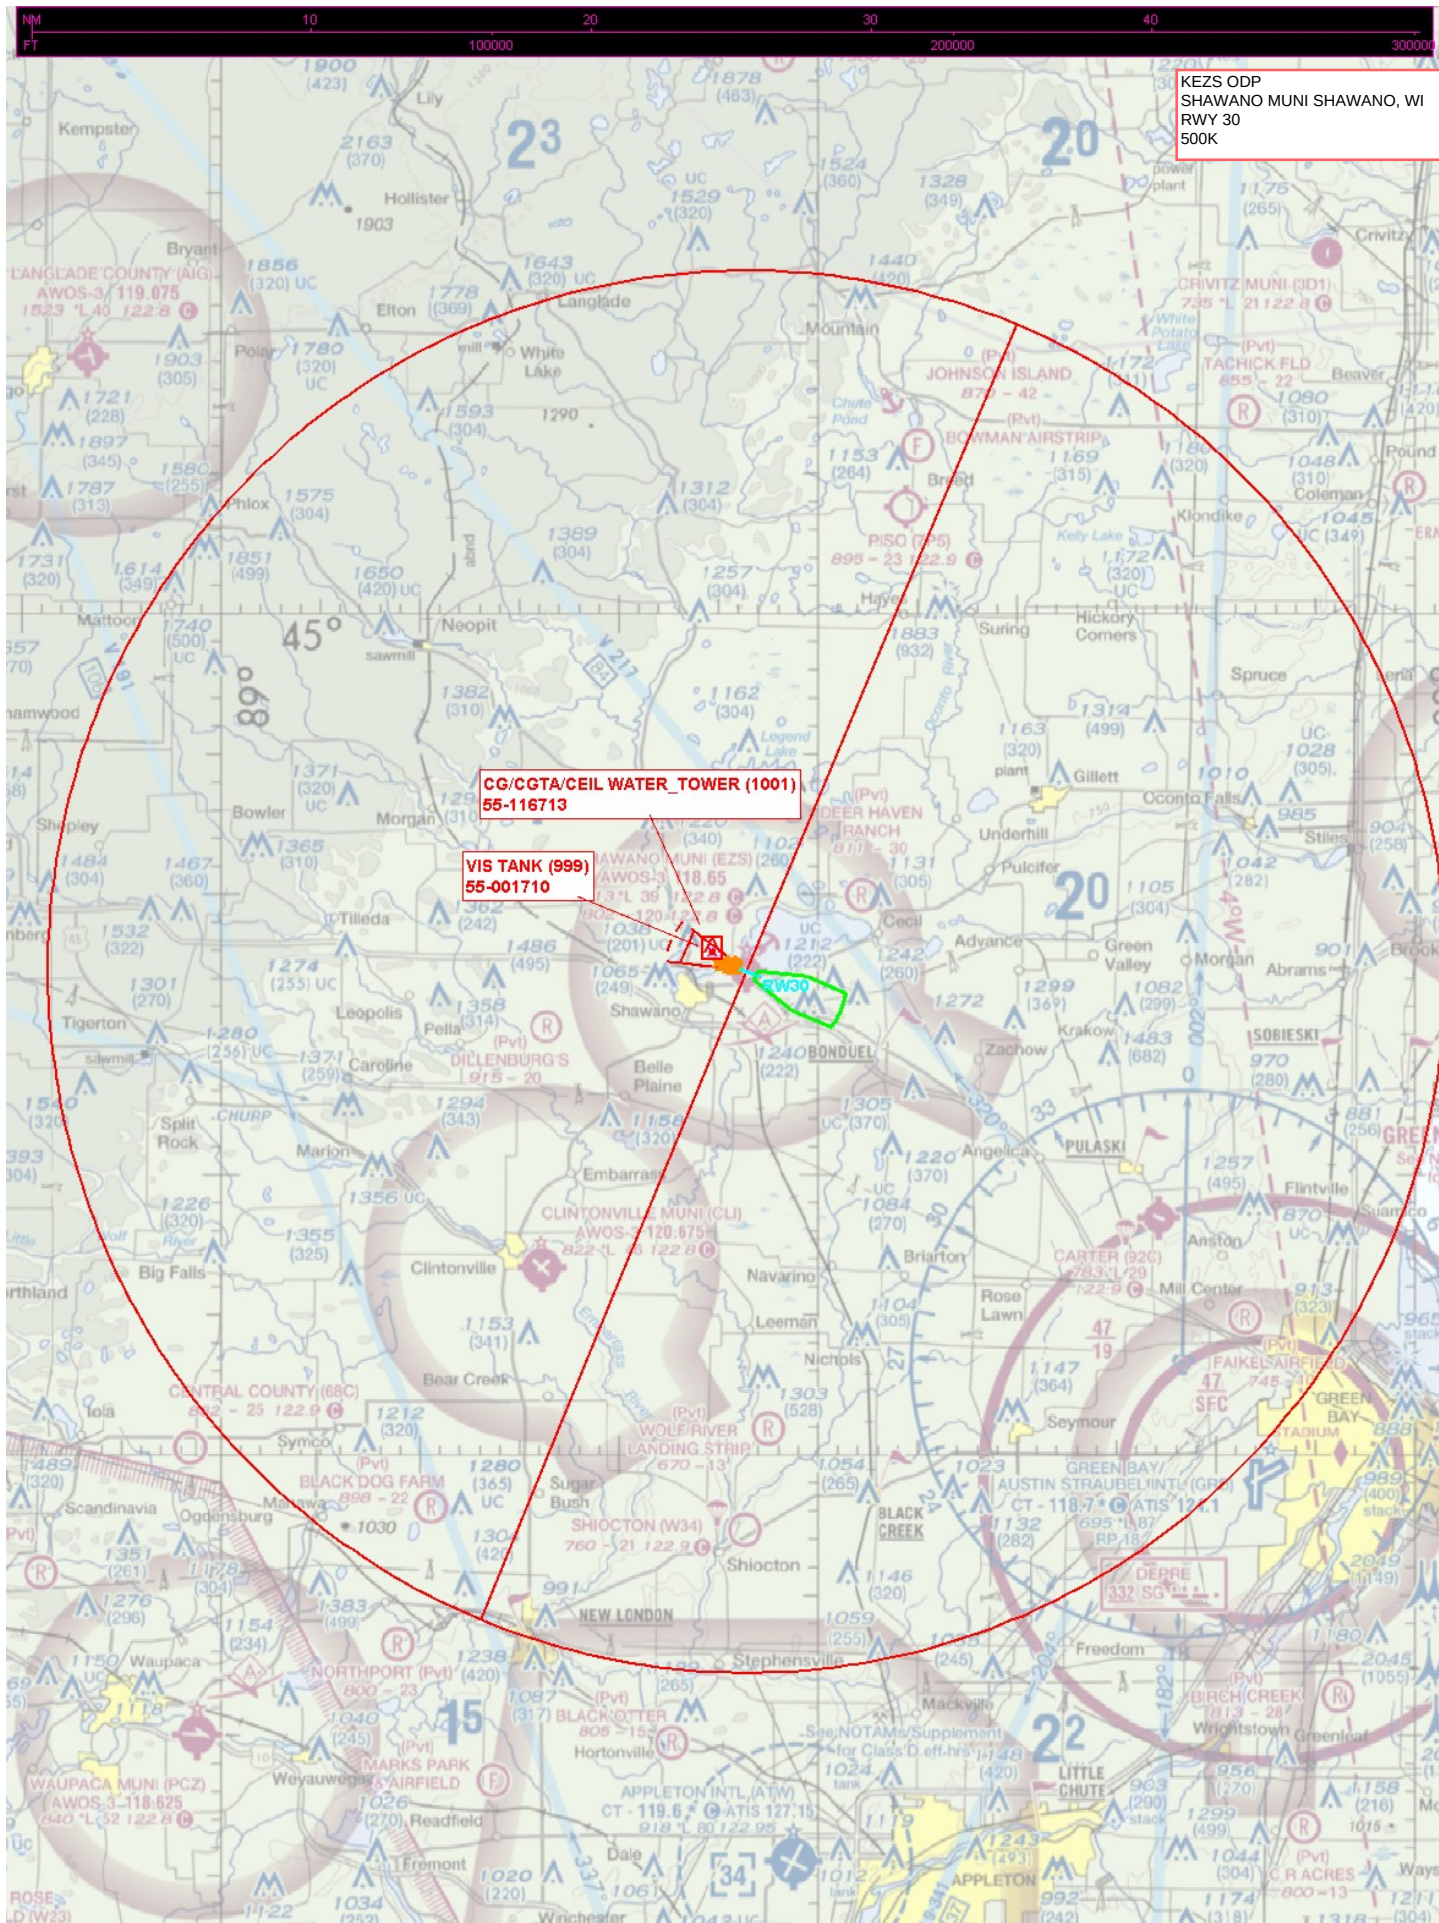

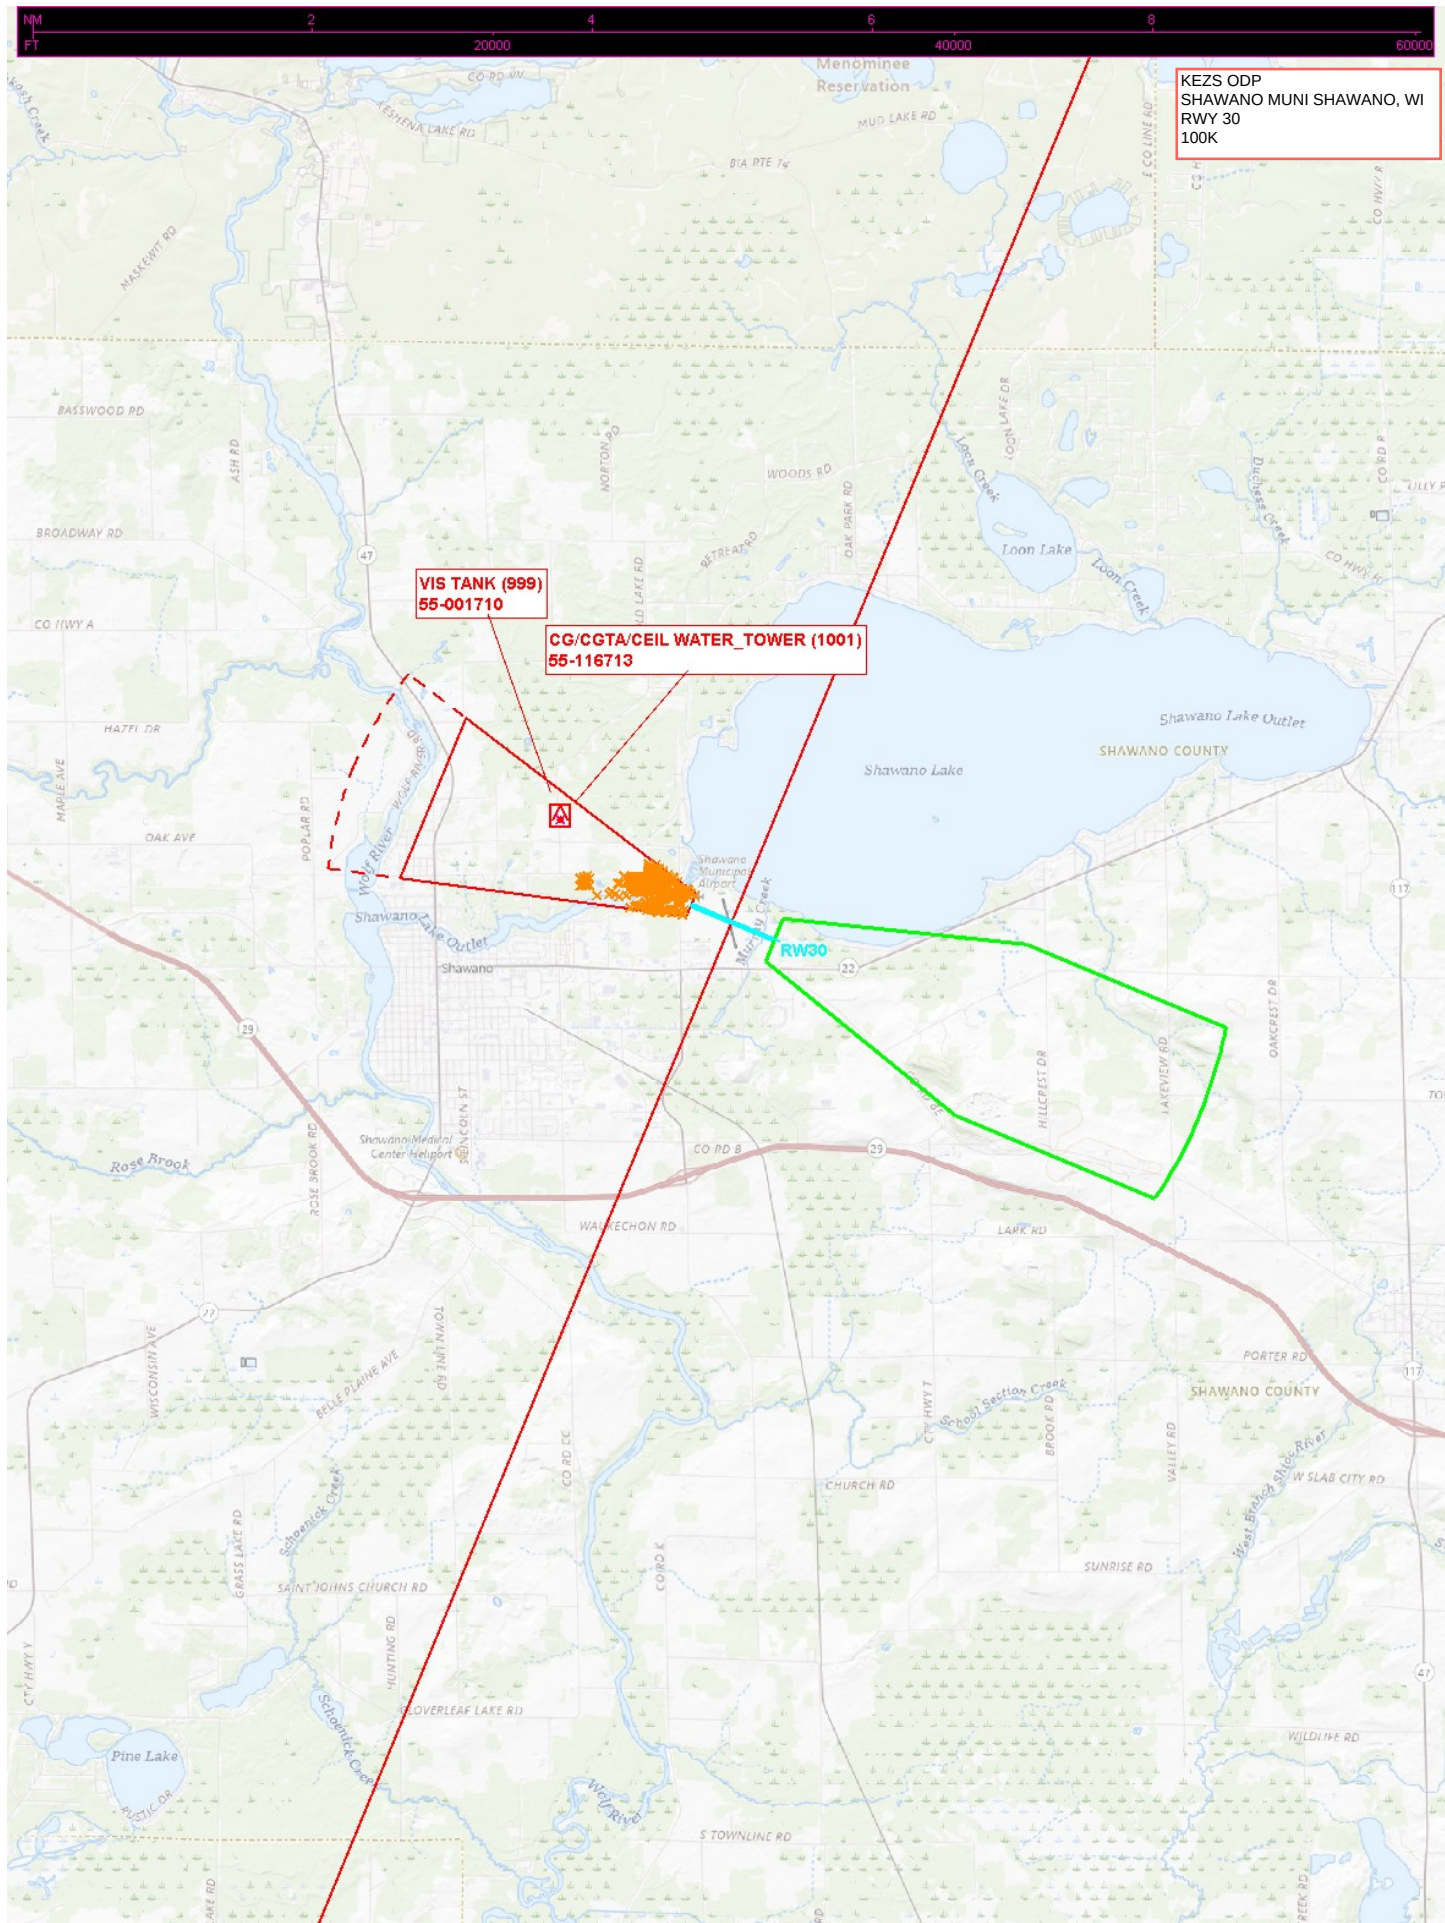

KEZS ODP
SHAWANO MUNI SHAWANO, WI
RWY 30
100K

VIS TANK (999)
55-001710

CG/CGTA/CEIL WATER_TOWER (1001)
55-116713

RW30

