

| | | | | | |
|---|------------------------------|---|---------------------------------------|---|--|
| Flight Procedures Cover Page | Task Action: FLIGHT CHECK | Task Type: Textual DP | Estimated Chart Date: 01/25/2024 | APWS Task ID: FEC22250378C435F9A19A73C39F7A192 | APWS Project ID: 80F8345BBE47440CB6D42D10C921FE11 |
| Procedure: TAKEOFF MINIMUMS AND OBSTACLE DP AMDT 2 | | Enroute: NO | Specialist: Wilkinson, Christopher | | Agreement Number: |
| Airport ID: KMLJ | | | Airport City: MILLEDGEVILLE | | State: GA |
| Facility ID: | Facility Type: | Flight Inspection Remark Type: New FC Slot | | | |
| <div>Procedure Comments: PENDING DATA USED FOR KMLJ AIRPORT. REVIEWED AND UPDATED TAKEOFF MINIMUMS DUE TO THRESHOLD RELOCATION. CONTACT CASIMIR TABAKA: AJV-430, (405) 954-7931</div> <div>QUALITY 20 CHECKED</div> | | | | | |



23110

TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)



MILLEDGEVILLE, GA

OLD

BALDWIN COUNTY RGNL (MLJ)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES
AMDT 1A 08NOV18 (18312) (FAA)

TAKEOFF MINIMUMS:

Rwy 28, 300-1 or std. w/min. climb of 330' per NM to 700.

DEPARTURE PROCEDURE:

Rwy 10, climb heading 096° to 1000 before turning.

Rwy 28, climb heading 276° to 1400 before turning right.

TAKEOFF OBSTACLE NOTES:

Rwy 10, trees beginning 67' from DER, 87' right of centerline, up to 100' AGL/449' MSL.

Utility poles beginning 196' from DER, 268' right of centerline, up to 30' AGL/372' MSL.

Trees beginning 62' from DER, 298' left of centerline, up to 100' AGL/445' MSL.

Utility poles beginning 135' from DER, 381' left of centerline, up to 30' AGL/380' MSL.

Multiple structures beginning 242' from DER, 523' left of centerline, up to 19' AGL/369' MSL.

Rwy 28, trees beginning 12' from DER, 64' right of centerline, up to 100' AGL/500' MSL.

Terrain 729' from DER, 495' right of centerline, 437' MSL.

Trees beginning 515' from DER, 59' left of centerline, up to 100' AGL/534' MSL.

MILLEN, GA

MILLEN (2J5)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES
AMDT 1 20AUG15 (15232) (FAA)

TAKEOFF OBSTACLE NOTES:

Rwy 17, tree 35' from DER, 377' left of centerline, 92' AGL/292' MSL.

Trees beginning 139' from DER, from 263' left of centerline, up to 100' AGL/307' MSL.

Trees beginning 1864' from DER, from 805' left to 451' right of centerline, up to 100' AGL/331' MSL.

Rwy 35, pole 237' from DER, 400' left of centerline, 33' AGL/283' MSL.

Vehicles on road beginning 272' from DER, 331' left of centerline, up to 15' AGL/279' MSL.

Poles, terrain, and building beginning 504' from DER, from 666' left of centerline to 34' right of centerline, up to 34' AGL/299' MSL.

Trees and poles beginning 983' from DER, left and right of centerline, up to 65' AGL/326' MSL.

Elevator and silo 1021' from DER, 760' left of centerline, up to 76' AGL/340' MSL.

MOBILE, AL

MOBILE INTL (BFM)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES
AMDT 1 07MAY09 (22195) (FAA)

TAKEOFF MINIMUMS:

Rwy 14, 400-2¼ or std. w/min. climb of 244' per NM to 500.

DEPARTURE PROCEDURE:

Rwy 36, climb heading 001° to 900 before turning right.

TAKEOFF OBSTACLE NOTES:

Rwy 18, trees beginning 1453' from DER, 54' right of centerline, up to 100' AGL/129' MSL.

Trees beginning 2646' from DER, 120' left of centerline, up to 73' AGL/102' MSL.

Rwy 32, sign 2780' from DER, 1041' left of centerline, 109' AGL/119' MSL.

Trees beginning 847' from DER, 35' right of centerline, up to 100' AGL/109' MSL.

Trees beginning 1089' from DER, 19' left of centerline, up to 100' AGL/107' MSL.

Rwy 36, poles beginning 1231' from DER, 319' right of centerline, up to 49' AGL/69' MSL.

Trees beginning 467' from DER, 325' right of centerline, up to 55' AGL/84' MSL.

MOBILE RGNL (MOB)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES
AMDT 1A 29MAY14 (14149) (FAA)

TAKEOFF OBSTACLE NOTES:

Rwy 15, tree 1758' from DER, 886' right of centerline, 79' AGL/270' MSL.

Tree 1987' from DER, 856' left of centerline, 73' AGL/277' MSL.

Tree 2102' from DER, 861' right of centerline, 78' AGL/269' MSL.

Tree 2131' from DER, left of centerline, 76' AGL/280' MSL.

Rwy 18, multiple trees beginning 1597' from DER, 15' left of centerline, up to 69' AGL/273' MSL.

Multiple trees beginning 1671' from DER, 207' right of centerline, up to 87' AGL/278' MSL.

Rwy 36, multiple trees beginning 1083' from DER, 210' right of centerline, up to 84' AGL/301' MSL.


Multiple trees beginning 532' from DER, 43' left of centerline, up to 73' AGL/287' MSL.




23110


TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)





AIRPORT ID: KMLJ
AIRPORT NAME: BALDWIN COUNTY RGNL
CITY/STATE: MILLEDGEVILLE, GA
PROC ID: DP RWY 28
AMDT: 2
SCALE: 1:100,000
TAKE OFF OBS - SEE 8260-15A

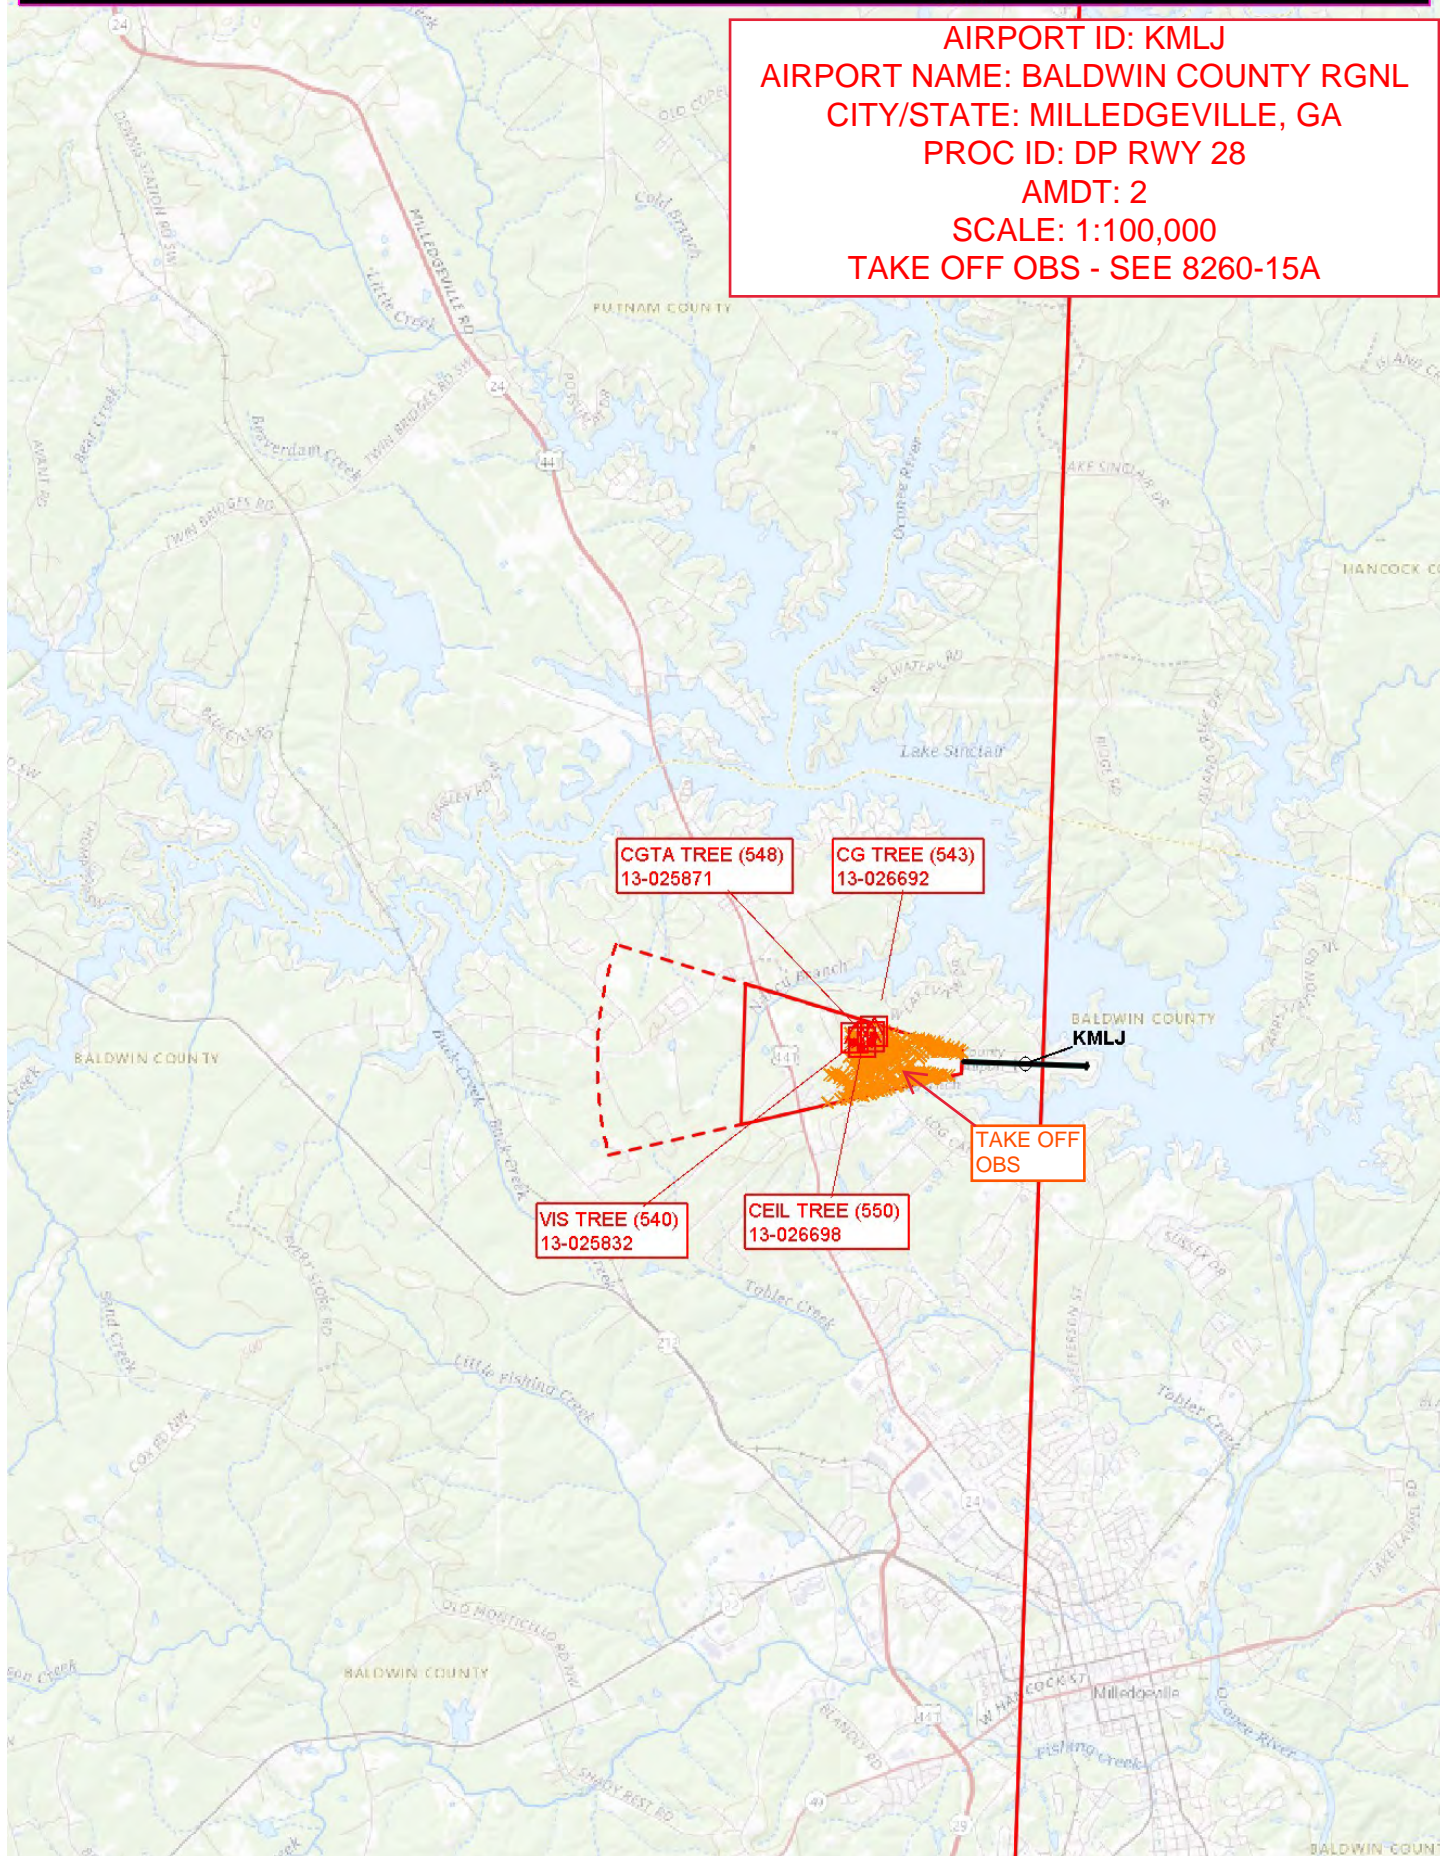

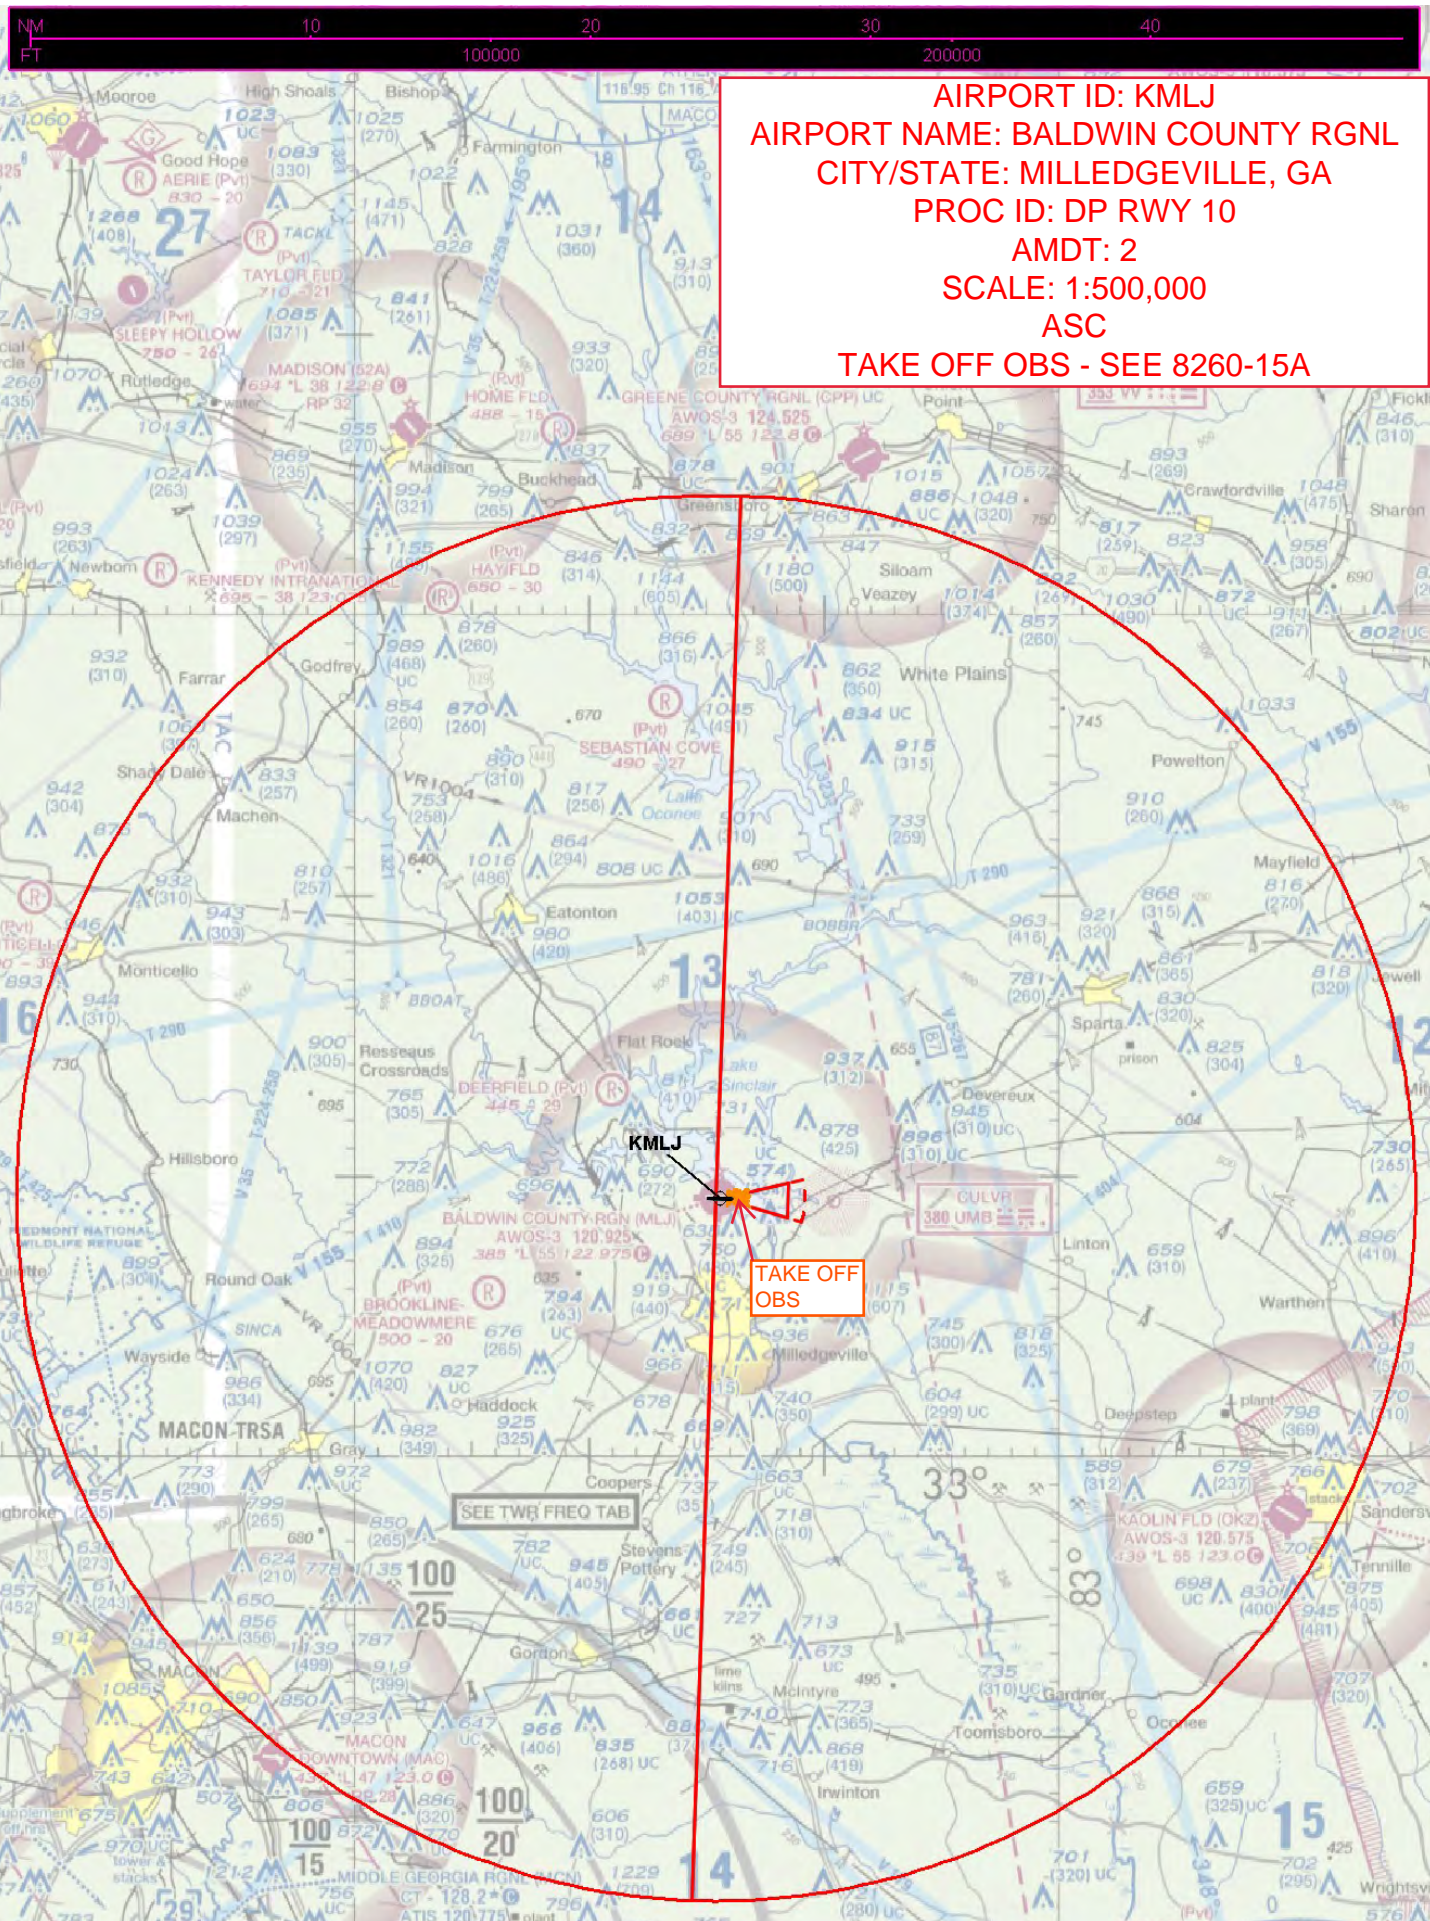

NM
FT

10

20

30

40

100000

200000

AIRPORT ID: KMLJ
AIRPORT NAME: BALDWIN COUNTY RGNL
CITY/STATE: MILLEDGEVILLE, GA
PROC ID: DP RWY 28
AMDT: 2
SCALE: 1:500,000
TAKE OFF OBS - SEE 8260-15A

CGTA TREE (548)
13-025871

CG TREE (543)
13-026692

VIS TREE (540)
13-025832

CEIL TREE (550)
13-026698

TAKE OFF
OBS

SEE TWR FREQ TAB
