

FIPC BASIC FORM									
PROCEDURE: TAKEOFF MINIMUMS AND OBSTACLE DP AMDT 2			AIRPORT NAME: MORITZ MEML		AIRPORT ID: KK61		SPECIAL CONTROL NO: OP-06-054-25		
FAC ID: KK61		CITY: BELOIT			ST: KS		ORIG CHART DATE: 11/27/2025		
DFL TYPE: PROC/T	THIRD PARTY: ☐ YES	EST. TIME ON SITE: 0.4	REIMB. NUMBER:		PTS TASK ID: F33984792935449996FF1CE2C6599B95				
PREFLIGHT NOTES									
REVIEWER: jeffrey a findley						DATE: 07/01/2025			
COMMENTS:						CHECK ONE:			
						☒ FLT CK REQ ☐ NFCR ☐ REJECT			
								YES	NO
						CPV COMPLETE?		X	
PROCEDURE RESULTS									
INSPECTION DATE: 07/01/2025		CREW #: VN450	N #: N84	INSTRUMENT PROCEDURE STATUS: ☒ SAT ☐ SAT W/CHANGES ☐ UNSAT		ARINC CODING: ☐ SAT ☐ SAT/GOLD ☐ UNSAT			
FLIGHT INSPECTOR SIGNATURE: jeffrey a findley @ 07/01/2025 17:59			PRINTED NAME: FINDLEY, JEFFREY ALLEN				NOTAM INITIATED? ☐ YES ☒ NO		
FLIGHT INSPECTOR REMARKS:									
IN-FLIGHT OBSTACLE REPORT									
OBSTRUCTION ID #:		COORDINATES OR LOCATION:		GNSS ALTITUDE (MSL):		BAROMETRIC ALTITUDE (MSL):		HEIGHT ABOVE GROUND LEVEL:	



TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)



25051

BASSETT, NE

ROCK COUNTY (RBE)

OLD

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

AMDT2 08APR10 (10098) (FAA)

TAKEOFF MINIMUMS:

Rwys 2, 20, NA-Environmental.

TAKEOFF OBSTACLE NOTES:

Rwy 13, fence and trees beginning 12' from DER, 298' left of centerline, up to 60' AGL/2449' MSL.

Fence and trees beginning 16' from DER, 320' right of centerline, up to 60' AGL/2459' MSL.

Rwy 31, rising terrain, trees, and train on railroad tracks beginning 2' from DER, 155' left of centerline, up to 60' AGL/2409' MSL.

Sign, obstruction light on airport beacon and multiple vehicles, towers, trees, fences, and fuel farms beginning 31' from DER, 330' right of centerline, up to 58' AGL/2403' MSL.

Train on railroad tracks, multiple buildings, vehicles and trees beginning 353' from DER, 322' right of centerline, up to 80' AGL/2416' MSL.

BEATRICE, NE

BEATRICE MUNI (BIE)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

AMDT 1 15DEC11 (11349) (FAA)

DEPARTURE PROCEDURE:

Rwy 18, Climb heading 176° to 1900 before turning right.

TAKEOFF OBSTACLE NOTES:

Rwy 14, trees beginning 696' from DER, 438' left of centerline, up to 51' AGL/1360' MSL.

Light pole 1208' from DER, 212' left of centerline, 35' AGL/1344' MSL.

Rwy 32, tree 859' from DER, 320' left of centerline, 27' AGL/1346' MSL.**Rwy 36**, trees beginning 779' from DER, 349' right of centerline, up to 58' AGL/1367' MSL.

Tree 1193' from DER, 50' left of centerline, 48' AGL/1357' MSL.

BELLEVILLE, KS

BELLEVILLE MUNI (RPB)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

ORIG 20OCT11 (11293) (FAA)

TAKEOFF MINIMUMS:

Rwys 14, 32, NA - Environmental.

TAKEOFF OBSTACLE NOTES:

Rwy 18, power pole 16' from DER, 394' left of centerline, 37' AGL/1557' MSL.

Wind sock and buildings 33' from DER, 374' left of centerline, 60' AGL/1570' MSL.

Beacon 136' from DER, 488' left of centerline, 69' AGL/1579' MSL.

Trees and power pole beginning 129' from DER, 397' left of centerline 66' AGL/1576' MSL.

Tree row 371' from DER, 162' left of centerline, 48' AGL/1558' MSL.

Trees 354' from DER, 464' left of centerline, 62' AGL/1572' MSL.

Rwy 36, train 693' from DER, right and left of centerline, 23' AGL/1552' MSL.

Trees beginning 240' from DER, 285' right of centerline, 36' AGL/1546' MSL.

Tree line 710' from DER, right and left of centerline, 45' AGL/1545' MSL.

BELLOIT, KS

MORITZ MEML (K61)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

AMDT 1B 26DEC24 (24361) (FAA)

TAKEOFF MINIMUMS:

Rwys 4, 8, 22, 26, NA-Environmental.

DEPARTURE PROCEDURE:

Rwy 17, climb on heading 174° to 2400 before turning left.**Rwy 35**, climb on heading 354° to 2400 before turning right.

TAKEOFF OBSTACLE NOTES:

Rwy 17, thld light 11' from DER, 17' left of centerline, 1' AGL/1417' MSL.

Trees beginning 173' from DER, 311' left of centerline, up to 50' AGL/1460' MSL.

Building 201' from DER, 380' right of centerline, 13' AGL/1425' MSL.

Building 208' from DER, 443' right of centerline, 19' AGL/1430' MSL.

Pole, building beginning 215' from DER, 379' right of centerline, up to 30' AGL/1440' MSL.

Trees, poles, building, tanks, transmission line, electrical system, vehicle on roads beginning 237' from DER, 15' left of centerline, up to 50' AGL/1461' MSL.

Electrical systems, buildings, pole, tree beginning 243' from DER, 381' right of centerline, up to 32' AGL/1443' MSL.

Electrical system, pole, vehicle on roads beginning 471' from DER, 37' right of centerline, up to 33' AGL/1444' MSL.

Poles, trees beginning 524' from DER, 275' right of centerline, up to 32' AGL/1445' MSL.

Tree, building beginning 565' from DER, 276' right of centerline, up to 29' AGL/1446' MSL.

Trees, pole, buildings beginning 617' from DER, 307' right of centerline, up to 46' AGL/1461' MSL.

Trees, poles beginning 726' from DER, 342' right of centerline, up to 47' AGL/1462' MSL.

Trees, pole beginning 803' from DER, 231' left of centerline, up to 65' AGL/1472' MSL.

Pole 2183' from DER, 549' left of centerline, 65' AGL/1480' MSL.

CON'T

20 FEB 2025 to 20 MAR 2025

20 FEB 2025 to 20 MAR 2025



TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)



25051

NC-2



TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)



25051

BELOIT, KS (CON'T)

MORITZ MEML (K61) (CON'T)

Rwy 35, thld light 9' from DER, 17' left of centerline, 1' AGL/1419' MSL.
 Terrain 63' from DER, 437' left of centerline, 1426' MSL.
 Terrain beginning 68' from DER, 309' left of centerline, up to 1427' MSL.
 Terrain beginning 218' from DER, 365' left of centerline, up to 1428' MSL.
 Terrain beginning 246' from DER, 336' left of centerline, up to 1429' MSL.
 Terrain beginning 355' from DER, 299' left of centerline, up to 1430' MSL.
 Trees, sign beginning 419' from DER, 314' right of centerline, up to 1442' MSL.
 Terrain beginning 537' from DER, 379' left of centerline, up to 1432' MSL.
 Pole, tree beginning 543' from DER, 417' right of centerline, up to 25' AGL/1450' MSL.
 Pole, vehicle on roads, fence beginning 545' from DER, 48' right of centerline, up to 25' AGL/1452' MSL.
 Pole, terrain, vehicle on roads, fence beginning 550' from DER, 23' left of centerline, up to 32' AGL/1465' MSL.
 Tree, poles beginning 723' from DER, 471' left of centerline, up to 36' AGL/1466' MSL.
 Tree 780' from DER, 484' left of centerline, 1472' MSL.
 Trees, vehicle on roads, buildings, fences, poles beginning 800' from DER, 133' left of centerline, up to 43' AGL/1476' MSL.

BENTON, KS

LLOYD STEARMAN FLD (1K1)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

ORIG 29JUL10 (21112) (FAA)

TAKEOFF OBSTACLE NOTES:

Rwy 35, vehicle on road beginning 20' from DER, left and right of centerline, up to 15' AGL/1384' MSL.
 Tree 2689' from DER, 1125' left of centerline, 100' AGL/1489' MSL.

BLAIR, NE

BLAIR EXEC (BTA)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

ORIG 02JUL09 (22251) (FAA)

DEPARTURE PROCEDURE:

Rwy 13, climb on a heading between 124° CCW to 314° from DER or min. climb of 239' per NM to 3000 for all other courses.

TAKEOFF OBSTACLE NOTES:

Rwy 13, rising terrain beginning at DER, 183' right of centerline, up to 1319' MSL.
Rwy 31, trees beginning 434' from DER, 1' right of centerline, up to 35' AGL/1364' MSL.

BROKEN BOW, NE

BROKEN BOW MUNI/KEITH GLAZE FLD (BBW)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

AMDT 4 05DEC19 (19339) (FAA)

TAKEOFF MINIMUMS:

Rwy 14, 400-2¼ or std. w/min. climb of 240' per NM to 3100.
Rwy 32, std. w/min. climb of 310' per NM to 3000 or 1100-3 for VCOA.

VCOA:

Rwy 32, obtain ATC approval for VCOA when requesting IFR clearance. Climb in visual conditions to cross Broken Bow Muni/Keith Glaze Field at or above 3500' before proceeding on course.

TAKEOFF OBSTACLE NOTES:

Rwy 14, vehicle on road 10' from DER, 487' right of centerline, 2532' MSL.
 Buildings beginning 12' from DER, 463' left of centerline, up to 19' AGL/2544' MSL.
 Building 56' from DER, 512' left of centerline, 24' AGL/2549' MSL.
 Building, general utility pole, pole, tree beginning 202' from DER, 170' left of centerline, up to 43' AGL/2572' MSL.
 Tree 1568' from DER, 20' left of centerline, 2575' MSL.
 Tree 1606' from DER, 90' right of centerline, 2573' MSL.
 Tree 1628' from DER, 107' left of centerline, 2576' MSL.
 Tree 1659' from DER, 21' left of centerline, 2579' MSL.
 Building 2574' from DER, 567' right of centerline, 66' AGL/2599' MSL.
 Tree 2831' from DER, 1243' right of centerline, 2605' MSL.
 Tower 2.2 NM from DER, 1858' right of centerline, 305' AGL/2931' MSL.
Rwy 32, electrical systems beginning 39' from DER, 71' left of centerline, up to 3' AGL/2548' MSL.
 Electrical system 39' from DER, 112' right of centerline, 4' AGL/2550' MSL.
 Pole, fences, tree beginning 46' from DER, 325' right of centerline, up to 12' AGL/2559' MSL.
 Vehicle on road 191' from DER, 341' left of centerline, 2556' MSL.
 Trees, vehicle on road beginning 760' from DER, 253' left of centerline, up to 2634' MSL.
 Trees beginning 1256' from DER, 780' right of centerline, up to 2627' MSL.
 Tree 2562' from DER, 1073' right of centerline, 2654' MSL.
 Tree, terrain beginning 2707' from DER, 1216' left of centerline, up to 2642' MSL.
 Terrain 3558' from DER, 1398' left of centerline, 2651' MSL.
 Terrain 3790' from DER, 1358' left of centerline, 2655' MSL.
 Terrain 4015' from DER, 1337' left of centerline, 2661' MSL.
 Tree, terrain beginning 4061' from DER, 1335' left of centerline, up to 2690' MSL.
 Terrain 4440' from DER, 1498' left of centerline, 2693' MSL.
 Terrain, tree beginning 4444' from DER, 1375' left of centerline, up to 2714' MSL.

CON'T

20 FEB 2025 to 20 MAR 2025

20 FEB 2025 to 20 MAR 2025




TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)




25051

NC-2

MORITZ MEML (K61)
BELOIT, KANSAS
TAKEOFF MINS AND ODP (AMDT 2)
RWY 35
SCALE: 1:500,000

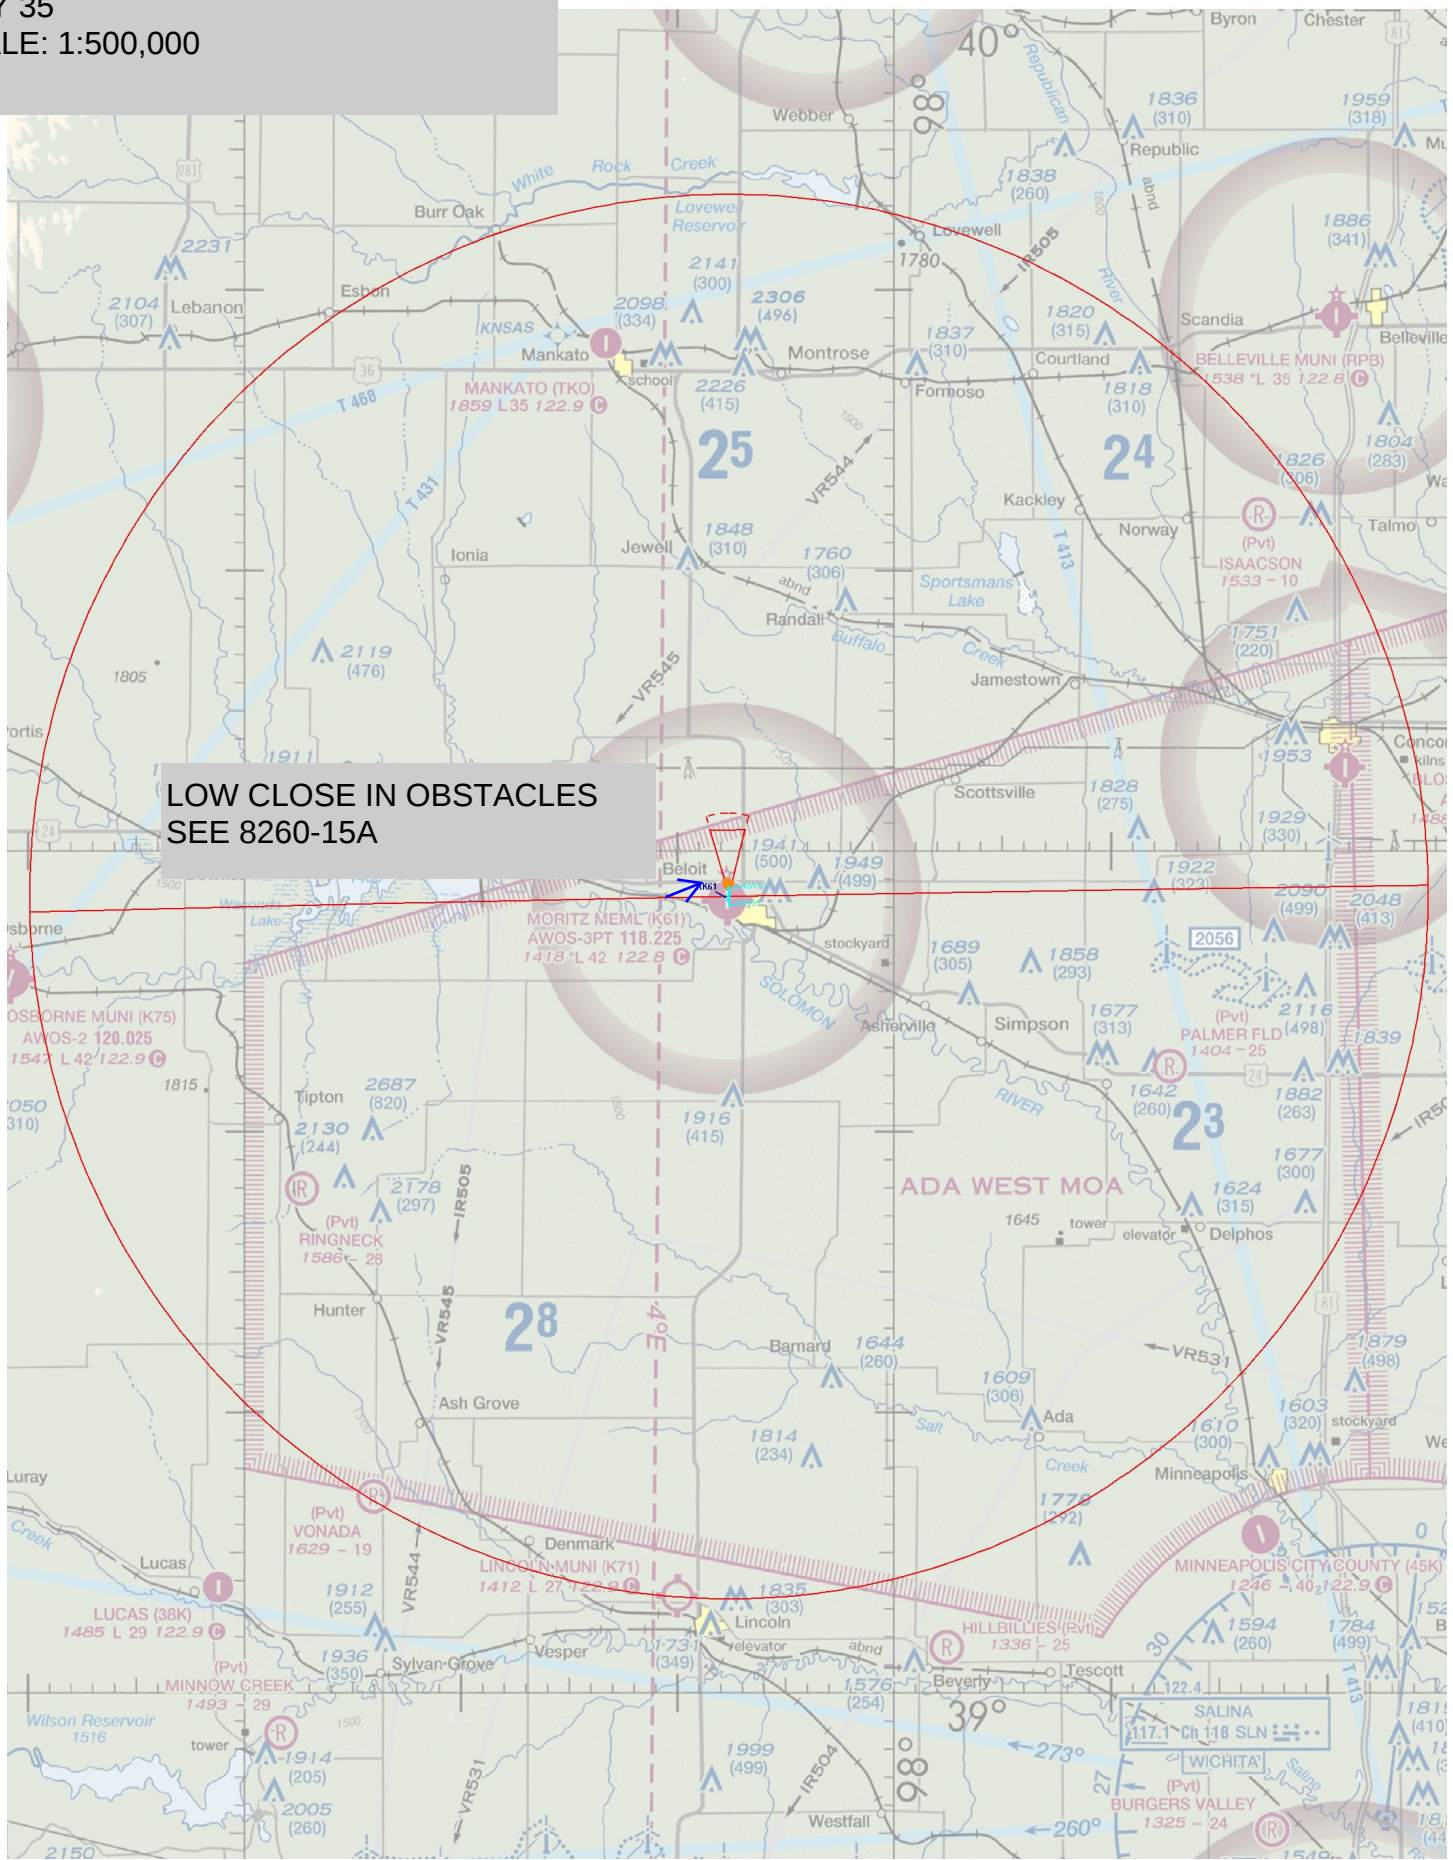

LOW CLOSE IN OBSTACLES
SEE 8260-15A

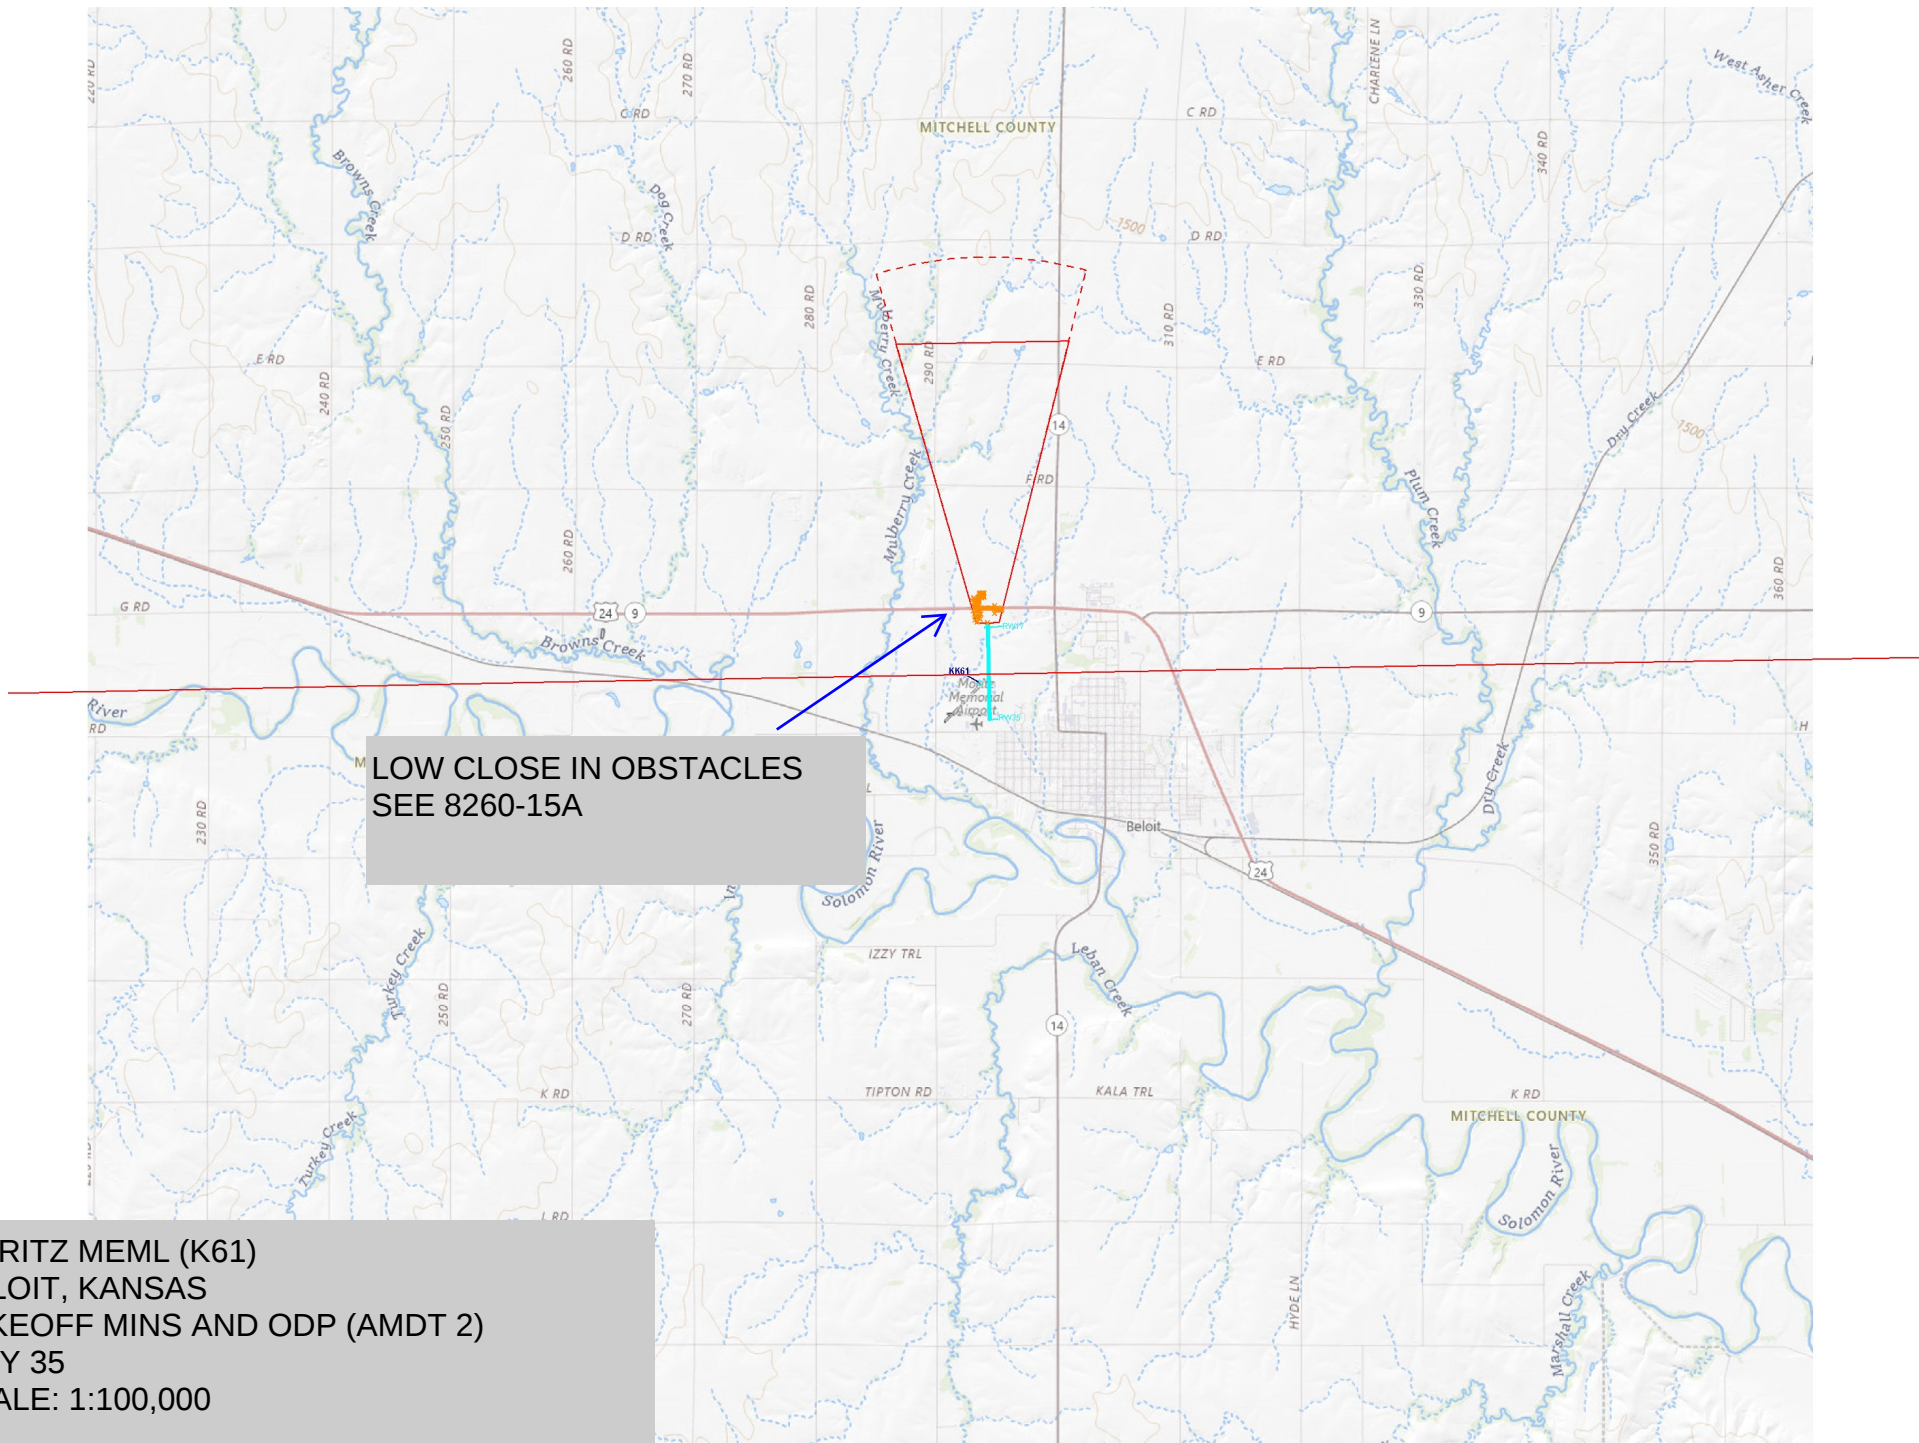

MORITZ MEML (K61)
BELOIT, KANSAS
TAKEOFF MINS AND ODP (AMDT 2)
RWY 17
SCALE: 1:100,000

